

REQUEST FOR TENDER

Shepherdsons Road Rehabilitation 2024-2025

CONTRACT NO: T2425.31

Request for Tender

PART 1 - PREAMBLE

Banana Shire Council invites tenders from suitably qualified tenderers for completion of construction works required for the rehabilitation of Shepherdsons Road, Biloela as described in more detail in Part 5 – Scope. Works are to be completed within 120 Business Days of the awarding of the contract.

| Contract details: | T2425.31 Shepherdsons Roa | d Rehabilitation | 2024-2025 | |
|---------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------|------------|---------------------------------------------------------------------------------------|
| 2. Communications by Tenderers: | Communications regarding the Procurement Process must be submitted to enquiries@banana.qld.gov.au no later than 5 calendar days prior to the time stated in Item 4 | | | |
| Briefing or site inspection: | Details | Maximum attendees | Mandatory | RSVP |
| | Tender Briefing, to be held on 12 th of March 2025. 08:00 am 62 Valentine Plains Road, Biloela QLD 4715 A Teams meeting link will be made avalabile for those who cannot attend in person. | N/A | □ Yes ⊠ No | RSVP to enquiries@banana.qld.go v.au 11 th of March 2025 11:00 am |
| 4. Submission of Tender: | Tenders must be submitted electronically only at vendor panel or tenders@banana.qld.gov.au by no later than 28 th of March 2025 11:00 am Note// Adequate time must be allowed for the Tender and all supporting documents to be uploaded or received by this time. | | | |
| 5. Evaluation Criteria: | Evaluation Criteria | Weighting (%) (Optional) | | |
| | Price | 40 | | |
| | Experience (past performance) | 20 | | |
| | Ability to complete works in spe | 20 | | |
| | Quality, Environmental & Safet | 15 | | |
| | Local Content | 5 | | |
| 6. Tenders should not be longer than: | N/A | | | |
| 7. Tenders to be valid for: | 90 calendar days after the time stated in Item 4 (as extended if at all, pursuant to the Procurement Process Conditions) | | | |
| 8. Complaints: | Complaints regarding Procurement Process to be directed to: enquiries@banana.qld.gov.au | | | |

PART 3 - PROCUREMENT PROCESS CONDITIONS

The Procurement Process is governed by, and this Request for Tender is to be read in conjunction with, the Procurement Process Conditions attached to or provided with this Request for Tender and identified as **T2425.31**Shepherdsons Road Rehabilitation 2024-2025 - Procurement Process Conditions

PART 4 – CONTRACT

The contract shall be substantially in the form attached to or provided with this Request for Tender and identified as T2425.31 Shepherdsons Road Rehabilitation 2024-2025 - Contract - Construct Only

Once the tender is awarded, the final contract documents will be forwarded. A copy of the contract document (AS4000-1997) is also available by request.

PART 5 - SCOPE

The Scope is described in the document(s) attached to or provided with this Request for Tender and identified as

- T2425.31 Shepherdsons Road Rehabilitation 2024-2025 Scope of Works
- T2425.31 Shepherdsons Road Rehabilitation 2024-2025 General Specification
- T2425.31 Shepherdsons Road Rehabilitation 2024-2025 Technical Specification
- T2425.31 Shepherdsons Road Rehabilitation 2024-2025 Locality Plan Appendix A
- T2425.31 Shepherdsons Road Rehabilitation 2024-2025 IFC Drawings Appendix B
- T2425.31 Shepherdsons Road Rehabilitation 2024-2025 Cultural Heritage Report Appendix C
- T2425.31 Shepherdsons Road Rehabilitation 2024-2025 Pricing Schedule Appendix D

PART 6 – RESPONSE SCHEDULES

The Tender must be submitted in the form provided in the response schedules attached to or provided with this Request for Tender and identified as **T2425.31 Shepherdsons Road Rehabilitation 2024-2025 - Response Schedule**.



Shepherdsons Road Rehabilitation 2024-2025

CONTRACT NO: T2425.31

Contents

| | Pa | age No. |
|-----|------------------------------------------------------------------|---------|
| 1. | GENERAL | 2 |
| 2. | BRIEFINGS AND SITE INSPECTIONS (RFT AND RFEOI ONLY) | 3 |
| 3. | COMMUNICATIONS DURING PROCUREMENT PROCESS | 3 |
| 4. | THE RESPONSE (RFT AND RFQ ONLY) | 3 |
| 5. | RESPONDENT'S GENERAL WARRANTIES AND REPRESENTATIONS | 4 |
| 6. | RESPONDENT'S FURTHER WARRANTIES AND REPRESENTATIONS (RFT AND RFQ | |
| 7. | LODGEMENT AND OPENING OF RESPONSES | 6 |
| 8. | ASSESSMENT OF RESPONSES | 7 |
| 9. | SHORTLISTING (RFEOI ONLY) | 8 |
| 10. | ACCEPTANCE (RFT AND RFQ ONLY) | 8 |
| 11. | DOCUMENTS AND INFORMATION | 9 |
| 12. | DEFINITIONS | 11 |
| 13. | GENERAL PROVISIONS | 16 |

1. GENERAL

- 1.1 (Conduct of the Procurement Process) The Principal will endeavour to conduct the Procurement Process in a manner which is consistent with these Procurement Process Conditions.
- 1.2 (**Rights of the Principal**) The Principal may do anything which it considers to be prudent or necessary for the proper conduct of the Procurement Process, including:
 - (a) (alteration of Procurement Documents) amend, add to or delete any part of the Procurement Documents including:
 - (i) the procedures and timeframes provided in the Procurement Process Conditions:
 - (ii) the Evaluation Criteria (including weightings);
 - (iii) the Scope; and
 - (iv) where one is included in the Procurement Documents, the Contract;
 - (b) (suspension or termination) suspend or terminate the Procurement Process;
 - (c) (attendances) request any one or more Respondents to attend a briefing, site inspection or other meeting or to make a presentation of their Response in person at the Principal's office at no cost to the Principal;
 - (d) (change or error in Procurement Documents) request any one or more Respondents to change their Response to take account of a change in the Procurement Documents or any error in such documents;
 - (e) (clarification or alteration) request any one or more Respondents to clarify or alter any aspect of the Respondent's Response;
 - (f) (additional information) request additional information from one or more Respondents relating to a Response, the Procurement Process, the Respondent's compliance with the Procurement Process Conditions or any other matter which the Principal considers relevant to its assessment (including information that should have been, but was not, included in the Respondent's Response);
 - (g) (negotiation) negotiate amendments to any aspect of a Response with any one or more Respondents and suspend or terminate such negotiations at any time;
 - (h) (revised Responses) invite one or more Respondents to provide a revised Response or best and final offer; and/or
 - (i) (**shortlisting**) create a shortlist of one or more Respondents and exercise any of its rights only in respect of one or more of the shortlisted Respondents.
- 1.3 (Conduct of Respondents) The Respondent must not, and must ensure that its Personnel do not, engage in any Improper Conduct. The Respondent must immediately notify the Principal in the event that it becomes aware that it, or any of its Personnel, have engaged in Improper Conduct. Where appropriate, the Principal may report Improper Conduct by the Respondent to the appropriate Authority and provide that Authority with any relevant information related to that conduct.
- 1.4 (Complaints in relation to the Procurement Process) The Respondent must make any complaint in relation to the Procurement Process using the Communication Method immediately upon the cause of the complaint arising or upon the Respondent becoming aware of the cause. The complaint must be made in writing to the Complaints Manager and must contain adequate detail to allow the Complaints Manager to properly investigate the complaint.

- 1.5 (**No warranty**) The Principal gives no warranty and makes no representation that the Procurement Documents or any other information provided to the Respondent in connection with the Procurement Process is accurate, adequate or complete.
- 1.6 (**No liability**) Neither the Principal nor its Personnel shall be liable upon any Claim for any Specified Loss in connection with the Procurement Process.

2. BRIEFINGS AND SITE INSPECTIONS (RFT AND RFEOI ONLY)

- 2.1 (Attendance) The Respondent must attend any briefing or a site inspection which is identified in the General Information as mandatory. Respondents are encouraged to attend any briefing or site inspection which is not described as mandatory.
- 2.2 (RSVP) The Respondent must confirm that it intends to attend the briefing or site inspection to the email address and by the time and date stated in the General Information and may only bring a maximum of the number of Personnel stated in the General Information.
- 2.3 (**Safety**) The Respondent must inform itself of risks to health and safety arising from attendance at the briefing or site inspection and take all reasonable steps to ensure that such risks are eliminated or, if it is not possible to eliminate them, to minimise them so far as is practicable.
- 2.4 **(Obligation to inspect)** Where no site inspection is identified in the General Information, the Respondent must make its own arrangements to inspect the site prior to lodging its Response.

3. COMMUNICATIONS DURING PROCUREMENT PROCESS

- 3.1 (Communication Method) All communications by the Principal to the Respondent shall at first instance be made using the Communication Method. Except where expressly permitted by these Procurement Process Conditions, all communications by the Respondent to the Principal in connection with the Procurement Process shall at first instance be directed to the Principal using the Communication Method. No other communication method may be utilised by the Respondent unless expressly permitted by the Principal or where technical difficulties prevent the Respondent from utilising the Communication Method or the Principal expressly agrees to an alternative method.
- 3.2 (Respondent's responsibility) The Respondent must ensure that it is capable of receiving and does receive all communications to the Respondent in connection with the Procurement Process. Where the Communication Method is email, it is the Respondent's responsibility to ensure that it notifies the Principal of the correct email address for receiving communications. Where the Communication Method is through a website, the Respondent must ensure that it is properly registered with and capable of receiving communications through the website.
- 3.3 (**Confidentiality of communications**) The Principal may notify any or all Respondents of a request for further information made by a Respondent and the Principal's response to it without identifying the submitting Respondent or may keep a request for information confidential and respond only to the Respondent if it considers that it is appropriate to do so.
- 3.4 (**No reliance**) The Respondent must not rely upon any information (including information provided at a briefing or site inspection) unless it is confirmed by the Principal through the Communication Method.
- 3.5 (**Communication Closing Time**) The Principal will not respond to any request for information received after the Communication Closing Time.

4. THE RESPONSE (RFT AND RFQ ONLY)

- 4.1 (**Application of clause**) This clause 4 only applies in respect of an RFT or an RFQ.
- 4.2 (Acceptance of Contract and Scope) If one has not been provided, the Respondent must obtain a copy of the Contract from the Principal by requesting a copy through the Communication Method. Except to the extent that the Respondent has detailed a proposed

alternative, amendment, qualification or departure in a Response, the Respondent will be taken to have unconditionally accepted and agreed to:

- (a) be bound by the terms and conditions of the Contract; and
- (b) carry out and complete the whole of the obligations described in or to be reasonably inferred from the Procurement Documents.
- 4.3 (**Price**) The Price must be submitted exclusive of GST and in Australian dollars.
- 4.4 (**Discrepancy in Price**) Where the Response Form requires the Respondent to provide a Price and there is a discrepancy between the amount stated in the Response Form as the Respondent's Price and the sum total of the items in any Price Schedule then:
 - (a) if the Contract provides that it is a lump sum contract, then the sum total of the items in the Price Schedule shall be the Respondent's Price; or
 - (b) if the Contract provides that it is a schedule of rates contract or a part lump sum and part schedule of rates contract, then the rate, price or lump sum of each item will prevail over the total shown, and the total shall be adjusted accordingly.
- 4.5 (Response Validity Period) The Respondent's Response will remain valid and open for acceptance by the Principal until the end of the Response Validity Period and thereafter until it is withdrawn in writing by the Respondent or the Procurement Process is finalised. The Principal may consent to the Respondent withdrawing its Response before the end of the Response Validity Period. The Principal may request an extension of the Response Validity Period at any time by giving written notice to the Respondent. If the Respondent does not agree to the requested extension then the Principal may exclude the Respondent's Response from assessment or further assessment as the case may be.
- 4.6 (Alternative Responses) If the Respondent wishes to submit an Alternative Response, then the Respondent is encouraged to:
 - (a) also submit a Conforming Response; and
 - (b) submit the Alternative Response on a separate Response Form to the Conforming Response, clearly marked, "ALTERNATIVE RESPONSE" accompanied by a clear summary of all points of difference between the Alternative Response and the Conforming Response.

5. RESPONDENT'S GENERAL WARRANTIES AND REPRESENTATIONS

- 5.1 (Warranties and Representations) By lodging a Response, the Respondent warrants and represents that:
 - (a) (**conduct of Respondent**) neither the Respondent nor any of its employees or agents has engaged in any Improper Conduct;
 - (b) (authority) the Response has been signed and lodged by a person with authority to do so on behalf of the Respondent;
 - (c) (basis of Response) the Respondent:
 - (i) has received or obtained copies of all of the Procurement Documents and all information or documents referred to in the Procurement Documents; and
 - (ii) has not relied on the accuracy, adequacy or completeness of any documents or information provided or any representation made by or on behalf of the Principal in connection with the Procurement Process in preparing its Response;

- (d) (accuracy of Response) all information provided in or with the Response is accurate;
- (e) (ability) the Respondent and its relevant Personnel:
 - (i) hold (and are compliant with all requirements of) all necessary competencies, licences (including if necessary, a licence under the *Queensland Building and Construction Commission Act 1991* (Qld)), accreditations, certifications, permits, clearances and other authorisations which will be required for the Respondent to carry out the Scope if it is ultimately engaged to carry out that Scope; and
 - (ii) are not excluded from submitting a tender under any applicable Queensland or Federal Government scheme, code or policy;
- (f) (suitability etc. of works, goods or services) where the Principal has stated in the Procurement Documents the purpose(s) for which the works, goods or services must be suitable, appropriate, adequate or fit, the works, goods or services shall be suitable, appropriate, adequate and fit for those purposes (but this warranty and representation will not apply to the extent (if any) that the Respondent has expressly excluded or limited it in the Respondent's Response);
- (g) (Effect of implied warranties) neither clause 5 nor clause 6 shall operate in any way to limit, exclude or otherwise restrict the operation of any warranty implied by law.

6. RESPONDENT'S FURTHER WARRANTIES AND REPRESENTATIONS (RFT AND RFQ ONLY)

- 6.1 (Application of clause) This clause 6 only applies in respect of an RFT or an RFQ.
- 6.2 (Warranties and Representations) By lodging a Response, the Respondent warrants and represents that:
 - (a) (investigations) the Respondent has undertaken its own enquiries and investigations to satisfy itself of:
 - (i) the nature and extent of the Scope, its contractual obligations and all other risks, contingencies and other circumstances which could have an impact on its ability to carry out and complete the obligations it will have under the Contract if its Response is accepted for the Price; and
 - (ii) the suitability, appropriateness and adequacy of the Scope (including, in respect of contracts under which the successful Respondent is required to design works, any preliminary design included in the Scope) for the purposes stated in or to be reasonably inferred from the Scope;
 - (b) (ability) the Respondent and its relevant Personnel:
 - (i) have and will maintain the necessary experience, expertise and skill to perform its obligations under the Contract in accordance with the requirements of the Contract in the event that its Response is accepted; and
 - (ii) have and will maintain the resources necessary to comply with the timeframes for the performance of the Contract stated in the Procurement Documents (as amended if at all, pursuant to these Procurement Process Conditions);
 - (c) (price) the Price, and all rates, sums and prices included in the Response allow for:
 - (i) all of the risks, contingencies and other circumstances which could have an effect on the Respondent's ability to carry out and complete the obligations it will have under the Contract if its Response is accepted for the Price, except to the extent that the Contract expressly allows an adjustment;

- (ii) the provision of all materials, plant, labour and other services necessary for the proper completion of the obligations it will have under the Contract if its Response is accepted, whether or not those items are expressly mentioned in the Contract; and
- (iii) unless the Contract expressly allows an adjustment, rise and fall in costs;
- (d) (competitive neutrality) if the Respondent is required by law to comply with principles of competitive neutrality, the Respondent has properly considered, assessed and complied with the applicable competitive neutrality principles in relation to the Procurement Process and the acceptance by the Principal of the Respondent's Response will not breach those principles;
- (e) (notice) the Respondent has notified the Principal in its Response of any:
 - (i) ambiguity, inconsistency, uncertainty, error or omission which it has discovered in or from the Procurement Documents;
 - (ii) any assumptions that it has made in determining its Price;
 - (iii) further information or investigations which it considers that it requires to enable it to give the warranties and make the representations in this clause 6.

and otherwise gives all warranties and makes all representations which the Contract requires to be given or made by the successful Respondent. The Respondent acknowledges that the Principal will rely on these warranties and representations in entering into a contract with the successful Respondent.

7. LODGEMENT AND OPENING OF RESPONSES

- 7.1 (Method of lodgement) A Response must be lodged:
 - (a) if the Tender Box is a website, by uploading it to the Tender Box;
 - (b) if the Tender Box is an email address, by sending it as an attachment to an email to the Tender Box; or
 - (c) if the Tender Box is a physical address, by delivering it to the Tender Box.

The Principal may direct or allow the Response to be lodged by an alternative method.

- 7.2 (**Time of lodgement**) A document forming part of a Response shall be deemed to have been lodged:
 - (a) where the Tender Box is a website, at the time that the document is successfully uploaded to the Tender Box, as indicated on the electronic receipt issued to the Respondent;
 - (b) where the Tender Box is an email address, at the time that an email attaching the document is successfully delivered to the Tender Box, as indicated on the email system on which the Tender Box is hosted:
 - (c) where the Tender Box is a physical address, at the time that the document is physically received at the Tender Box; or
 - (d) where the Response is lodged by an alternative method allowed by the Principal, when it is received by the Principal by that method.
- 7.3 (**Response opening**) Responses will not be opened publicly and the Respondent will not be permitted to attend the opening of Responses.

8. ASSESSMENT OF RESPONSES

- 8.1 (Evaluation Criteria) In determining which Response(s) are most advantageous to the Principal, each Response evaluated in accordance with these Procurement Process Conditions will be assessed, but not necessarily exclusively, against the Evaluation Criteria (if any).
- 8.2 (**Considerations**) In assessing Responses, the Principal may consider any information which the Principal reasonably considers to be relevant to its assessment (however obtained), including:
 - (a) information contained in the Response or any amendment to or clarification of a Response;
 - (b) information provided at a meeting with or presentation by the Respondent;
 - (c) outcomes from discussions with a Respondent's referees (if any);
 - (d) information obtained pursuant to clause 8.5;
 - (e) the Respondent's past performance under other contracts with the Principal or third parties; and
 - (f) the reasonably held subjective opinions of the persons appointed by the Principal to evaluate Responses or any advisor to such persons.
- 8.3 (**Uncertainties**) The Principal may ignore any part of a Response which is ambiguous, uncertain, unclear or illegible without seeking clarification from the Respondent and may assess the balance of the Response.
- 8.4 (**Right to exclude**) The Principal may, but shall not be obliged to, reject or exclude from assessment any Response including:
 - (a) a Non-Conforming Response, an Alternative Response or a Late Response;
 - (b) a Response, in respect of which the Principal reasonably believes that the Respondent has:
 - failed to comply with these Procurement Process Conditions or any request made by or on behalf of the Principal pursuant to them within the time required; or
 - (ii) breached a warranty given or representation made pursuant to these Procurement Process Conditions or that a warranty, declaration or representation in the Respondent's Response is false or misleading in any material respect;
 - (c) a Response in respect of which the Principal reasonably believes that the Respondent cannot reasonably comply with the obligations which it will have under the Contract (in the event that its Response is successful) for the Price; or
 - (d) a Response which fails to achieve a satisfactory score against any of the Evaluation Criteria, even if the overall score of the Response is satisfactory;
- 8.5 (Other information or assistance) The Principal may undertake its own investigations, or engage third parties to do so on its behalf, in relation to any aspect of a Response (including verifying any warranty, representation or declaration made or given in the Response or pursuant to these Procurement Process Conditions) or any other matter which it considers relevant to the conduct of the Procurement Process. The Respondent must cooperate with such investigations and provide all information and assistance reasonably requested by or on behalf of the Principal in connection with the investigation.

9. SHORTLISTING (RFEOI ONLY)

- 9.1 (Application of clause) This clause 9 only applies in respect of an RFEOI.
- 9.2 **(Shortlisting)** The Principal intends, but is not bound, to create a shortlist of Respondents and invite tenders from the shortlisted Respondents.
- 9.3 (**No obligation**) The Principal is not bound to shortlist or invite a tender from any Respondent, including the Respondents with the highest scores against the Evaluation Criteria. The Principal may shortlist and invite tenders from as many or as few Respondents as the Principal sees fit and may choose not to shortlist any Responses or invite any tenders.
- 9.4 (**Local preference**) The Principal may shortlist an EOI that is from a Local Supplier in preference to comparable EOIs from Non-Local Suppliers even if the EOIs from the Non-Local Suppliers have been assessed as more favourable in terms of one or more Evaluation Criteria.
- 9.5 (**RFT**) A Respondent shall not be entitled to submit a tender unless and until the Principal expressly invites the Respondent to submit a tender in writing.
- 9.6 (Unsuccessful Respondents) Unsuccessful Respondents will be notified after the Procurement Process is concluded. The Principal may provide feedback to unsuccessful Respondents if requested to do so, but such feedback may be general in nature, will be limited to the Respondent's EOI only and may be postponed until after any related Request for Tender process is finalised.

10. ACCEPTANCE (RFT AND RFQ ONLY)

- 10.1 (Application of clause) This clause 10 only applies in respect of an RFT or an RFQ.
- 10.2 (Ability to accept) The Principal is not bound to accept the Response with the lowest Price or the Response with the highest score against the Evaluation Criteria, or any Response. The Principal will, if it accepts a Response, accept the Response(s) which it reasonably believes are the most advantageous to it having regard to the Sound Contracting Principles and the requirements of the Local Government Regulation 2012 (Qld) to the extent that they are applicable and relevant to the Procurement Process.
- 10.3 (Local preference) The Principal may accept a Response lodged by a Local Supplier in preference to comparable Responses from Non-Local Suppliers even if the Responses from the Non-Local Suppliers have been assessed as more favourable in terms of one or more Evaluation Criteria, so long as the overall differences are not substantial, and so long as it is clear that the Local Supplier can meet the Principal's requirements at an acceptable standard which is generally comparable to that of the Non-Local Suppliers.
- 10.4 (Acceptance of more than one Response and acceptance of part of a Response) The Principal may accept a Response in whole or in part. Without limiting this, where the Scope comprises distinct portions of works, goods or services, the Principal may accept a Response from one or more Respondents in relation to different portions of the works, goods or services as if those portions had been the subject of separate Procurement Processes.
- 10.5 (No contract or appointment until formal acceptance) Unless and until the Principal expressly notifies the Respondent in writing that the Respondent's Response (as amended by any post-Response negotiation, if any) has been successful or the parties execute a contract:
 - (a) no binding contract for the provision of any work, services and/or goods by the Respondent will exist between the parties; and
 - (b) in respect of an RFT for appointment as a Pre-qualified Supplier or Preferred Supplier, the Respondent will not be considered to be appointed as a Pre-qualified Supplier or Preferred Supplier.

For clarity, a statement published by the Principal but not specifically notified to the Respondent (including a record of a council resolution) to the effect that a Response has been accepted or a contract has been awarded does not, of itself, constitute an acceptance of the Response or notice that the Response has been successful or constitute a rejection of any other Response.

- 10.6 (Form of Contract) Unless the RFT or RFQ stated that the Respondent would not be required to enter into a contract until it is separately engaged by the Principal to provide works, goods or services, if a Response is accepted, the successful Respondent will be required to enter into a contract in the form of the Contract, as amended by agreement between the parties.
- 10.7 (Unsuccessful Respondents) Unsuccessful Respondents will be notified after a Response has been accepted. The Principal may, at its discretion, notify unsuccessful Respondents of the name of, and Price submitted by, the successful Respondent. The Principal may provide feedback to unsuccessful Respondents if requested to do so, but such feedback may be general in nature and will be limited to the Respondent's Response only.
- 10.8 (Arrangement with other local governments) The Respondent acknowledges that if, pursuant to the Procurement Process, the Respondent is selected to be a Preferred Supplier or Pre-qualified Supplier for goods and/or services then any Related Local Government may make a contract with the Respondent for the supply of those goods and/or services, as if that Related Local Government had itself selected the Respondent to be a Preferred Supplier or Pre-qualified Supplier of those goods and/or services.

11. DOCUMENTS AND INFORMATION

- 11.1 (**Ownership**) The Procurement Documents remain the property of the Principal. The Response will become the property of the Principal upon lodgement.
- 11.2 (Intellectual Property Rights) Intellectual Property Rights in documents and information provided on behalf of a party in connection with the Procurement Process remain, as between the parties, with the party on whose behalf they were provided. The Principal and the Respondent grant each other a perpetual, non-exclusive, royalty free licence to do the things contemplated by clause 11.9. The licence so granted by the Respondent is irrevocable. The licence granted by the Principal may be revoked at any time on the giving of written notice.
- 11.3 (Warranty and representation) The Respondent warrants and represents that:
 - (a) it owns or has a right to use the Intellectual Property Rights in its Response for the purpose of lodging a Response and undertaking the obligations which it will have under a contract with the Principal in the event that the Respondent's Response is accepted; and
 - (b) it has the right and authority to grant the licence in clause 11.2 and the Principal's exercise of the rights so granted will not infringe the Intellectual Property Rights of a third party.
- 11.4 (Confidentiality) Except to the extent otherwise provided in these Procurement Process Conditions, each party shall keep Confidential Information of the other party confidential. The Respondent must inform each of its Personnel and any other person to whom Confidential Information of the Principal is disclosed of the Respondent's obligations under this clause 11.4. Subject to clause 11.9(b), the Respondent must return any and all Confidential Information when requested to do so by the Principal.
- 11.5 (Information Privacy Act) If the Respondent collects or has access to 'Personal Information' as that term is defined in the *Information Privacy Act 2009* (Qld) in connection with the Procurement Process, the Respondent must comply with Parts 1 and 3 of Chapter 2 of that Act as if the Respondent was the Principal. The Principal collects and uses personal information and non-personal information in the Response so that it can properly conduct the Procurement Process and otherwise carry out its functions as a Local Government. The Principal is authorised to collect this information under the *Local Government Act 2009* (Qld) and the *Local Government Regulation 2012* (Qld) and other law. The information in the Respondent's Response will be accessible by employees of the Principal and third party personnel engaged

to assist the Principal in conducting the Procurement Process or otherwise carrying out the functions of the Principal. Information in the Response may also be disclosed as required by the *Local Government Regulation 2012* (Qld) and the *Right to Information Act 2009* (Qld) as described below.

- 11.6 (Local Government Regulation) The Local Government Regulation 2012 (Qld) provides that the Principal must, as soon as possible after entering into a contractual arrangement worth \$200,000 or more (exclusive of GST) publish relevant details of the contract (including the person with whom the Principal has entered into the contractual arrangement, the value of the contractual arrangement and the purpose of the contractual arrangement) on the Principal's website and display those details in a conspicuous place in the Principal's public office. The relevant details must be published or displayed in this manner for a period of at least 12 months.
- 11.7 The Local Government Regulation 2012 (Qld) may also require the Principal to make documentation and information contained in, or provided by the Respondent in connection with, a Response (including documentation and information identified by the Respondent as confidential) publicly available where that documentation or information is:
 - (a) discussed in a Local Government Meeting;
 - (b) included in a report or other document that:
 - (i) relates to an item on the agenda for a Local Government Meeting and is made available to Councillors or committee members for the purposes of the meeting;
 - (ii) is directly relevant to a matter considered or voted on at a Local Government Meeting; or
 - (iii) is presented at a Local Government Meeting for the consideration or information of the Local Government or committee; or
 - (c) otherwise required to be disclosed pursuant to a provision of the Local Government Act 2009 (Qld) or the Local Government Regulation 2012 (Qld).
- 11.8 (Right to Information) The Right to Information Act 2009 (Qld) provides members of the public with a legally enforceable right to access documents held by Queensland Government agencies (including the Principal). The Act requires that documents be disclosed upon request, unless the documents are exempt or on balance, disclosure is contrary to public interest. Information or documentation contained in or provided by the Respondent in connection with a Response is potentially subject to disclosure to third parties, including documentation and information identified by the Respondent as confidential. Any application for disclosure will be assessed in accordance with the terms of the Act. Notwithstanding any other provision of the Procurement Documents or a Response, if a Response is accepted, the Principal may publish on a Queensland Government website or by any other means, contract information including:
 - (a) the name and address of the Principal and the successful Respondent;
 - (b) a description of the goods and/or services to be provided or works to be carried out pursuant to the contract;
 - (c) the date of award of the contract (including the relevant stages if the contract involves more than one stage);
 - (d) the contract value (including the value for each stage if the contract involves more than one stage and advice as to whether any non-price criteria were used in the evaluation of Responses);
 - (e) the procurement method used; and
 - (f) for contracts with a value over \$10 million, the contract, or summary information in respect of the contract, between the Principal and the Respondent.
- 11.9 (**Use of documents and information**) Documents and information provided on behalf of a party to the other party in connection with the Procurement Process (including documentation and

information identified by the Respondent as confidential) may be used, copied, modified or disclosed as required by any law and otherwise:

- (a) by the Principal, as the Principal considers to be reasonably necessary to:
 - (i) properly conduct the Procurement Process;
 - (ii) exercise the rights granted to it in these Procurement Process Conditions;
 - (iii) obtain legal, accounting or other professional advice in connection with the Response;
 - (iv) report any actual or suspected Improper Conduct to the appropriate Authority; and/or;
 - (v) to otherwise properly carry out its functions as a Local Government;
- (b) by the Respondent, as is reasonably necessary to enable the Respondent to:
 - (i) prepare the Response;
 - (ii) obtain legal, accounting or other professional advice in connection with the Response; or
 - (iii) comply with the Respondent's corporate governance requirements.

If the Respondent is required by law to disclose Confidential Information of the Principal, the Respondent must notify the Principal of this prior to making such disclosure and must only disclose the minimum amount of information required to meet is obligation to disclose.

11.10 (Media) The Respondent must not, either on its own account or in conjunction with other parties, issue any publication, advertisement, document, article or information whether verbal or written, in connection with the Procurement Process in any media without the prior approval of the Principal.

12. **DEFINITIONS**

- 12.1 (**Definitions**) In these Procurement Process Conditions, unless the context otherwise requires:
 - (a) Addenda and Addendum means any communication issued to Respondents in accordance with these Procurement Process Conditions which is identified as an Addendum;
 - (b) **Alternative Response** means a Response which is otherwise a Conforming Response but which in the opinion of the Principal, contains significant alternatives, qualifications or amendments to or departures from the Contract or the Scope;
 - (c) Authority means a local government, the State of Queensland, the Commonwealth or other any Federal, State, or local government authority, administrative or judicial body or tribunal, department, commission, agency, government owned corporation, statutory body or instrumentality having jurisdiction over the project;
 - (d) **Business Day** means a day that is not a Saturday, Sunday or public holiday at Biloela;
 - (e) Claim includes any claim, action, demand, proceeding, suit, defence or set-off, however arising including at law (including a breach of an express or implied term of contract), under statute, in equity, in tort (including for negligence), in quasi-contract, for unjust enrichment and to the extent permitted by law, pursuant to any other principle of law, in connection with the Procurement Process:

- (f) **Communication Closing Time** means the time identified in the General Information as the time by which communications by Respondents must be submitted;
- (g) **Communication Method** means submitting an enquiry through the website forum or sending an email to the email address nominated for communications by Respondents in the General Information:
- (h) **Complaints Manager** means the person identified in the General Information as the person to whom complaints regarding the Procurement Process should be directed;
- (i) **Confidential Information** means documents and information provided or made available by or on behalf of one party to the other party in connection with the Procurement Process which are of their nature confidential (including copies of such documents and information) but not including documents and information which are in the public domain other than through a breach of clause 11.4;
- (j) **Conforming Response** means a Response which, in the opinion of the Principal:
 - is substantially in the form and contains substantially all of the documentation, information, acknowledgements, warranties, declarations and undertakings required by the Response Schedules;
 - (ii) contains no significant alternatives, qualifications or amendments to or departures from the Contract or the Scope; and
 - (iii) in respect of Tenders or EOIs only, does not substantially exceed the Maximum Page Limit (if any);

(k) Contract means:

- (i) a contract which may be entered into between the Principal and a Respondent pursuant to an RFT or RFQ and which will be in the form referenced in Part 4 – Contract of the RFT or RFQ, as amended (if at all) by the express written agreement of the Principal; and
- (ii) where an RFT is for appointment as a Preferred Supplier or Pre-qualified Supplier, also includes a contract which may be entered into during the term of the appointment unless the context requires otherwise:
- (I) Councillor has the same meaning as in the Local Government Act 2009 (Qld);
- (m) EOI (Expression of Interest) means a Response lodged by a Respondent in response to an RFEOI and includes all documents and information lodged with or as part of the expression of interest;

(n) Evaluation Criteria means:

- (i) for an RFT or an RFEOI, the evaluation criteria (if any) set out in the General Information; and
- (ii) for an RFQ, the evaluation criteria (if any) set out in the RFQ;
- (o) **General Information** means Part 2 General Information of the RFQ, RFT or RFEOI (as the case may be);
- (p) **GST** has the same meaning as in the *A New Tax System (Goods and Services Tax) Act 1999* (Cth);
- (q) Improper Conduct means:

- engaging in any activity or obtaining any interest which results in or is likely to result in any actual, potential or perceived conflict between the interests of the Respondent and the Respondent's obligations to the Principal in connection with the Procurement Process;
- (ii) engaging in misleading or deceptive conduct in connection with the Procurement Process;
- (iii) engaging in any collusive tendering, anticompetitive conduct, or any other unlawful or unethical conduct with any other Respondent, or any other person in connection with the Procurement Process;
- (iv) canvassing, attempting to improperly influence, offering any inducement to or accepting or inviting improper assistance from any Councillor or other Personnel (or former Personnel) of the Principal in connection with the Procurement Process;
- using any information improperly obtained, or obtained in breach of any obligation of confidentiality in preparing the Respondent's Response;
- (vi) breaching any law in connection with the Procurement Process;
- (vii) engaging in aggressive, threatening, abusive, offensive or other inappropriate behaviour or committing a criminal offence; or
- (viii) engaging in conduct contrary to sections 199 and 200 of the *Local Government Act* 2009 (Qld);
- (r) Intellectual Property Rights means copyright, patents and all rights in relation to inventions, registered and unregistered trademarks (including service marks), registered designs, circuit layouts and all other rights resulting from intellectual activity in the industrial, scientific, literary or artistic fields;
- (s) Late Response means any Response that is not received in the Tender Box (or otherwise received by the Principal by an alternative method permitted under the Procurement Process Conditions) by the Response Closing Time;
- (t) **Local Government** has the same meaning as in the *Local Government Act 2009* (Qld);
- (u) **Local Government Meeting** has the has the same meaning as in the *Local Government Act 2009* (Qld);

(v) Local Supplier:

- (i) where the Principal's procurement policy provides a meaning of local supplier, has the meaning given in the Principal's procurement policy, a copy of which can be obtained from the Principal upon request; or
- (ii) where the Principal does not have a procurement policy, or the procurement policy does not provide a meaning of local supplier, means a supplier that:
 - (A) is beneficially owned and operated by persons who are residents or ratepayers of the local government area of the Principal as determined under the *Local Government Regulation 2012* (Qld); or
 - (B) has its principal place of business within that local government area; or
 - (C) otherwise has a place of business within that local government area that solely or primarily employs persons who are residents or ratepayers of that local government area;

- (w) Maximum Page Limit means the number of pages which may be lodged as, with or in relation to the Response (including, unless otherwise indicated, all attachments, annexures, supplements, parts, schedules or appendices), which the General Information states a Response should not be longer than;
- (x) **Non-Conforming Response** means a Response which is not a Conforming Response or an Alternative Response;
- (y) **Non-Local Supplier** means a supplier (including a Respondent) that is not a Local Supplier;
- (z) **Personnel** includes the officers, employees, agents, representatives, contractors and consultants of a party and any other person or entity for whom that party is vicariously liable;
- (aa) **Preamble** means Part 1 Preamble of the RFEOI, RFT or RFQ (as the case may be);
- (bb) **Preferred Supplier** means a supplier that has been selected as a preferred supplier pursuant to section 233 of the *Local Government Regulation 2012* (Qld);
- (cc) **Pre-qualified Supplier** means a supplier that has been selected as a pre-qualified supplier pursuant to section 232 of the *Local Government Regulation 2012* (Qld);
- (dd) **Price** means:
 - (i) where the Procurement Process is for appointment as a Preferred Supplier or Pre-qualified Supplier, the rates, sums or prices stated in the Response;
 - (ii) otherwise, subject to clause 4.4, the total price stated in the Response;
- (ee) **Price Schedule** means a Response Schedule which provides a breakdown of the Price, and which may include rates, lump sums, prices, provisional sums, estimated quantities and other information;
- (ff) Principal or Purchaser means Banana Shire Council;
- (gg) Procurement Documents means:
 - (i) the RFEOI, RFT or RFQ (as the case may be); and
 - (ii) any Addenda issued pursuant to these Procurement Process Conditions,

and includes all documents included in or incorporated by reference into these documents;

- (hh) **Procurement Process** means the process by which the Principal intends to, or does, invite, assess and where applicable, accept or reject Responses in respect of the Scope;
- (ii) **Procurement Process Conditions** means these procurement process conditions;
- (jj) **Quotation** means a Response lodged by a Respondent in response to an RFQ and includes all documents and information lodged with or as part of the quotation;
- (kk) Related Local Government means a local government that has entered into an arrangement with the Principal, as contemplated in section 235(f) of the Local Government Regulation 2012 (Qld), to the effect that the local government may make a contract with a supplier that has been selected by the Principal to be a Preferred Supplier or Pre-qualified Supplier of goods and/or services, as if that local government had itself selected that supplier to be a Preferred Supplier or Pre-qualified Supplier of those goods and/or services.

- (II) Respondent means:
 - (i) any person who lodges a Response; and
 - (ii) to the extent to which the term can apply to any other person who obtains a copy of any of the Procurement Documents during the Procurement Process, also includes such other persons,

and includes a Tenderer;

- (mm) **Response** means, where these Procurement Process Conditions are incorporated into an:
 - (i) RFEOI, an EOI;
 - (ii) RFT, a Tender; or
 - (iii) RFQ, a Quotation;
- (nn) **Response Closing Time** means the time identified in the General Information as the time by which Responses must be submitted as varied (if at all) pursuant to these Procurement Process Conditions:
- (oo) **Response Form** means in respect of an:
 - (i) RFEOI, the document identified as the EOI form in the Response Schedules;
 - (ii) RFT or RFQ:
 - (A) the document identified as the tender form or the quotation form (as the case may be) in the Response Schedules; or
 - (B) otherwise where there is no document identified as the tender form or quotation form, any document (other than a Price Schedule) which states the total price offered by the Respondent in the Response:
- (pp) **Response Schedules** means the schedules identified in Part 5 Response Schedules of the RFEOI or Part 6 Response Schedules of the RFT or RFQ (as the case may be);
- (qq) **Response Validity Period** means the period stated in the General Information as the time for which Responses are to be valid as extended (if at all) pursuant to clause 4.5;
- (rr) RFEOI (or Request for Expressions of Interest) means the request for expressions of interest issued by the Principal and all documents included in or incorporated by reference into it (including these Procurement Process Conditions and the Scope);
- (ss) **RFQ (or Request for Quotation)** means the request for quotations issued by the Principal and all documents included in or incorporated by reference into it (including these Procurement Process Conditions, the Contract and the Scope);
- (tt) **RFT (or Request for Tender)** means the request for tenders issued by the Principal and all documents included in or incorporated by reference into it (including these Procurement Process Conditions, the Contract and the Scope);
- (uu) **Scope** means the scope described in Part 4 Scope of the RFEOI or Part 5 Scope of the RFT or RFQ (as the case may be) and all documents incorporated into it (whether physically or by reference), and includes any amendments provided for in an Addendum;
- (vv) **Sound Contracting Principles** has the meaning given in section 104(3) of the *Local Government Act 2009* (Qld);

(ww) Specified Loss means:

- (i) any loss of, or loss of anticipated, profit, income, revenue, saving, production; business, contract or opportunity; increase in financing or operating costs; liability for loss or damage suffered by third parties; legal costs (on a solicitor and client basis); fines levied; loss of reputation or embarrassment and the cost of abating or reducing such; any other financial or economic loss; and
- (ii) any indirect, special or consequential loss, damage, cost, expense or penalty not expressly referred to in the preceding paragraph, howsoever arising;
- (xx) **Tender** means a Response lodged by a Tenderer in response to an RFT and includes all documents and information lodged with or as part of the tender;
- (yy) **Tender Box** means the website, email address or physical location at which the General Information states that Responses are to be submitted;

(zz) **Tenderer** means:

- (i) any person who lodges a Tender; and
- (ii) to the extent to which the term can apply to any other person who obtains a copy of any of the Procurement Documents during the Procurement Process, also includes such other persons,

and words or terms not defined in these Procurement Process Conditions but defined in a Contract have the same meaning as in the Contract, except where the context otherwise requires.

13. GENERAL PROVISIONS

- 13.1 (Interpretation of Procurement Documents) The Procurement Documents must be read and construed together and are intended to be mutually explanatory.
- 13.2 (**Joint and several obligations**) An obligation of two or more parties binds them jointly and each of them severally and an obligation incurred in favour of two or more parties is enforceable by them severally.
- 13.3 (**Headings**) Clause headings are for reference purposes only and must not be used in interpretation.
- 13.4 (**No limitation**) The words 'include', 'includes' and 'including' shall be read as if followed by 'without limitation'.
- 13.5 (**Grammatical Forms**) Where any word or phrase is given a defined meaning, any other part of speech or other grammatical form concerning the word or phrase has a corresponding meaning. Words importing the singular number include the plural number and words importing the plural number include the singular number.
- 13.6 **(Time)** References to time are to local time in Queensland. Where time is to be reckoned from a day or event, the day or the day of the event must be excluded. If any time period specified in the Procurement Documents expires on a day which is not a Business Day, the period will expire at the end of the next Business Day.
- 13.7 (**Discretion**) Unless expressly provided otherwise:
 - (a) any right of the Principal pursuant to these Procurement Process Conditions may be exercised; and
 - (b) any consent of the Principal required under these Procurement Process Conditions may be given, withheld or given subject to conditions,

in the absolute discretion of the Principal without giving reasons and without reference to the Respondent unless, and then only to the extent that the Procurement Process Conditions provide otherwise.

13.8 (Law) A reference to 'law' includes:

- (a) legislation (including subordinate legislation), local laws, by-laws, orders, ordinances, awards, requirements and proclamations of an Authority having jurisdiction and any related fees and charges; and
- (b) certificates, licences, accreditations, clearances, authorisations, approvals, consents, and permits and any related fees and charges,

which are applicable to the Procurement Documents, the Procurement Process or the Contract or which are otherwise in force at any place where an obligation under the Contract is to be carried out.

- 13.9 (Governing Law) The Procurement Process is governed by the laws of Queensland and the Commonwealth of Australia which are in force in Queensland. The Principal and the Respondent submit to the jurisdiction of the Courts of Queensland, relevant Federal Courts and Courts competent to hear appeals from them.
- 13.10 (**Contra proferentem**) The *contra proferentem* rule and other rules of construction will not apply to disadvantage a party whether that party put the clause forward, was responsible for drafting all or part of it or would otherwise benefit from it.
- 13.11 (**Rights Cumulative**) The rights and remedies of the Principal and the Respondent provided in the Procurement Process Conditions are cumulative on each other and on any rights or remedies conferred at law or in equity.
- 13.12 (**Severance**) If a provision of the Procurement Process Conditions is void or unenforceable it must be severed and the provisions that are not void or unenforceable are unaffected by the severance.
- 13.13 (**No waiver**) No waiver by the Principal of a provision of these Procurement Process Conditions is binding unless made in writing.

13.14 (Other references) A reference to:

- a person includes any other legal entity and a reference to a legal entity includes a person;
- (b) the Respondent or the Principal includes their respective heirs, executors, successors and permitted assigns;
- (c) writing includes any mode of representing or reproducing words in tangible and permanently visible form, and includes email and facsimile;
- (d) a monetary amount is a reference to an Australian currency amount; and
- (e) a measurement or quantity is a reference to an Australian legal unit of measurement as defined under the *National Measurement Act 1960* (Cth).



SCOPE

Shepherdsons Road Rehabilitation 2024-2025

CONTRACT NO.: T2425.31

1. INTERPRETATION AND DEFINITIONS

- 1.1 (**Documents comprising this Scope**) The Scope comprises the following documents:
 - (a) Appendix A Locality Maps;
 - (b) Appendix B IFC Drawings;
 - (c) Appendix C Cultural Heritage Report;
 - (d) Appendix D Pricing Schedule;
 - (e) Technical Specification; and
 - (f) General Specification.
- 1.2 (**Precedence**) If there is any ambiguity, inconsistency, conflict or discrepancy between any of the documents listed in clause 1.1, then the document which contains the higher standard or more onerous obligation will prevail. If that does not resolve the ambiguity, inconsistency, conflict or discrepancy then the documents will take precedence in the order set out in clause 1.1 with the document listed at 1.1(a) being the highest in the order.

2. APPROVALS AND OTHER LAW

- 2.1 (Identifying, obtaining and maintaining Approvals) The Supplier must identify and notify the Principal of all Approvals which are necessary for the proper performance of the Services (other than Approvals which the Principal has advised the Supplier it has already obtained). The Supplier must obtain and maintain all such Approvals until all of the Supplier's other obligations under the Contract are complete. The cost of obtaining and maintaining all such Approvals shall be borne by the Supplier.
- 2.2 (**Compliance**) The Supplier must and must ensure that its Personnel comply with all Approvals and other law which are in anyway applicable to the Services, including, unless the Contract expressly provides otherwise, by paying all fees, royalties, levies, charges, costs, expenses, taxes or duties.
- 2.3 (**Obtaining or granting of Approvals by Principal**) The Principal gives no warranty and makes no representation that:
 - (a) it will be able to obtain, or obtain within any particular time; or
 - (b) where the Principal is the relevant Authority, that it will grant,
 - any Approval required for the Supplier to perform the Services.
- 2.4 (**No fetter**) Nothing in the Contract shall be taken to fetter the power, rights or authority of the Principal as the sublessor under the *Land Act 1994* (Qld) or an Authority under the *Local Government Act 2009* (Qld), the *Local Government Regulation 2012* (Qld) or any other law.
- 2.5 (**Obligation to report breach**) The Supplier must notify the Principal immediately if it becomes aware of or reasonably suspects in the course of carrying out its obligations under the Contract, that the Supplier has breached an obligation under clauses 2.1, 2.2 or 2.3. Unless otherwise directed by the Principal, the Supplier must take immediate steps to remedy such a breach at its expense.

3. **PROCUREMENT SERVICES**

3.1 Where the Services require the Supplier to manage, conduct or otherwise participate in a Procurement Process for the engagement of a contractor or other supplier by the Principal, then

the Supplier must, and must ensure that its Personnel, to the extent that it is within the control of the Supplier or its Personnel ensure that the procurement process is conducted consistently with:

- (a) the Principal's procurement policy;
- (b) the Local Government Act 2009 (Qld) and the Local Government Regulation 2012 (Qld);
- (c) the requirements of the request for tender or request for quotation documentation issued to tenderers:
- (d) any probity plan or evaluation plan implemented for the Procurement Process;
- (e) principles of probity; and
- (f) Good Industry Practice,

with a view to ensuring that the selected contractor or supplier is the most advantageous to the Principal having regard to the sound contracting principles in section 104 of the *Local Government Act 2009* (Qld).

4. PRINCIPAL SUPPLIED INFORMATION AND OTHER INVESTIGATIONS

- 4.1 (**Definitions**) In this clause "**Principal Supplied Information**" means any information relating to the Contract which does not form part of the Contract but which is or has been provided or made available by or on behalf of the Principal to the Supplier in any form, whether such information is made available before or after the date of the Contract.
- 4.2 (Acknowledgement and agreement by Supplier) The Supplier acknowledges and agrees that:
 - (a) the Principal gives no warranty and makes no representation in respect of this Contract. Without limiting this, the Principal gives no warranty and makes no representation:
 - (i) that the Principal Supplied Information is accurate, adequate or complete; and
 - (ii) as to the physical condition, suitability or other characteristics of the Site;
 - (b) the Supplier has not relied and will not rely on the Principal Supplied Information unless and until the Supplier has independently verified the adequacy, accuracy and completeness of that information;
 - (c) the Supplier:
 - (i) has carefully, thoroughly and critically reviewed, examined, investigated, inspected and checked the Principal Supplied Information and the Site and undertaken all other necessary enquiries and investigations to satisfy itself of the suitability of the Site to enable the Supplier to comply with its obligations under this Contract and of any other logistical considerations, risks, contingencies and other circumstances which could have an effect on the cost of carrying out and completing Services or compliance with the Supplier's other obligations under the Contract;
 - (ii) the Supplier has made its own interpretations, deductions and conclusions from such enquiries and investigations and accepts full responsibility for those interpretations, deductions and conclusions; and

- (iii) the Supplier, having undertaken those enquiries and investigations, accepts the risk of any inadequacy, inefficiency, deficiency or fault in the Site and that it can and will carry out and complete the Services in accordance with the Contract and comply with its other obligations under the Contract for the Price (as adjusted pursuant to the Contract); and
- 4.3 (**No liability**) The Principal shall not be liable upon any Claim by the Supplier in connection with the Principal Supplied Information or the physical condition, suitability or other characteristics of the Site.

5. **SUPPLIER'S PERSONNEL**

- (Minimum Personnel levels) The Supplier must ensure that at all times during the Term, the minimum number of each type of Personnel identified in the Contract perform the roles identified in the Contract for the periods indicated in the Contract (Minimum Personnel Levels). The Minimum Personnel Levels must be maintained notwithstanding any planned or unplanned absences, personal breaks, attendance at training or performance of other duties by any Personnel. Provision of the Minimum Personnel Levels does not relieve the Supplier of any obligation under the Contract. If further Personnel are required in addition to the Minimum Personnel Levels for the Supplier to comply with its obligations under the Contract, then the Supplier must provide such additional Personnel at its expense.
- 5.2 (Further requirements on Personnel) In addition to any other requirement in the Contract, the Supplier must ensure that its Personnel:
 - (a) are familiar with and properly trained for their allocated role;
 - (b) perform their allocated role competently and safely and where the role involves the operation of plant or equipment, in accordance with all manufacturer's recommendations;
 - (c) do not either directly or indirectly cause any unreasonable nuisance or interference to the owners, tenants or occupiers of properties on or adjacent to the places where the Services are to be carried out (including Personnel of the Principal) or to the public generally;
 - (d) are not affected by alcohol or drugs whilst performing any part of the Supplier's obligations under the Contract (other than prescription medication which does not affect the ability of the person to perform the relevant obligations under the Contract).
- (Police checks) If the Principal directs the Supplier to obtain police checks then the Supplier must not permit any Personnel to perform any part of the Services or to have access to any of the Site unless and until 5 Business Days after the Supplier has given the Principal a written copy of a criminal history check produced by the Queensland Police Service for that person. If the criminal history check contains any entries, the Principal may, in its absolute discretion, notify the Supplier that the person is not permitted to perform the Services or may otherwise place conditions upon that person's role in performing the Services.

6. MANAGEMENT PLAN

- 6.1 (**Preparation**) The Supplier must, prior to commencing the Services, prepare and obtain the Principal's approval of a management plan or plans which addresses the following matters:
 - (a) Workplace Health and Safety Management;
 - (b) Environmental Management;
 - (c) Erosion and Sediment Control;

- (d) Quality Management; and
- (e) Traffic Management.

If the Principal notifies the Supplier that all or part of the plan(s) is not suitable, the Supplier must at its cost amend and resubmit the relevant plan(s).

- 6.2 (**Updating**) The management plan must be updated as often as required to:
 - (a) ensure that the Supplier continues to comply with the warranties and representations as to Supplier Documents given in the Contract;
 - (b) address any deficiencies in the systems described in the plan of which the Supplier becomes aware; and
 - (c) take into account any Variations or improvements in the Services.

A copy of a revised management plan must be submitted to the Principal for approval prior to implementation of it.

6.3 (**Compliance**) The Supplier must comply with the management plan at all times during the Term. Such compliance will not release or discharge the Supplier from any liability or obligation under the Contract.



GENERAL SPECIFICATION

Shepherdsons Road Rehabilitation 2024-2025

CONTRACT NO: T2425.31

Contents

| 1. | THE SPECIFICATION2 | 2 |
|-----|-------------------------------------------------------------------|---|
| 2. | DEFINITIONS2 | 2 |
| 3. | CONTRACTOR'S GENERAL OBLIGATIONS, WARRANTIES AND REPRESENTATIONS3 | 3 |
| 4. | CONTRACT MANAGEMENT | 4 |
| 5. | APPROVALS AND OTHER LAW | 5 |
| 6. | SITE6 | ò |
| 7. | PROGRAM | 3 |
| 8. | STAKEHOLDER MANAGEMENT |) |
| 9. | QUALITY MANAGEMENT SYSTEM10 |) |
| 10. | REPORTS, MEETINGS AND RECORD KEEPING11 | ı |
| 11. | PAYMENT CLAIMS13 | 3 |
| 12. | SAFETY14 | 1 |
| 13. | ENVIRONMENTAL PROTECTION14 | 1 |
| 14. | WASTE MANAGEMENT16 | ò |
| 15. | BIOSECURITY MANAGEMENT16 | ò |
| 16. | CULTURAL HERITAGE17 | 7 |
| 17. | TRAFFIC MANAGEMENT17 | 7 |
| 18. | HEAVY VEHICLE NATIONAL LAW18 | 3 |
| 19. | LABOUR HIRE20 |) |
| 20. | AS CONSTRUCTED DRAWINGS |) |
| 21. | PRACTICAL COMPLETION20 |) |

1. THE SPECIFICATION

- 1.1 (Documents comprising the specification) The specification comprises the following documents:
 - (a) this General Specification;
 - (b) Scope of Works;
 - (c) Technical Specifications;
 - (d) other documents to the extent that they are incorporated (whether physically or by reference) into the specification, namely:
 - (i) Water Services Association of Australia (WSAA) standard specification;
 - (ii) relevant Australian Standards;
 - (iii) Principal's Policies and Procedures:
 - (iv) Capricorn Municipal Development Guidelines;
 - (v) Department of Transport and Main Roads Specifications.
- 1.2 (Precedence of documents comprising specification) The documents comprising the specification shall be taken to be mutually explanatory. If there is any ambiguity, inconsistency, conflict or discrepancy between any of the documents listed in clause 1.1 then the documents will take precedence in the order set out in clause 1.1, with the document listed at 1.1(a) being the highest in the order.
- 1.3 (**Documents incorporated by reference into specification**) The Contractor is deemed to have obtained copies of, read, understood, and allowed for compliance with the Specification (including any documents which are incorporated into it by reference only).

2. **DEFINITIONS**

- 2.1 (**Definitions**) Capitalised terms used in the General Specification have the meanings assigned to them in the General Conditions of Contract (if any) unless the context otherwise requires. Terms which are separately defined in a specific clause have the meanings assigned in those clauses. Otherwise, in the General Specification:
 - (a) **Administrator** means, when used in or by reference to Department of Transport and Main Roads documents, the Superintendent;
 - (b) **Approvals** means certificates, licences, accreditations, clearances, authorisations, consents, permits, approvals, determinations, and permissions from any Authority and any related fees and charges;
 - (c) **Authority** means any Federal, State, or local government authority, administrative or judicial body or tribunal, department, commission, agency, government owned corporation, statutory body or instrumentality, or any other person having jurisdiction over the project;
 - (d) **General Conditions of Contract** means the General Conditions of Contract referred to in the formal instrument of agreement to which this General Specification is attached;
 - (e) General Specification means this document and all attachments to it which forms part of the Contract:
 - (f) Good Industry Practice means:

- (i) the standard of skill, care, and diligence; and
- (ii) the practices, methods, techniques, and acts,

of a skilled, competent, and experienced contractor engaged in the business of carrying out Work similar to the WUC:

- (g) **Principal** has the same meaning as given to the term "Principal" or "Purchaser" in the General Conditions of Contract (as the case may be);
- (h) **Principal's Policies and Procedures** means the policies, procedures, codes, plans, guidelines, and the like provided or made available by or on behalf of the Principal to the Contractor from time to time, including those published on the Principal's website which are in any way applicable to this Contract;
- (i) **Program** has the same meaning as given to the term "construction program" or "program" in the General Conditions of Contract (as the case may be);

3. CONTRACTOR'S GENERAL OBLIGATIONS, WARRANTIES AND REPRESENTATIONS

- 3.1 **(Ability)** The Contractor must ensure, and warrants and represents that the Contractor and, to the extent applicable to them, its Personnel:
 - (a) have the experience, skills, expertise, and resources;
 - (b) hold all necessary competencies, licences, accreditations, qualifications, permits, clearances, or other authorisations,

which are required for the Contractor to comply with its obligations under the Contract and will maintain such competencies, licences, accreditations, qualifications, permits, clearances, or other authorisations at all times until the Contractor has completed its obligations under the Contract.

- 3.2 **Standard**) The Contractor must, and warrants and represents that it will, and to the extent applicable to them will ensure that its Personnel, carry out WUC and Contractor's other obligations in connection with the Contract in accordance with Good Industry Practice.
- 3.3 (**Methodology**) The Contractor:
 - (a) warrants and represents that the methodology for carrying out and completing WUC stated in the Contract is suitable, appropriate and adequate; and
 - (b) must, and warrants and represents that it will, carry out and complete WUC in accordance with that methodology (if any) unless otherwise directed by the Superintendent or permitted or required under the Contract.
- 3.4 **(Goods)** The Contractor warrants and represents that all plant, equipment, materials, parts, consumables or other goods ('Goods') supplied, used or installed as part of WUC shall:
 - (a) at the time that they are supplied, used, or installed, be new;
 - (b) be free from defects and of merchantable quality;
 - (c) comply in all respects with the Contract including as to quality, quantity, performance, functionality and description;
 - (d) conform to any sample goods approved by the Principal or Superintendent;
 - (e) comply with any applicable requirement, code, guideline, policy, drawing, or specification included or incorporated by reference into the Contract or, if none is

- included or incorporated, any Australian Standards applicable to the Goods and any applicable Legislative Requirements; and
- (f) be suitable and adequate for the purposes for which they are supplied, used or installed.
- 3.5 (Investigations) The Contractor warrants and represents that the Contractor has:
 - (a) carefully reviewed the Contract and all other information provided by the Principal to the Contractor for the purpose of WUC, and is satisfied that the Contract and other information is appropriate and adequate to enable the Contractor to comply with its obligations under the Contract;
 - (b) inspected the Site;
 - (c) familiarised itself with factors that could affect the ability of the Contractor to carry out WUC for the Contract Sum, including weather conditions and the availability of temporary access, temporary lighting, power, telephone services, water supply, waste disposal facilities and local labour.
- 3.6 (**Construction Plant**) The Contractor warrants and represents that all Construction Plant utilised in carrying out WUC shall be in good working condition, suitable and appropriate for the Work for which it is used, and compliant with all applicable Legislative Requirements.
- 3.7 (Contractor Documents) The Contractor warrants and represents that all Contractor Documents will:
 - (a) comply with the requirements of the Contract and applicable law;
 - (b) be consistent with or exceed applicable industry standards;
 - (c) be of a standard and quality expected of a contractor using Good Industry Practice;
 - (d) be suitable and adequate for the purpose for which they are provided.

In this clause, Contractor Documents means:

- (i) those records, reports, designs, specifications, certificates, plans (including management plans), procedures, manuals and other documents, whether electronic documents or hard copy format, required by the Contract to be handed over to the Principal by the Contractor; and
- (ii) all information advice, designs, calculations and recommendations in those documents;

but does not include those that are incomplete at the time at which the Principal exercises its rights under subclause 39.4 of the General Conditions of Contract or the Contractor exercises its rights under subclause 39.9 of the General Conditions of Contract);

4. CONTRACT MANAGEMENT

- 4.1 (Contractor's Superintendence) The Contractor shall provide all superintendence necessary for the proper fulfilment of the Contractor's obligations under the Contract, including, unless the Superintendent directs otherwise, a competent site manager and site foreman approved by the Superintendent (with such approval not to be unreasonably withheld). Unless otherwise agreed by the Superintendent, the site manager shall be the Contractor's representative under clause 22 of the General Conditions of Contract.
- 4.2 (Requests for review and information) The Superintendent will endeavor to provide a response and/or Direction in relation to a written request for information from the Contractor within 5 Business Days of receipt of such request. The response time will be dependent on the

complex nature and or quantity of clarifications per information request submitted. The Contractor is encouraged to make recommendations and or suggestions for the Superintendent's consideration when submitting such requests.

- 4.3 (**Direction by Principal or Superintendent**) The Principal shall not be bound by any verbal advice given or information furnished by any Personnel of the Principal or Superintendent in respect of the Contract. The Contractor must not accept instructions from any person other than the Superintendent and/or the Superintendent's Representative. The Contractor acknowledges and agrees that its obligations and liabilities in connection with the Contract are not affected by any:
 - (a) receipt or review of, or comment or Direction on, a document submitted by the Contractor;
 - (b) failure by the Principal or Superintendent to review, comment on, or give a Direction on any document submitted by the Contractor; or
 - (c) failure by the Superintendent to give its approval pursuant to clause 8.3.

Before relying on the receipt, review, or comment by the Superintendent, or Principal, or complying with a Direction in relation to a document, the Contractor must notify the Superintendent in writing, if doing so will affect a warranty, representation or obligation of the Contractor under the Contract.

- 4.4 (**Code of Conduct**) In this clause, 'Code of Conduct' means the Principal's code of conduct which is available on the Principal's website. The Code of Conduct identifies the standards and behaviours expected from all workers, including contractors, in delivering services to the local community. The Contractor must:
 - (a) communicate the Code of Conduct to all of the Contractor's Personnel;
 - (b) comply with, and ensure that its Personnel comply with, all requirements of the Code of Conduct, including all standards contained within the Code of Conduct; and
 - (c) if directed to do so by the Superintendent, obtain and provide to the Superintendent a signed form from all Personnel engaged by the Contractor to perform any part of WUC which states that the person has read, understood and agrees to comply with the Code of Conduct.

5. APPROVALS AND OTHER LAW

- 5.1 (Identifying, obtaining and maintaining Approvals) The Contractor must identify and notify the Principal of all Approvals which are necessary for the proper performance of WUC (other than Approvals which the Principal has advised the Contractor it has already obtained). The Contractor must obtain and maintain all such Approvals until the end of the last Defects Liability Period to expire. The cost of obtaining and maintaining all such Approvals shall be borne by the Contractor.
- 5.2 (**Compliance**) The Contractor must ensure that its Personnel comply with all Approvals and other laws which are in anyway applicable to WUC, including, unless the Contract expressly provides otherwise, by paying all fees, royalties, levies, charges, costs, expenses, taxes, or duties.
- 5.3 (**Obtaining or granting of Approvals by Principal**) The Principal gives no warranty and makes no representation that:
 - (a) it will be able to obtain, or obtain within any particular time; or
 - (b) where the Principal is the relevant Authority, that it will grant,

- any Approvals required for the Contractor to perform WUC.
- 5.4 **(Timing)** The Contractor is deemed to have allowed a reasonable time in the Program for all required Approvals to be applied for and obtained.
- 5.5 (**No fetter**) Nothing in the Contract shall be taken to fetter the power, rights, or authority of the Principal as an Authority under the *Local Government Act 2009* (Qld), the *Local Government Regulation 2012* (Qld), or any other law.

6. SITE

- 6.1 (Location) The Site is identified in Appendix A.
- 6.2 (Requirements of access or possession) The Contractor's attention is drawn to clause 24 of the General Conditions of Contract. The Contractor must provide the following documentation and information to the Superintendent. The documentation and information must be provided:
 - (a) in a form that complies with the requirements of the Contract;
 - (b) as a requirement of the Principal giving access to or possession of the Site; and
 - (c) within the earlier of:
 - (i) 20 Business Days after the Date Of Acceptance Of Tender; and
 - (ii) 5 Business Days prior to any scheduled pre-start meeting.

| Item | Description | Relevant clause |
|------|-----------------------------------------------|--------------------------------------------------------------------------|
| (A) | Updated Program | Clause 77 of this General Specification |
| (B) | Quality management plan | Clause 9.2 of this General Specification |
| (C) | Inspection and test plan | Clause 9.3 of this General Specification |
| (D) | Dilapidation survey | Clause 10.66 of this General Specification |
| (E) | Environmental management plan | Clause 13.22 of this General Specification |
| (F) | Erosion and sedimant control plan | Clause 13.33 of this General Specification |
| (G) | Biosecurity risk management plan | Clause 15.25 of this General Specification |
| (H) | Traffic management plan | Clause 17 of this General Specification |
| (1) | Compliance Plan | Clause 10.3 of this General Specification |
| (J) | Security in the form required by the Contract | Clause 2 and Annexure Part A of the General Conditions of Contract |

- 6.3 (Site specific induction) The Contractor must ensure that:
 - (a) each of the Contractor's Personnel working on Site receives a site-specific induction;

- (b) every visitor to the Site either receives a site-specific induction or is accompanied at all times at the Site by someone who has received a site-specific induction for that Site (or, where the Site comprises more than one location, the particular part of the Site).
- 6.4 (Site specific requirements) The Contractor must comply with the reasonable requirements of the Principal in relation to the Contractor's access to or conduct on the Site.
- 6.5 (**Locations within Site**) The Contractor must ensure that all plant, equipment, materials, temporary workshops, stores, and offices are kept within the confines of the Site at locations approved by the Superintendent.
- 6.6 (**Unauthorised entry to site**) The Contractor must use all reasonable endeavours to prevent any unauthorised entry to the Site.
- 6.7 (**Security fencing**) The Contractor must supply, install, maintain, repair, and remove security fencing around the Site. The security fencing must:
 - (a) clearly identify the extents of the Site to the public;
 - (b) be covered with opaque screening/printed fence wrap to limit viewing into the Site and include any graphic design provided by the Principal; and
 - (c) be kept in good condition.
- 6.8 (**Signage**) No signage is to be placed on the Site or the perimeter (other than safety signage) without the prior written consent of the Superintendent.
- 6.9 (**Deliveries**) The Contractor is responsible for delivery and unloading of all goods, equipment and other materials used in WUC (including any such materials used by subcontractors), providing space for the storage of the materials, handling the materials, and checking that the materials comply with the requirements of the Contract.
- 6.10 (**Setting out**) The Contractor's attention is drawn to clause 26 of the General Conditions of Contract. The Contractor must:
 - (a) set out The Works from the information shown on the drawings;
 - (b) check all dimensions on Site before proceeding with WUC; and
 - (c) notify the Superintendent of any omissions or discrepancies within the drawings or General Specification.

Notwithstanding subclause 26.2 of the General Conditions of Contract, any errors in the position, level, dimensions, or alignment of any WUC shall be rectified at the Contractor's expense, unless the Contractor gave the Superintendent written notice of the error before commencing Work in reliance on the erroneous position, level, dimension, or alignment.

- 6.11 (Interference) The Contractor must use all reasonable endeavours to minimise interference with existing amenities, whether natural or man-made, and the amount of noise caused by the carrying out of WUC.
- 6.12 (**Public utilities and other assets**) Without limiting the Contractor's obligations under clause 15 of the General Conditions of Contract, the Contractor must use all reasonable endeavours to identify, locate, and prevent damage to overhead public utility lines, surface drainage works, underground pipes, conduits, and cables in the vicinity of The Works. If the Contractor or any of its Personnel damage any such assets, then:
 - (a) the Contractor must immediately report such damage to the owner of the asset and the Superintendent; and

(b) comply with the requirements of the owner of the asset (including by paying for any required repairs or renewals).

The Contractor must notify the Superintendent immediately if the Contractor considers that it is necessary to alter the location or level of any existing assets to conform with the requirements of the Contract. If directed to do so by the Superintendent, the Contractor must arrange for the relocation Work to be carried out by the appropriate Authority. Subject to clause 25 of the General Conditions of Contract, the Contractor shall bear the cost of such relocation.

6.13 (Other property) The Contractor must:

- (a) arrange for any other land (in addition to land made available by the Principal) required by the Contractor to carry out WUC, whether for the storage of materials, plant, or equipment, or for any other purposes;
- (b) obtain the Principal's permission in writing to enter any private property (as that term is defined in the *Local Government Act 2009* (Qld) ('Private Property') before entering the Private Property for the purpose of carrying out WUC or fulfilling any other obligation of the Contractor under the Contract;
- (c) comply with all Legislative Requirements, including the *Local Government Act 2009* (Qld) in relation to entering Private Property;
- (d) not unreasonably obstruct, destroy, or damage any Private Property, other land or other property, and ensure that all roadways, drains, watercourses, buildings, fences, gardens, walls, concrete surfaces and paths, grass and trees, and other property are left in a condition equivalent or better than that in which the property was found, unless the Contractor provides written evidence that the owner of the property agrees otherwise;
- (e) take over control of any approval, permit, or license that the Principal has in place, in relation to the Site or other land made available by the Principal, prior to commencing any WUC on the Site or using or occupying the other land.

7. PROGRAM

7.1 (Format and details) The Program shall:

- (a) be prepared utilising native format Microsoft Project software, or alternative software as approved in writing by the Superintendent;
- (b) be submitted in electronic format with copies in both PDF format and native Microsoft Project file format; and
- (c) detail the Contract milestone dates, the commencement and completion dates of each trade, and/or sub-contract;
- (d) work activity, procurement activities and supply contract activity, with activities linked in a logical progression through a 'critical path' and identify any float based on a continuous cycle of WUC.
- 7.2 (Allowances in program) The Contractor must allow, and is deemed to have allowed, in the program for:
 - (a) the time permitted under the General Conditions of Contract for the Superintendent to review documents for which the Contract requires the Contractor to obtain the Superintendent's Direction about such documents; and
 - (b) other timeframes under the Contract within which the Superintendent and the Principal are permitted to act.

- 7.3 (Approval of Program) The approval of, or permission to adopt, a Program by the Superintendent will not relieve the Contractor of any of its obligations under the Contract, including the obligation to not, without reasonable cause, depart from an earlier approved Program.
- 7.4 (**Improving progress**) If, in the opinion of the Superintendent, the Contractor falls behind an approved Program, the Contractor must, unless otherwise directed by the Superintendent:
 - (a) take such steps as are necessary to improve progress (including the use of additional resources):
 - (b) promptly, and within the time directed by the Superintendent, submit a revised Program, identifying the steps taken or to be taken.

The Principal shall not be liable upon any Claim in connection with the Contractor's compliance with this clause.

8. STAKEHOLDER MANAGEMENT

- 8.1 (Notice to Superintendent) With respect to notification, the *Contractor* shall give the Superintendent a minimum of 15 business days' written notice of changes in traffic movements or any Work impacting individual property owners or businesses. The notice shall be clearly titled 'Notice of Changes in Traffic Movements' or 'Notice of Any Works Impacting Individual Property Owners or Businesses' and contain the following information:
 - (a) title of notice;
 - (b) start and finish dates of Work;
 - (c) purpose of communications;
 - (d) type and length of interruption;
 - (e) affected locations (chainages, streets, property accesses, etc);
 - (f) whether the works subject to weather;
 - (g) who is carrying out the works (i.e. contractor or subcontractor); and
 - (h) Contractor details.
- 8.2 (Notice to stakeholders) The Principal shall be responsible for undertaking public notification distributing through their normal channels. The Contractor shall be responsible for hand delivering written notices prepared by the Principal to individuals impacted and must do so not later than 5 Business Days prior to commencing the Works. The Contractor shall also send a copy of the written notice via registered post 5 Business Days prior to commencing The Works with a covering letter confirming the dates and times the written notice was hand delivered.
- 8.3 (**Sign board**) The Contractor must provide a sign board comprising the following information, at the entrance to the Site or as required:
 - (a) Contractor's name;
 - (b) Contractor's postal address; and
 - (c) Site supervisor's name and 24-hour contact number.
- 8.4 (Complaints) With respect to complaints, the Contractor shall:

- (a) maintain a record of any complaints received from any stakeholder or the public, including documentary evidence that complaints have been addressed and attended to, to the satisfaction of the Superintendent; and
- (b) discuss all complaints with the Superintendent promptly after being made aware of it and follow any directions of the Superintendent in relation to the complaint.

9. QUALITY MANAGEMENT SYSTEM

- 9.1 (**General**) The Contractor must:
 - (a) prior to commencing WUC at the Site, implement a quality management system which accords with the requirements of ISO 9001 or with any alternative standard approved by the Superintendent (acting reasonably);
 - (b) provide a copy of the ISO9001 certification (or other documentary evidence suitable to the Superintendent, acting reasonably) of the Contractor's system;
 - (c) comply with, and ensure that all of the Contractor's Personnel comply with the system;
 - (d) appoint a suitably qualified quality management representative, who shall have such authority to effectively manage and control the implemented quality system.
- 9.2 (Quality management plan) The Contractor's quality management system must include a quality management plan which contains at least the following information:
 - (a) a project organisation chart clearly showing the lines of authority, responsibility, and communication that will be in effect;
 - (b) details of the qualifications and experience of all project management and supervision staff;
 - (c) a lot plan;
 - (d) details of project specific procedures, including those related to the following to the extent that they are applicable to WUC:
 - (i) all shop drawing formation and coordination;
 - (ii) management of all services subcontractor/trades;
 - (iii) management of all services/operational commissioning;
 - (e) applicable inspection and test plans;
 - (f) a register of all proposed quality records; and
 - (g) a copy of the NATA terms of registration for the Contractor's compliance testing laboratory.

The Contractor must obtain and comply with the Superintendent's Direction regarding the plan pursuant to subclause 8.3 of the General Conditions of Contract.

- 9.3 (Inspection and test plan) The Contractor must, as part of the Contractor's quality management system, prepare and obtain the Superintendent's Direction regarding an inspection and test plan. The inspection and test plan must, at a minimum, detail:
 - (a) the items of Work to be inspected or tested;
 - (b) the party who will carry out the inspection or test;

- (c) the stages at which Work is to be inspected and tested or the frequency of inspections and tests;
- (d) the testing procedures and methodologies;
- (e) acceptance criteria;
- (f) non-conformance management and corrective processes;
- (g) Work which shall not be covered up or made inaccessible without the prior approval of the Superintendent;
- (h) witness points for Work for which a Superintendent's Representative must be present;
- (i) hold points beyond which Work cannot proceed without approval of the Superintendent;
- (j) relevant standards; and
- (k) the records to be maintained by the Contractor.

The Contractor must obtain and comply with the Superintendent's Direction regarding the plan pursuant to subclause 8.3 of the General Conditions of Contract.

- 9.4 (**Reporting**) The Contractor must provide the Superintendent with all documents and information:
 - (a) reasonably requested to support or evidence the Contractor's quality management system:
 - (b) which are produced by the Contractor in compliance with the quality management system.
- 9.5 (Inspections) The Principal and the Superintendent may carry out inspections of the Site at any time. During inspections, the Contractor shall provide the Principal and the Superintendent with all documents, access and assistance reasonably requested by either. The Contractor shall provide a sufficient and safe access for all inspections at the Site. Unless otherwise specified, the Contractor must give the Superintendent no less than 2 Business Days' notice of its intention to commence each stage of the following Work (further details are listed in the Technical Specifications).

If the Contractor does not provide the required notification for an inspection, particularly in the event that an urgent after-hours inspection is required to ensure WUC is not delayed, the Superintendent may deduct the cost of the inspection as a Required Deduction pursuant to clause 37.2 of the General Conditions of Contract.

10. REPORTS, MEETINGS AND RECORD KEEPING

- 10.1 (**Progress reports**) The Contractor must:
 - (a) keep the Principal fully informed of the progress and performance of WUC;
 - (b) at the times stated in the Contract and when otherwise reasonably required by the Principal, meet and discuss the performance of the Contractor and/or any other matter concerning the Principal in connection with the Contract; and
 - (c) comply with any recommendations or directions given by the Principal in relation to the performance of the Contractor's obligations under the Contract (but such compliance will not release or discharge the Contractor from any liability or obligation under the Contract).

10.2 (Meetings) The Contractor must, at the times reasonably required by the Principal, meet and discuss the performance of the Contractor and/or any other matter concerning the Principal in connection with the Contract. The Contractor shall provide a sufficient and safe access for all meetings at the Site.

Without limiting the preceding paragraph, the Contractor must attend and ensure that the Personnel noted below attend the following meetings:

| Item | Meeting description | Topics for discussion | Time for meetings | Required attendees |
|------|------------------------|-------------------------------------------------------------------------------------------------------------------------------|-------------------|---------------------------------------------------------|
| (a) | Pre-start meeting | Discussion of the requirements of the contract and answer any questions the contractor may have regarding the project/designs | | Contractor Project Management / Supervision Staff |

10.3 ((**Record of compliance**) The Contractor must:

- (a) create and maintain complete and accurate records, reports and other documents demonstrating the Contractor's compliance with the Contract, including:
 - (i) Quality Records (including survey results confirming quantities and test and inspection results);
 - (ii) Site Safety and Environmental records;
 - (iii) As constructed survey.

and any other records, reports or documents reasonably required by the Principal in connection with the Contract; and

- (b) create any document required to be prepared under any management plan prepared under the Contract.
- 10.4 (Audit) The Principal may at any time up to the expiry of the last Defects Liability Period to expire (or where the Contract is earlier terminated, up to 12 months after the date on which the termination takes effect), on the giving of reasonable notice, audit the Contractor's compliance with the Contract or any obligation under it. The Contractor shall facilitate the audit by:
 - (a) allowing the auditors to undertake any inspections;
 - (b) providing such assistance, information and access to the Site, systems and equipment and other cooperation;
 - (c) providing the auditor with copies of, and facilitating the copying by the auditor of, all the other records, information, and documentation required to be created under clause 10,

as reasonably required by the auditor. If the audit reveals any non-compliance by the Contractor with its obligations under the Contract, then the costs reasonably and necessarily incurred by the Principal in conducting the audit shall be a debt due and payable by the Contractor. Otherwise, the Principal shall bear the cost of the audit. For clarity, the Contractor is not required to provide to the Principal under this clause, any documents to the extent that they contain material which is subject to legal professional privilege.

10.5 (**Photographic evidence**) The Contractor must provide to the Superintendent a progressive photographic record of the progress of WUC at the following stages and as otherwise reasonably required by the Superintendent:

| Item | Stages at which photographic record to be made | |
|------|-----------------------------------------------------------------------------------------------------|--|
| (a) | On the giving of possession of the Site | |
| (b) | At the end of each calendar month prior to the month in which Practical Completion is achieved; and | |
| (c) | At Practical Completion. | |

Photographs shall be in high-definition digital format and shall be dated and labelled to describe the photograph's content.

- 10.6 (**Dilapidation survey**) The Contractor must, prior to the commencement of WUC, undertake a dilapidation survey including a photographic record clearly indicating the date and time of photos taken, of all areas identified as forming part of the Site and the following areas:
 - (a) Any stockpile/plant parking area
 - (b) If project site office/compound location is created, the area used for this purpose.

The dilapidation survey shall be replicated prior to and as a requirement of Practical Completion. The purpose of this survey is to confirm the pre and post-construction condition of the Site. The dilapidation survey shall be completed by the Contractor in the company of the Superintendent.

11. PAYMENT CLAIMS

- **11.1** (Additional documentation) In addition to the requirements stated in the General Conditions of Contract, the Contractor must provide the following documentation with each claim for payment submitted under the Contract:
 - (a) Evident of the completion of the works included in the claim being to the standard required by this contract (including copies of all compliance test results);
 - (b) Surveyors reports (as applicable) to support the quantities listed in the claim; and
 - (c) Full breakdown (as per the supplied day labour rates) of any variation claims, with a copy of the written instruction from the Principal for the undertaking of the additional works.
- 11.2 (Particular items in Price Schedule) Further to clause 3 of the General Conditions of Contract where an item is identified in the Price Schedule as:
 - (a) a prime cost item, then the relevant sum(s) included in the Price Schedule shall in themselves not be payable, but where that item of Work is to be supplied or carried out:
 - (i) the Contractor must, if directed to do so by the Superintendent:
 - (A) use its best endeavours to obtain 3 quotes for the prime cost item from suppliers which the Contractor considers are capable of carrying out the relevant Work and that are reasonably available to do so; and
 - (B) provide a complete written copy of each quote received to the Superintendent;

- (ii) the Superintendent may (but shall not be obliged to) within 5 Business Days after receiving the quotation(s) direct the Contractor as to which supplier to engage and the Contractor must comply with that Direction. If the Superintendent does not give a Direction within this time, then the Contractor may engage any one of the suppliers that provided a quotation;
- (iii) the Contractor shall be entitled to payment of the actual direct cost paid by the Contractor to the supplier for the supply of that item (excluding any damages payable to the supplier or vice versa) and without any payment for the Contractor's profit and overheads; and
- (iv) the costs for labour, installation, and for all other costs required to incorporate the goods into The Works shall be deemed to have been included in the Price Schedule generally;
- (b) a provisional quantity, provisional item, if ordered, as directed, optional or similar term (other than provisional sum), then where that item of Work is supplied or carried out in accordance with a Direction of the Superintendent:
 - (i) the relevant sum(s) included in the Price Schedule shall in themselves not be payable;
 - (ii) where there is a rate for the item in the Price Schedule, the Contractor shall be entitled to payment for the item at the rate provided in the Price Schedule for the measured quantity of the item so supplied or carried out; or
 - (iii) where there is a lump sum for the item in the Price Schedule, the Contractor shall be entitled to payment of that lump sum,

A Direction to carry out or supply such an item, or the absence of a direction to carry out or supply such an item, shall be deemed to be within the general scope of the Contract.

12. SAFETY

12.1 (Relationship to General Conditions of Contract) The Contractor's attention is drawn to clause 12A of the General Conditions of Contract. Nothing in clause 12 shall be taken to limit or exclude any obligation or liability of the Contractor under the General Conditions of Contract or at law in relation to work, health and safety.

13. ENVIRONMENTAL PROTECTION

- 13.1 (**Environmental protection**) The Contractor must, and must ensure that its Personnel, perform the Contractor's obligations in accordance with:
 - (a) best practice environmental management (as that term is defined in Section 21 of the Environmental Protection Act 1994 (Qld));
 - (b) the requirements of all other Legislative Requirements relating to the protection of the Environment; and
 - (c) the Principal's policies and procedures relating to the protection of the Environment.
- 13.2 (Environmental Management Plan) The Contractor must, within the time required by clause 6.2, prepare and provide to the Superintendent for review an environmental management plan ('EMP') for WUC, detailing how the Contractor will prevent or minimise the risk of harm to the environment in performing its obligations under the Contract. The Contractor must obtain and comply with the Superintendent's Direction regarding the plan pursuant to subclause 8.3 of the General Conditions of Contract. The Contractor must comply, and ensure that all of the Contractor's Personnel comply, with the EMP at all times until the expiration of the last Defects liability Period to expire. The EMP must:

- (a) comply with ISO14001;
- (b) cover all WUC to be undertaken at the Site;
- (c) describe the Contractor's process and procedures for the management of the risk of harm to the environment in connection with WUC;
- (d) be consistent with relevant Australian Standards and Legislative Requirements;
- (e) be a practical and achievable plan;
- (f) detail each environmental issue and impact which is to be addressed;
- (g) include all control measures which the Contractor shall undertake and any issues which the Contractor shall address during the construction process (including any required pre or post construction activity);
- (h) detail who is responsible for ensuring the control measures are undertaken, the verification of such actions, and the reporting process;
- (i) provide a trigger for undertaking an action, and where possible, timing of each action;
- (j) detail procedures for the monitoring of the EMP by the Contractor;
- (k) detail a procedure for recording any non-compliance with the EMP; and
- (I) detail a system for registration and action of environmental complaints.

If the Contractor wishes to commence any WUC prior to obtaining the Superintendent's Direction in relation to the complete EMP, sections of the EMP relevant to that WUC may be submitted at least 10 Business Days prior to the planned commencement of that WUC. A hold point shall occur and no WUC shall proceed until written acceptance of the complete EMP or a section of the EMP relevant to a particular construction operation is received from the Superintendent.

- 13.3 (Erosion and sediment control plan) The Contractor must prepare and obtain the Superintendent's Direction regarding an erosion and sedimentation control plan ('ESCP') pursuant to subclause 8.3 of the General Conditions of Contract. The ESCP must describe the Contractor's process and procedures for the prevention or minimisation of harm caused by erosion and sediment in connection with WUC, including by control of overland flows, minimisation of flow path lengths, and the use of trapping devices to capture sediment. The Contractor must undertake the installation, inspection, repair, and maintenance of all environmental control measures required by the ESCP. The Contractor must inspect all environmental control measures at least:
 - (a) once each week;
 - (b) immediately after any major rainfall event; and
 - (c) as otherwise directed by the Superintendent.
- 13.4 (**Protection of Fauna**) The Contractor must:
 - use all reasonable endeavours to minimise disruption to any fauna at or in the vicinity of the Site;
 - (b) ensure that each of the Contractor's Personnel and every other person carrying out WUC at the Site:
 - (i) is appropriately trained in relation to the protection of fauna prior to carrying out any part of WUC;

(ii) aware of the potential for impacts on fauna and the need to minimise these impacts,

prior to that person carrying out any WUC; and

- (c) use all reasonable endeavours to ensure that each of the Contractor's Personnel and every other person carrying out WUC at the Site minimises disruption to any fauna in the vicinity of the Site; and
- (d) at the Contractor's expense, comply with any Directions issued by the Superintendent to address any excessive or avoidable adverse impact on fauna at or in the vicinity of the Site.

13.5 (**Protection of Flora**) The Contractor must:

- use all reasonable endeavours to minimise disruption to any flora at or in the vicinity of the Site;
- (b) ensure that each of the Contractor's Personnel and every other person carrying out WUC at the Site is appropriately trained in relation to the protection of flora prior to that person carrying out any part of WUC;
- (c) use all reasonable endeavours to ensure that that each of the Contractor's Personnel and every other person carrying out WUC at the Site minimises disruption to existing flora at or in the vicinity of the Site;
- (d) make good any damage to flora caused by the Contractor or its Personnel, other than damage which is the unavoidable consequence of carrying out WUC; and
- (e) at the Contractor's expense, comply with any Directions issued by the Superintendent to address any excessive or avoidable adverse impact on flora at or in the vicinity of the Site.

14. WASTE MANAGEMENT

14.1 (**Definitions**) In this clause 'Levyable Waste Disposal Site", "Levyable Waste", "Waste", "Waste Disposal Site" and "Waste Levy" have the meanings given to those terms in the *Waste Reduction and Recycling Act 2011* (Qld).

14.2 (Contractor's obligation) The Contractor must:

- (a) ensure that all Waste from the Site is placed in appropriate containers and removed from the Site to a legal Waste Disposal Site in accordance with the *Waste Reduction* and *Recycling Act 2011* (Qld) and any other applicable Legislative Requirements;
- (b) otherwise, ensure that all Waste arising from WUC is disposed of in accordance with the requirements of the *Waste Reduction and Recycling Act 2011* (Qld) and any other applicable Legislative Requirements relating to the disposal of Waste; and
- (c) pay all royalties, levies, fees, charges, costs, expenses, taxes, or duties in connection with the disposal of Waste.
- 14.3 (**Energy Use**) The Contractor shall ensure that the use of energy for WUC is minimised by undertaking regular maintenance of all machinery to ensure energy efficiency and by utilising minimum sized machinery to undertake tasks.

15. BIOSECURITY MANAGEMENT

15.1 (**Definitions**) In this clause:

(a) a **Biosecurity Risk** is the risk that exists when dealing with:

- (i) any pest, disease, or contaminant (including plants, seeds, spores, eggs, vertebrate, and invertebrate pest); or
- (ii) something that could carry a pest, disease or contaminant (e.g., animals, plants, soil, equipment and water—known as 'carriers').
- (b) a **Potential Biosecurity Risk** is a Biosecurity Risk that does not currently occur at the Site, but which has the capacity to occur at the Site. It may be present but not visible or may be introduced during WUC. It includes risks associated with carriers and the movement and sourcing of materials, vehicles, and machinery; and the disturbance, import, or export of soils;
- (c) a **Known Biosecurity Risk** is a Biosecurity Risk that is currently recorded within the footprint or proximity of the Site which is:
 - (i) identified within biosecurity plans or programs active for the area;
 - (ii) identified during WUC; or
 - (iii) otherwise identified by the Principal;
- (d) **BRMP** means a Biosecurity Risk management plan;
- (e) **General Biosecurity Obligation** has the meaning given to that term in the *Biosecurity Act 2014* (Qld).
- 15.2 (**Biosecurity Risk management plan**) The Contractor must prepare and obtain the Superintendent's Direction regarding a BRMP pursuant to subclause 8.3 of the General Conditions of Contract. The BRMP must:
 - describe the processes and procedures for the management of Biosecurity Risks in connection with WUC;
 - (b) outline reasonable and practical steps to address Biosecurity Risks;
 - (c) describe how the Contractor will meet its General Biosecurity Obligation;
 - (d) address both Potential Biosecurity Risks and Known Biosecurity Risks.

The Contractor must comply with and ensure that all of the Contractor's Personnel comply with the BRMP.

15.3 (**Training**) The Contractor must ensure that each of the Contractor's Personnel and every other person carrying out WUC at the Site is appropriately trained to be aware of Biosecurity Risks prior to that person carrying out any part of WUC. If at any time during WUC a breach of the BRMP or a significant Biosecurity Risk is identified, then the Contractor must immediately contact the Superintendent for Direction.

16. CULTURAL HERITAGE

16.1 (Compliance) Without limiting any other obligation of the Contractor under the Contract or any law, the Contractor's attention is drawn to, and the Contractor must comply, and must use all reasonable endeavours to ensure that its Personnel comply with the requirements of, the Aboriginal Cultural Heritage Act 2003 (Qld), Torres Strait Islander Cultural Heritage Act 2003 (Qld) and the Aboriginal and Torres Strait Islander Heritage Protection Act 1984 (Cth).

17. TRAFFIC MANAGEMENT

17.1 (**Traffic management plan**) The Contractor must comply with the Principal's traffic management plan for WUC.

17.2 (General) The Contractor:

- is responsible for the safety of all pedestrians and vehicular traffic at, or adjacent to the Site, or in any way affected by the execution of WUC;
- (b) must provide all necessary lights, barriers, notices and signs, and other traffic control devices required for the safe and appropriate management of traffic.
- (c) must comply with and ensure that all traffic control devices conform to:
 - (i) the current Manual of Uniform Traffic Control Devices published by the Department of Transport and Main Roads;
 - (ii) Queensland Guide to Temporary Traffic Management;
 - (iii) AS1742 Manual of Uniform Traffic Control Devices;
 - (iv) Austroads Australian Guide to Temporary Traffic Management;
 - (v) Queensland Guide to Road Safety;
 - (vi) Guideline Traffic Management at Works on Roads,

as amended or replaced from time to time. In the event of any inconsistency, ambiguity, discrepancy, or conflict between any requirement or standard in the documents listed above, the Contractor shall comply with the more onerous requirement or higher standard unless otherwise directed by the Superintendent.

17.3 (**No obstruction**) The Contractor must:

- (a) provide for the continuous operation of normal traffic along all roads, and pedestrian and vehicular access to properties included in the Contract or intersected by WUC;
- (b) where necessary, provide side-tracks which must be appropriately constructed, signposted, lit, and maintained; and
- (c) use all reasonable endeavours to avoid obstructing any side road, branch track, drain, or watercourse and to the extent that such obstructions cannot be avoided, remove such obstructions as soon as possible.

18. HEAVY VEHICLE NATIONAL LAW

- 18.1 (**Meaning of terms**) Terms used in this clause which are defined in the Heavy Vehicle National Law (Queensland) (the 'National Law') have the same meaning as in that law.
- 18.2 (**General obligations**) The Contractor must ensure, so far as is reasonably practicable, the safety of the Contractor's transport activities. Without limiting this, the Contractor must, so far as is reasonably practicable:
 - (a) eliminate public risks and, to the extent it is not reasonably practicable to eliminate public risks, minimise the public risks; and
 - (b) ensure the party's conduct does not directly or indirectly cause or encourage:
 - (i) the driver of the heavy vehicle to contravene the National Law; or
 - (ii) the driver of the heavy vehicle to exceed a speed limit applying to the driver; or
 - (iii) another person, including another party in the chain of responsibility, to contravene the National Law.

- 18.3 (**Notice**) The Contractor must immediately:
 - (a) notify the Superintendent if the Contractor considers that anything in this Contract, or any act or omission of the Principal or its respective officers, employees, agents or representatives, has or is likely to, directly or indirectly, cause or encourage the Contractor or any Personnel of the Contractor:
 - (i) being the driver of a heavy vehicle to contravene the National Law; or
 - (ii) being the driver of a heavy vehicle to exceed a speed limit applying to the driver;
 - (iii) being another person, including another party in the chain of responsibility, to contravene the National Law; and
 - (b) notify the Principal and the Superintendent in writing in the event that it, or any Personnel, is issued with any warning, request for information or production of documents, notice or fine in respect of any breach of chain of responsibility law in respect of WUC. The Contractor undertakes to provide the Principal and the Superintendent with a copy of any such warning, request, notice or fine, and any response or submissions made by it in relation to the same.
- 18.4 (**Chain of Responsibility**) In addition to its obligations under the chain of responsibility law, the Contractor must comply with the following chain of responsibility compliance assurance conditions, that:
 - (a) the Principal has a policy of compliance for its chain of responsibility obligations under the National Law. The Contractor agrees that it complies with its obligations under the chain of responsibility laws, and has a policy of training and compliance that is subject to periodic review and assessment. The Contractor will require its subcontractors and agents to comply with chain of responsibility obligations in any supply chain arrangement or any arrangement whatsoever in connection with WUC;
 - (b) the Principal is committed to taking all reasonable steps to ensure that any carriage of goods by road performed as part of WUC is performed safely and in accordance with the National Law and the chain of responsibility provisions it contains. The Principal will not comply with any instruction or requirement of the Contractor that might have the effect of contributing to a breach of the National Law, or preventing the Principal from taking all steps that it considers necessary to prevent any breach of the National Law;
 - (c) upon becoming aware of any breach of mass, dimension, load restraint, fatigue, speed, or maintenance requirement, the Principal may report the breach to the relevant Authority and retain records of the breach; and
 - (d) as a requirement of access to the Site, the Contractor must provide copies of any/all:
 - (i) chain of responsibility policy;
 - (ii) mass, dimension, or load restraint policy;
 - (iii) speed management policy;
 - (iv) fatigue management policy; and
 - (v) maintenance management policy,

that is in place in respect of its business.

19. LABOUR HIRE

The Contractor must not provide or utilise any labour for any WUC, unless the provider of that labour hire is registered under the *Labour Hire Licensing Act 2017* (Qld).

20. AS CONSTRUCTED DRAWINGS

- 20.1 (Requirements for as constructed drawings) Unless the Superintendent otherwise directs, as constructed drawings must:
 - (a) comply with AS 1100.101-1992: Technical Drawing General as amended or replaced from time to time:
 - (b) clearly detail the finished line, level, arrangements, layouts, and the like of The Works as completed, including the pickup of any existing in-ground services encountered in the execution of WUC:
 - (c) be prepared utilising the latest issued version of the construction drawings and must be prepared using AutoCAD format, or an alternative software package/format approved by the Superintendent; and
 - (d) must be clearly identified as 'as constructed drawings', be appropriately titled, and must be dated and signed by the Contractor.
- 20.2 (**Final as constructed drawings**) The Contractor must give to the Superintendent, as a requirement of Practical Completion, as constructed drawings of The Works as follows:
 - (a) 3 complete copies of as constructed drawings in A3 hardcopy format;
 - (b) 1 complete electronic copy of as constructed drawings in PDF; and
 - (c) 1 complete copy in the electronic format in which the drawings were created (native format).

21. PRACTICAL COMPLETION

- 21.1 (Requirements of achieving practical completion) The Contractor acknowledges that the Contract may elsewhere include additional obligations which must be satisfied as a requirement of Practical Completion. In addition to any such obligations, the Contract must, as a requirement of Practical Completion:
 - (a) satisfy all requirements of the Contract in relation to commissioning and operator training;
 - (b) provide to the Superintendent one (1) bound and one (1) PDF copy of an end-of-job report which shall contain the following as a minimum:
 - (i) material test results;
 - (ii) as constructed drawings which comply with clause 20;



TECHNICAL SPECIFICATION

Shepherdsons Road Rehabilitation 2024-2025

CONTRACT NO.: T2425.31

TABLE OF CONTENTS

TABLE OF CONTENTS

| Tab | le of Contents | 2 |
|-----|------------------------------------------------|----|
| TEC | CHNICAL SPECIFICATION | 3 |
| 1. | Introduction | 3 |
| 2. | Available Information | 3 |
| 3. | Scope of Works | 3 |
| 4. | Nature of Tender | 7 |
| 5. | lapsing of Offer | 7 |
| 6. | Term of Contract | 7 |
| 7. | Appointment of the Principal Contractor | 7 |
| 8. | Working Hours | 7 |
| 9. | Possession of site | 8 |
| 10. | Defects Liability Period | 8 |
| 11. | Bonds/Retentions | 8 |
| 12. | Pricing | 8 |
| 13. | Lodgement of Claims | 8 |
| 14. | Project Variations | 9 |
| 15. | Accuracy of Supplied Information | 9 |
| 16. | Local Industry Participation Reporting | 10 |
| 17. | Dimensions and Levels | 10 |
| 18. | Survey | 10 |
| 19. | Material, Plant & Equipment and Labour | 10 |
| 20. | Construction Specifications | 11 |
| 21. | Travel to and from Site | 11 |
| 22. | Mobilisation and Demobilisation | 11 |
| 23. | Existing Services | 11 |
| 24. | Temporary Services | 12 |
| 25. | Inspections, monitoring and Compliance Testing | 12 |
| 26. | Additional Works | 15 |
| 27. | Salvaged Materials | 15 |
| 28. | Community Liaison | 15 |
| 29. | Impact on Neighbouring Properties | 16 |

TECHNICAL SPECIFICATION

1. INTRODUCTION

Due to safety concerns regarding the current condition Shepherdsons Road, Banana Shire Council has undertaken a design to rehabilitate the road under the Local Roads and Community Infrastructure Program (LRCIP) funding.

Council is looking for a contractor to undertake the stabilisation and rehabilitation of Shepherdsons Road as per the Design, Specifications and Pricing Schedule supplied in Appendices of this document.

All work undertaken are to meet the requirements of the Capricorn Municipal Development Guidelines (CMDG).

2. AVAILABLE INFORMATION

The following information is available to help with your understanding of existing and intended scope of this project:

- Locality Map (Appendix A);
- IFC Drawings (Appendix B);
- Cultural Heritage Report (Appendix C) and
- Pricing Schedule (Appendix D).

The Contractor shall familiarise themselves as to the nature of the Site of the Works and of all matters and things relating to the Works, including but not limited to the nature of ground, slope stability, services and amenities, in ground services, condition of the sites, access to the sites and likely weather conditions.

3. SCOPE OF WORKS

The Works Under the Contract (WUC) are located within the boundaries of Banana Shire Council along Shepherdsons Road near Biloela as shown in the Locality Map Appendix A.

The scope of this project is for the construction works as per the following:

- CH1010 3770 Stabilisation and rehabilitation of the road inclusive of the construction of concrete floodways. The work is generally summarised below. Please refer to IFC drawings for specific details.
 - o Insitu stabilise 300mm of the subgrade with triple blend.
 - 300mm of subbase, reuse 300mm of existing pavement (top 300mm of suitable material inclusive of seal) as subbase. Top up with Type 2.3 Gravel material (TMR Spec.) as required.
 - o 150mm base with Type 2.1 Gravel material (TMR Spec.)
 - Replace existing floodways as concrete floodways in accordance with Drawing CMDG-R-094.
 - Double/Double Seal (1st Coat 16mm, 2nd Coat 10mm, Binder AMC 7) contractor provide seal design based on constructed conditions. Seal area through lanes, shoulders and batter (50mm below base)

More information regarding the scope of each of the projects is listed in the Appendices of this document.

The scope of the project may be increased or decreased due to budget requirements at any time. Council reserves the right to award any, all or none of the scheduled items in any combination.

The scope of works includes but is not limited to:

- It is noted the additive rate of 3% triple blend is nominal. The applicable additive rate
 with be advised by the Principal after undertaking laboratory testing. Testing will be
 conducted by the Principal and the additive rate confirmed before the commencement
 of construction.
- The following changes to the IFC drawings are noted. These are shown as markups in the drawing.
 - Subgrade triple blend stabilisation depth amended to 300mm. Nominal triple blend additive rate 3% with 40% Lime / 30% Cement / 30% Flyash. UCS 1-2 MPa.
 - o 300mm subbase layer to incorporate seal.
 - Seal Double/Double Seal (1st Coat 16mm, 2nd Coat 10mm, Binder AMC 7) contractor provide seal design based on constructed conditions. Seal area through lanes, shoulders and batter (50mm below base)
- Banana Shire Council Schedule 15 Aboriginal Cultural Heritage Identification Report attached. Report notes that area is cleared of cultural heritage aspects by the traditional owners of the land (Gangulu). However, it is the responsibility of the contractor to ensure all cultural heritage legislative requirements are met on site.
- Lots RP611619 and RP836483 are at adjacent to the works and are also on the EMR (Environmental Management Register). Stockpiling of gravel and spoil on these lots should be avoided. Please see aerial image below, these lots are highlighted with a white outline and shading.
- Two trees with nests have been identified at approximately Chainage 1660. A spotter/catcher must be engaged if these trees require to be removed during construction. The tree locations are marked on the aerial image below in pink.



- Establishment and disestablishment including cleaning up and making good, except to the extent that establishment and disestablishment are the subject of a separate specific work item in the Schedule of Rates
- Provision of all site facilities, except to the extent that the provision of any site facilities is the subject of a separate specific work item in the Schedule of Rates
- Provision of all labour, plant and equipment
- Provision of all supervisory and support staff
- Development, submission to Council for approval and Implementation of the following:
 - Construction Program (in a Critical Plath Network format)
 - o Quality Management Plan
 - Environmental Management Plan
 - Erosion and Sediment Control Plan
 - Workplace Health and Safety Plan
 - Traffic Management Plan (if required)
- All costs associated with the operation of the Contractor's Workplace Health and Safety obligations, Quality System, Environmental Management obligations, Traffic Management obligations, Community Liaison obligations, Public Utility Plant obligations, works programming, road maintenance obligations and all other supervisory and coordination functions, except to the extent that such obligations and functions are the subject of separate specific work items in the Schedule of Rates.
- The identification and creation of suitable stockpile/park-up locations for each site
 with approval for each site to be obtained from Council be commencing use. The
 contractor will be responsible (at no cost to Council) for obtaining any approvals
 required for the use of these locations, the implementation of any conditions of use
 listed on these approvals and the tidying/re-establishment of the sites to pre-use or
 better condition.
- Purchase and delivery of gravel (all gravel is to be manufactured and compliant with relevant Department of Transport and Main Roads standard)
- Supply, delivery and installation of Geosynthetics as per the requirements of the design for each site
- Supply, delivery and storage of stabilising agent and lime as per the safety requirements of each.
- Purchase and delivery of concrete (Concrete is to meet the standards required
 of the design and the relevant CMDG standard).

- Any setout survey required for construction using the Council supplied electronic design files
- Survey of works completed (eg. Before and after surveys to show excavation and embankment quantities and to confirm levels of each gravel layer)
- Supply of As Constructed survey of the site
- Tidy up of site.
- Obtain all necessary approvals for water extraction (if required). The approval requires completion of paperwork for water extraction records.
- Maintenance of haul roads, including the use of unsealed roads for the Project, used during construction to maintain a safe road condition and minimise dust. The maintenance may include water carts, grading and rolling to ensure the road is in no worse condition following completion of works than before commencement.
- All costs associated with compliance testing requirements as per the requirements of CMDG and/or DTMR and the Appendices of this document.
- Regular communication with the Council and its Superintendent throughout the Project
- All costs incurred by the Contractor in complying with Commonwealth and State legislation and Local Government By-laws
- All costs associated with the work with respect to security, interest, fees, charges, taxes, royalties, insurance and compensation.
- Cooperation and coordination, using "best for project" mindset.
- Provision of a weekly progress report, to be sent to the Superintendent every Friday.
 The information shall include progress from the previous weeks' works (including photographs), planned works for the next week, any issues affecting the contract delivery, adjusted monthly expenditure, safety statistics, audits (e.g., safety/environmental).
- Provision of Inspection Testing Plans (ITPs)/Lot Sheets for all the completed works.
- Provision of the Handover Data at Practical Completion which includes asconstructed drawings, test results, photos, the register for the completed works etc.
- All overheads and profit, and
- All other expenses associated with the work not specifically listed above.

Tenderers are to note that Council, may at its sole and unfettered discretion, amend/modify the scope of works at any time during the contract.

If the scope of works is amended/modified, the Contractor is not entitled to any compensation.

4. NATURE OF TENDER

This tender is to be considered a Lump Sum Contract under AS4000 – 1997. The submitted price shall be based on a Pricing Schedule (included in Appendix D of this document) and payment shall be made on the basis of:

- a unit rate for those Works Items which have a stated unit of measurement and a stated quantity; or
- a lump sum for those Works Items which do not have a stated unit of measurement and a stated quantity.

Unless stated otherwise in this Document, the Tender shall be for the whole of the Works specified in the Tender Documents and Notices to Contractor (if any) with all rates submitted fixed for the life of the contract.

5. LAPSING OF OFFER

Offers submitted under this tender shall remain valid for a period of three (3) months after the closing time and date and may be accepted by Council at any time before the expiry of that period unless otherwise notified, in writing, by Council.

6. TERM OF CONTRACT

The initial term of this Contract shall begin on the issuing of the Letter of Acceptance by Council.

All works related to this contract are to be completed **no later than 120 days after this date**.

If the Contractors business is sold or transferred to another entity the submission cannot be transferred and will be null and void.

7. APPOINTMENT OF THE PRINCIPAL CONTRACTOR

Upon the Date of the Letter of Acceptance of Tender:

- Council is deemed to have appointed the Contractor to be the Principal Contractor and the Contractor is deemed to have accepted the appointment.
- The Contractor, in respect of the work to be executed under the Contract, becomes responsible for the performance of the Principal Contractor's functions under the Act and under the Regulations and compliance standards in force under the Act.
- The Contractor's appointment as Principal Contractor must continue until the Contractor completes all of the work under the Contract unless sooner revoked by Council giving twenty one (21) days' notice in writing to the Contractor of its revocation or by Council taking over or terminating the Contract pursuant to any provision of the Contract or according to law.

8. Working Hours

Allowable working hours for the contract shall be restricted to 6am to 6pm Monday to Friday and 7am to 4pm Saturday (excluding Public Holidays and the Christmas period 22 December 2025 to 10 January 2025). Works outside of these hours cannot be undertaken without approved from the Principal.

9. Possession of site

Possession of site is to be granted within 10 business days of acceptance of tender. Prior to being given possession of site by Council the Contractor must:

- a) Provide proof of all required insurances
- b) Submit and have approved by Council all Project Management Plans and the project schedule.

10. DEFECTS LIABILITY PERIOD

A Defects Liability Period of **twelve (12) months** will apply for all works completed under this contract.

11. BONDS/RETENTIONS

The following bond and retention requirements will be enforced as part of this project:

Bond – a bond to the amount of 10% of the total project cost, in the form of a minimum 2 non-expiring bank guarantees (5% each), is to be submitted to Council ten (10) days before the issuing of Possession of Site. One guarantee will be returned on the issuing of practical completion (after the completion of a Project Completion inspection and the submission of all project documentation) with the remaining guarantee to be held by Council until the successful end of the Defects Liability Period

OR

• Retention – Alternatively a retention amount of 10% can be removed from each claim until the maximum 5% of each project is reached. This money will be held by Council for the Defect Liability Period and the Contractor can claim for each project on the successful completion of the Defects Liability Period for each.

12. PRICING

All prices are to be quoted as GST excl. and cover all costs associated with the performance of the service. **Prices are to be fixed and guaranteed for the duration of the contract**.

13. LODGEMENT OF CLAIMS

Progress Claims are to be submitted by the Contractor each month. A further two (2) progress claims can be made during the project at the following times if required:

- Once upon the issue of the certificate of Practical Completion; and
- Once upon the issue of Final Certification

Progress claims are to be made via the following process:

- A spreadsheet listing the quantity of works completed for the month along with the associated quality records (including supporting documentation for the quantities listed) is to be submitted to Council no later than the 21st of each month
- Council will then assess this information

- Council will forward a request for an invoice to be submitted for the approved claim amount by the Contractor
- Payment of the invoice will be made through Council's payment procedures on receipt of the invoice

All progress claim amounts/quantities (including any variations) are subject to approval by Council before payment is agreed.

Banana Shire Council will not have any obligation to pay the respondent for Goods until the Authorised Officer has been given a correctly rendered invoice.

A correctly rendered invoice must:

- Specify details of order in sufficient detail to enable Authorised Officer to assess;
 and
- Specify BSC Order number and Tender number; and
- Specify the respondent's Invoice number and Invoice date; and
- Specify the Contract Price payable by BSC and particulars of any GST payable in respect of the Contract Price; and
- Otherwise comply with the requirements of a Tax Invoice for the purposes of the GST Act.

14. PROJECT VARIATIONS

Council may, by written notice given to the Contractor, require the Contractor to vary the Works in nature, scope (extent and quantity) or timing.

The Contractor may be directed to:

- Increase, decrease or omit any part of the Works and / or
- Perform additional work.

Where the contractor is given a direction to vary the work under the contract which is not expressly identified in writing as a variation, the contractor must promptly, and where practicable before complying with the direction, give the Council Representative a written notice which identifies the direction and states that the contractor considers that the direction involves a variation. The approved variation number should be noted on the Invoice and be itemised.

All project variations must be approved by Council before a claim can be made. The Contractor is to include a breakdown of the proposed cost of any variation (based on the day labour rates submitted as part of this tender) as part of any variation submission.

15. ACCURACY OF SUPPLIED INFORMATION

For a Work Item, listed in the Pricing Schedule Appendix E, as Provisional quantity and/or Provisional Item, no limits of accuracy are specified.

For all other Work Items, the limits of accuracy shall be plus 10% or minus 10% unless otherwise approved by Council.

16. LOCAL INDUSTRY PARTICIPATION REPORTING

The contractor must provide a report to accompany each payment claim, which must describe the local industry participation achieved since the previous payment claims, and the cumulative totals to date. The minimum information to be included must be:

- Name of the Local Suppliers / Contractors;
- Contact details for Suppliers/ Contractors (Name and telephonic contact will suffice);
- Nature of work completed by specific supplier/contractor;
- Value of Work Completed / Services Provided; and
- Estimated Labour hours completed (where applicable).

17. DIMENSIONS AND LEVELS

The Contractor must not rely on dimensions and levels provided by the Principal and must obtain or check all measurements before commencing the Works. The Contractor shall verify details of existing work before modifying it. Any discrepancies must be reported to the Superintendent immediately.

Specific (spot) levels shown on drawings take precedence over contour lines and ground profile lines.

18. SURVEY

Standard AHD and Geocentric Datum of Australia (GDA94) is the basis of all levels and coordinates associated with the Works unless stated otherwise.

The contractor is responsible for setting out of the Works from the design or project scopes and a qualified Surveyor is to be engaged to undertake the set out (if applicable).

A qualified surveyor is also required to conform design conformance at each level of construction.

19. MATERIAL, PLANT & EQUIPMENT AND LABOUR

All materials used in the works under contract (WUC) are to be the best of their respective kinds and in accordance with the current specifications of the Standards Association of Australia for those particular materials where such specifications are applicable and do not otherwise conflict with an express requirement of this Contract. If there is no relevant Australian Standard, the British Standard Specification if any, will apply.

The Superintendent may require samples of any or all materials to be submitted for its approval before their use. Whether the Superintendent has called for samples or not, all materials used in the WUC are subject to the Superintendent's written approval: -

- a) the Contractor may request the Superintendent to direct that alternative materials or equipment be substituted; and
- b) the Superintendent may, if the Superintendent is of the opinion that the characteristics of type, quality, appearance, finish, method of construction and/or performance are not

less than is required by the Contract, direct a variation for the convenience of the Contractor allowing the substitution.

The Contractor shall provide all materials, plant, personnel and other items of work necessary for the proper completion of WUC or the compliance by the Contractor with any of its other obligations under the Contract, (including items which are not expressly mentioned in the Contract but which are obviously and indispensably necessary for the proper completion of such work or the compliance of the Contractor with its other obligations under the Contract);

All plant and equipment shall be appropriately licenced/registered and worthy for use in accordance with current legislative requirements and manufacturer's specifications.

All work shall be carried out by suitably qualified persons having experience in the particular types of work to be executed.

20. CONSTRUCTION SPECIFICATIONS

Where there is no specific reference made to a works specification the Capricorn Municipal Development Guidelines (CMDG) Standard Specifications apply. Copies of CMDG Specifications are not included in this document.

Should an item not be covered within the CMDG, Department of Transport and Main Roads standards and specifications will apply. These standards/specifications are not invluded in this document.

21. TRAVEL TO AND FROM SITE

The Contractor is responsible for any costs related to daily travel to and from the site including vehicle, plant, fuel, maintenance, accommodation and any other costs.

22. MOBILISATION AND DEMOBILISATION

The Contractor shall include the following during the site establishment: -

- Sanitary facilities, shelters, storage facilities which are required for the Contractor's establishment on the Site and execution of the work under the Contract;
- Provision of all services for construction purposes as required:
- Maintenance and security of site facilities; and
- Mobilisation and demobilisation of all site facilities.

The Contractor shall be responsible for the security of the Contractor's Work Area and of construction plant and materials. Work sites shall be free from rubbish, waste materials and refuse of any description at all times. Disestablishment shall include removal of all surplus materials, rubbish, waste materials and refuse of any description from the work site and from all construction or storage areas.

23. EXISTING SERVICES

The Contractor is to undertake "Dial Before You Dig" (DBYD) for all operations.

The Contractor shall make enquires to all authorities to determine the locations of services and shall exercise care in not disturbing these services during the execution of the works.

The location and size of services shown on the drawings should be considered approximate only. Confirmation shall be made on site with the assistance of authorities where possible.

The Contractor shall be responsible for the rectification of any services damaged or interfered with on the Work Site or during activities directly associated with the Works during the course of the Works. Rectification shall include details such as bedding and overlays of granular materials.

Should conflicts occur with services, the Contractor shall arrange to divert or relocate as required by the Superintendent.

Should conflicts occur with service mains, the Contractor shall notify the Superintendent promptly in writing and shall arrange to have the service relocated/diverted by the appropriate authority.

24. TEMPORARY SERVICES

The Contractor shall provide and maintain temporary services necessary for the execution of the work under the Contract, install such services in accordance with the requirements of the relevant authorities and pay charges in connection with the installation and use of such services. Unless there is a specific reference to the provision of temporary services in the contract scope of works, the cost of providing temporary services shall be considered as being included in the cost of the scope of works, unless otherwise agreed in writing by the Superintendent.

Such services shall be made available to Sub-contractors. On completion, the Contractor shall disconnect temporary services and clear away all traces.

Temporary Services includes detours and side-tracks etc.

25. INSPECTIONS, MONITORING AND COMPLIANCE TESTING

The Contractor shall be responsible for the quality of all products and services supplied under the Contract, and provide all necessary facilities and resources to perform the inspection and tests required to achieve the specified quality.

The Contractor's Quality Assurance System (QAS) shall clearly identify and details the contract requirements for inspections, monitoring and compliance testing.

Prior to the commencement of any services/works, the Contractor shall prepare and submit to the Superintendent or Superintendent's Representation for approval, an Inspection Test Plan (ITP) prepared in accordance the requirements of the tender specification and the requirements of the CDMG and/or DTMR specifications.

The Contractor shall, for the duration of the Contract carry out inspections, monitoring and testing in accordance with the approved ITP, Quality Assurance System and the technical specification.

Inspections

When the Contractor is required to give notice to the Superintendent for inspections in accordance with the specification, the Contractor should arrange to have a representative freely available for consultation during the inspection. The Contractor should also supply all equipment and labour requested by the Superintendent to check any dimensions, levels, bearings or build quality relating to the works.

The Contractor shall be liable for any costs relating to additional inspections required as a result of the Contractor not being ready.

Inspections are to be timed to minimise the number of times that the Superintendent is required to travel to site.

Random audit type inspections of the works may be undertaken by the Superintendent at any time.

Hold Points

A Hold Point is defined as a position in the progress of the Contractor's Activities, beyond which further work shall not proceed without mandatory verification by the Contractors Quality Assurance Representative (QAR) and the Superintendent. If the Contractor proceeds beyond this point without the Hold Point's being observed, the Superintendent may direct the Contractor to halt the work and to remove any materials from the Site.

Mandatory Hold Points shall apply prior to commencement of designated work lots or work items. Mandatory Hold Points shall be verified by the Superintendent. The Contractor's Quality System shall include at least the following Hold Points. Those marked "Mandatory" shall be Mandatory Hold Points.

| Gravel Supply | MANDATORY HOLD POINT |
|--------------------------------------|----------------------|
| Gravel Placement/Compaction/Trimming | MANDATORY HOLD POINT |
| Pre-seal inspection | MANDATORY HOLD POINT |
| Formwork/Pre-Pour Inspection | MANDATORY HOLD POINT |
| Concrete Supply | MANDATORY HOLD POINT |
| | |

The Superintendent may direct the Contractor to insert additional Hold Points (including Mandatory Hold Points) in the Contractor's Inspection and Test Plans. The Superintendent may direct that any Mandatory Hold Point indicated in the Contractor's Inspection and Test Plans shall not be a Mandatory Hold Point.

Witness Points

A Witness Point is defined as a position in the progress of the Contractor's Activities, where the Contractor must notify it's QA Officer and the Superintendent prior to proceeding and the option for attendance for witnessing of inspection and test may be exercised. If any do not attend, then work may nevertheless proceed, unless otherwise instructed.

Proceeding beyond a Hold Point or Witness Point

The Contractor shall give the Superintendent not less than two (2) working days' notice of its intention to proceed beyond a Hold Point.

The Contractor shall give the Superintendent not less than one (1) working days' notice of its intention to proceed beyond a Witness Point.

The Contractor shall ensure that all work lots or work items affected by the lot or item in question are conforming; and that all Conformance Reports for all work lots or work items affected by the lot or item in question have been made available to the Superintendent at least 6 working hours prior to the time the Contractor intends to proceed with the lot or item in question, thus ensuring that defective work are not built-in.

Test results shall be provided with the monthly report. Processing of monthly progress payments by the Principal may be delayed if monthly reporting information is not provided by the Contractor.

In the event of any non-conformance to the requirements of the Specification, the Contractor shall immediately advise the Superintendent the details of such non-conformance, including location in the Works, and the proposed remedial actions.

Compliance Testing

Compliance testing shall be carried out for each lot or item. The Contractor shall perform all compliance and testing in accordance with the minimum testing requirements to ensure that the works comply with the standards and requirements of the Contract.

Compliance testing shall be at the Contractor's expense and deemed to be included in the Contract Sum.

The Superintendent will have the right to be present at, or have a representative present at all tests, at the time of taking of samples and specimens and at the time of preparation of material for testing. The Superintendent may reject the results of tests carried out without reasonable notice to him and may direct that such tests will be repeated at the Contractor's expense.

The Contractor shall give sufficient notice to the Superintendent to enable any materials or workmanship to be examined prior to incorporation into the finalised Works and must give sufficient notice to the Superintendent to enable sighting of any test results required by the contract or ordering of any test results prior to incorporation of materials or workmanship into the finalised Works.

Tests undertaken throughout the duration of the Contract must be submitted to the Superintendent not more than two (2) Business Days following the date of testing. In the event that test results indicate non-compliance with quality targets, notification of non-compliances is to be notified to the Superintendent within not more than 24 hours of the time of the test.

The Contractor shall prepare and submit all necessary documentation and records as verification that installation, testing and commissioning has been successfully completed.

The Contractor is to provide, free of charge, any materials, labour, compressed air and equipment that may be necessary to carry out all testing required.

In addition to any test result provided during the month, all test results shall be provided and presented in an orderly and organised manner with the Contractor's monthly report. Processing of monthly progress payments by the Principal may be delayed if monthly reporting information is not provided by the Contractor or provided in an unsatisfactory manner.

In the event of any non-conformance to the requirements of the Specification, the Contractor shall make available to the Superintendent, a Non-Conformance Report (NCR) that details the non-conformance, including location in the works, and the proposed remedial actions. If any portion of the work fails to reach the specified testing requirements, that portion of the works so affected will be re-tested after rectification by the Contractor at the Contractor's expense.

A NATA-registered laboratory certified for the tests specified shall be engaged to undertake all compliance testing.

The location of each density test shall be chosen by a method of random stratified sampling and the relative compaction shall be determined by Test Method. Reporting and correction for

oversize material is mandatory as part of the test. The density index of non-cohesive materials shall be determined using Test Methods in accordance with AS1289.

In circumstances where the Superintendent requests additional tests in excess of the approved testing schedule/plan and where the results of the tests comply with the requirements of the Specification, the Contractor may request The Principal to reimburse the costs of the tests. The Contractor must provide evidence of the testing costs. The Principal shall not be responsible for costs relating to test results that do not meet the requirements of the Specification.

26. ADDITIONAL WORKS

Should during the course of the inspection of sites (for the generation of a seal design) of during construction the Contractor identify complementary works outside the scope of the project they believe would be beneficial to Council, the contractor is to advise the Superintendent of these observations. Contractors must provide an offer for the complementary scope as detailed on the Pricing Worksheet. Council will evaluate the offers for the complementary scope and determine if any will be included in the contract scope for award.

Council reserves the right to accept or reject any tender offer for complementary/betterment scope.

27. SALVAGED MATERIALS

Unless otherwise stated, all materials, plant equipment, fixtures and other items salvaged from the Site of the Works shall be the property of the Principal and shall not be removed from the site without the prior approval of the Superintendent. The Superintendent is to be immediately consulted when any find is made that is considered of relevant heritage value.

The Contractor is to obtain written approval from the Superintendent prior to removal from site of any material or material which is or may be suitable for use as fill on the site.

Material which is unsuitable for re-use should be transported and dumped in an approved dump area.

Approval for dumping of materials, not otherwise designated, should be obtained from the Superintendent.

Council operates a spoil permit system where residents can request approval to access spoil material. Disposal of spoil material to local residents is as by written direction and approval of the Superintendent. In these circumstances, The Contractor must be a willing participant in assisting with the management of this system.

28. COMMUNITY LIAISON

The Contractor must make available a 24 hour contact number to respond to all community queries, concerns, issues or the like during the construction period. These contact details must be provided to Banana Shire Council (a customer services and after hours telephone number shall be provided at site handover) at the commencement of works as well as being displayed prominently on site and at the Contractor's site office.

The Contractor must appoint a representative to act as the primary contact for all enquiries during the construction period.

All costs incurred by the Contractor for liaison with the community are deemed to be included within other items of the schedule.

Notifications of the commencement date, scope and duration of the works will be sent out by Council before the commencement of construction based on the information supplied by the successful Contractor.

29. IMPACT ON NEIGHBOURING PROPERTIES


In performing the work under the Contract, the Contractor must not enter or permit its constructional plant and equipment (including that of any subcontractor) to enter land adjoining the Project Site without first obtaining the written approval of the land occupier and the landowner (where these are not the same person/company).

The Contractor must submit a copy of this written approval to Council's Representative upon request. The Contractor must, by the action of the entering on to the neighbouring land, be deemed to have indemnified Council against any claims which may arise from such entry or subsequent operations on the land. Upon completion of work on neighbouring land, the Contractor must forward to Council's Representative a statement signed by the landowner and occupier to the effect that the landowner and occupier are satisfied that any damage to the land which may have arisen from the Contractor's operations has been adequately repaired or otherwise compensated by the Contractor. All costs associated with work on private land must be borne by the Contractor.

This clause also applies to any property that may be impacted on by the works (if not neighbouring to the Project Site) and includes properties along the haulage route or routes that the construction work vehicles travel along during the works.

APPENDICES

- A. LOCALITY MAP
- **B. IFC DRAWINGS**
- C. CULTURAL HERITAGE REPORT
- D. PRICING SCHEDULE

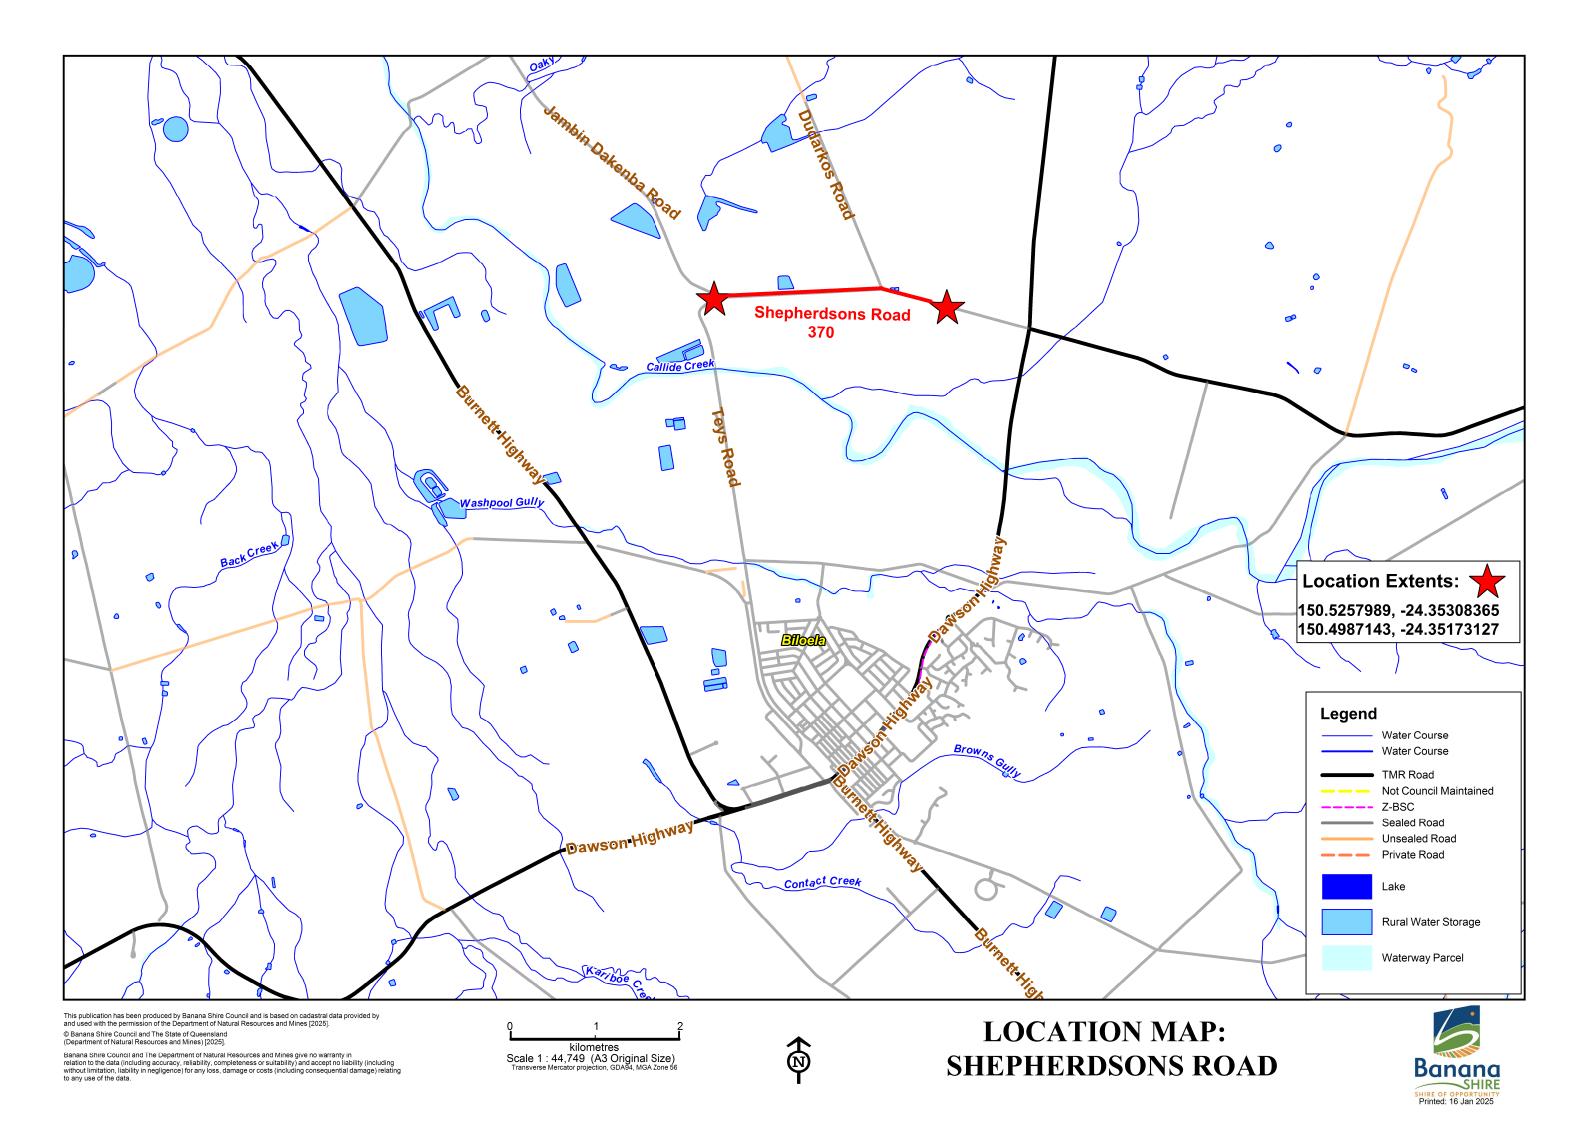



NO WORK IS SO IMPORTANT THAT IT CANNOT BE DONE SAFELY

PAVEMENT REHABILITATION, RESEAL & DRAINAGE WORKS SHAPHERDSONS ROAD, BILOELA QLD 4715



| | | NDEX OF DRAWINGS |
|------------------|----------|------------------------------------------------------|
| DRAWING NO. | SHEET | DRAWING DESCRIPTION |
| PRJ-0342-01-GN01 | 01 OF 19 | LOCALITY PLAN AND SCHEDULE OF DRAWINGS |
| PRJ-0342-01-GN02 | 02 OF 19 | GENERAL NOTES AND LEGEND |
| PRJ-0342-01-GN03 | 03 OF 19 | SITE PLAN |
| PRJ-0342-01-ES01 | 04 OF 19 | CONCEPT EROSION & SEDIMENT CONTROL NOTES AND DETAILS |
| PRJ-0342-01-RC01 | 05 OF 19 | ROADWORKS & SURVEY CONTROL SETOUT PLAN |
| PRJ-0342-01-RT01 | 06 OF 19 | ROADWORKS TYPICAL SECTIONS |
| PRJ-0342-01-RT02 | 07 OF 19 | ROADWORKS TYPICAL DETAILS |
| PRJ-0342-01-RI01 | 08 OF 19 | ROADWORKS INTERSECTION DETAILS |
| PRJ-0342-01-RL01 | 09 OF 19 | ROADWORKS LINEMARKING AND SIGNAGE PLAN |
| PRJ-0342-01-RS01 | 10 OF 19 | ROADWORKS LONGITUDINAL SECTIONS - SHEET 01 |
| PRJ-0342-01-RS02 | 11 OF 19 | ROADWORKS LONGITUDINAL SECTIONS - SHEET 02 |
| PRJ-0342-01-RS03 | 12 OF 19 | ROADWORKS LONGITUDINAL SECTIONS - SHEET 03 |
| PRJ-0342-01-RS04 | 13 OF 19 | ROADWORKS LONGITUDINAL SECTIONS - SHEET 04 |
| PRJ-0342-01-RS05 | 14 OF 19 | ROADWORKS CROSS SECTIONS - SHEET 01 |
| PRJ-0342-01-RS06 | 15 OF 19 | ROADWORKS CROSS SECTIONS - SHEET 02 |
| PRJ-0342-01-RS07 | 16 OF 19 | ROADWORKS CROSS SECTIONS - SHEET 03 |
| PRJ-0342-01-RS08 | 17 OF 19 | ROADWORKS CROSS SECTIONS - SHEET 04 |
| PRJ-0342-01-RS09 | 18 OF 19 | ROADWORKS CROSS SECTIONS - SHEET 05 |
| PRJ-0342-01-RS10 | 19 OF 19 | ROADWORKS CROSS SECTIONS - SHEET 06 |

| | | | = |
|-----|--------------|----------|----------|
| | | | |
| A | FOR APPROVAL | 05.08.24 | \dashv |
| No. | Revision | Date | |

| | ABN 27 158 351 663 PH: 1300 220 195 | M |
|---|----------------------------------------|---|
| | EMAIL: admin@hartecs.com.au | ı |
| ı | OFFICE: ROCKHAMPTON | L |

| anana Shire Council | a/WtW - Banana Shire Council | DIS Review - Banana St |
|---------------------|------------------------------|----------------------------|
| n: NTHA WILSON | Designed: CHASE KEMP | Certified: CHARLES COOK |
| | | RPEQ #: 8480 |



| PAVEMENT REHABILITATION, RESEAL & DRAINAGE WORKS |
|----------------------------------------------------|
| SHEPHERDSONS RD, BILOELA, QLD 4715 (REF: VP381329) |
| LOCALITY PLAN AND SCHEDULE OF DRAWINGS |

| Dwg. No. | Sheet | |
|------------------|-------|----|
| PRJ-0342-01-GN01 | 01 OF | 19 |

| 1-GN01 | 01 | 0F | 19 | A |
|--------|----|----|----|---|
| | | | | |

IMPORTANT NOTICE

- ALL WORKS SHALL BE CARRIED OUT IN ACCORDANCE WITH RELEVANT COUNCIL SPECIFICATIONS AND STANDARD DRAWINGS UNLESS DIRECTED OTHERWISE
- THE CONTRACTOR MUST AT ALL TIMES ADOPT 'SAFE' WORK PRACTICES, CONSTRUCTION TECHNIQUES & MUST ENSURE THAT THE SITE IS ALWAYS MANAGED IN A MANNER THAT ENSURES THE SAFETY & WELL BEING OF PROPERTY ENVIRONMENT & PERSONNEL AND OTHERS ENTERING THE SITE & ADJACENT TO THE SITE. A 'ZERO HARM' POLICY IS REQUIRED TO BE ENFORCED AT ALL TIMES.
- HARTECS GROUP ACCEPTS NO RESPONSIBILITY WHATSOEVER FOR ANY LOSS OR DAMAGE SUFFERED HOWSOEVER ARISING TO ANY PERSON OR CORPORATION WHO MAY RELY ON OR USE THESE DRAWINGS IN CONTRAVENTION OF THE TERMS OF ANY NOTES SHOWN ON THIS SET OF DRAWINGS.
- THESE NOTES FORM AN INTEGRAL PART OF THIS SET OF DRAWINGS.
- SAFETY IN DESIGN INFORMATION. THE CONTRACTOR IS ADVISED THAT THERE MAY BE ADDITIONAL HAZARDS/RISKS NOT NORMALLY ASSOCIATED OR INFERRED WITH THE TYPE OF WORKS DETAILED ON THESE DRAWINGS

EXISTING LEVELS AND SERVICES

- ES.1. NO WORK IS TO BE STARTED WITHIN 3m OF EXISTING SERVICES PRIOR TO NOTIFYING THE RELEVANT SERVICE AUTHORITY. DETAILS OF EXISTING SERVICES INCLUDING LOCATIONS POSITION AND LEVEL THAT HAVE ALREADY BEEN DETERMINED ARE SHOWN ON THE DRAWINGS. PRIOR TO COMMENCING CONSTRUCTION WORKS THE CONTRACTOR SHALL OBTAIN THE NECESSARY SERVICE DETAILS FROM 'DIAL BEFORE YOU DIG' AND THE SERVICE AUTHORITY FOR ALL SERVICES SHOWN ON THE DRAWINGS AND ANY OTHERS STILL TO BE LOCATED ANY WORKS WITHIN THE VICINITY OF EXISTING SERVICES INCLUDING ANY REQUIREMENTS FOR PROTECTION WORKS TO THE SERVICES SHALL BE CARRIED OUT IN ACCORDANCE WITH THE DETAILS SHOWN ON THE DRAWINGS AND AS DIRECTED BY THE SERVICE AUTHORITY.
- THE CONTRACTOR MUST VERIFY THAT THE EXISTING LEVELS AT POINTS WHERE CONNECTIONS TO EXISTING INFRASTRUCTURE ARE REQUIRED ARE AS PER THIS DESIGN. ANY DIFFERENCES TO BE NOTIFIED TO THE COUNCIL TO ORDERING MATERIALS OR COMMENCING ANY
- PRIOR TO COMMENCING WORKS THE CONTRACTOR MUST VERIFY LOCATION AND DETAILS OF ALL EXISTING SERVICES,

ENVIRONMENTAL MANAGEMENT

- THE CONTRACTOR IS DEEMED TO BE FAMILIAR WITH THE CURRENT ENVIRONMENTAL LAWS AND HIS LEGAL RESPONSIBILITIES AND LIABILITIES UNDER THE LAWS.
- THE CONTRACTOR IS DEEMED TO BE RESPONSIBLE FOR THE ENVIRONMENTAL MANAGEMENT OF THE SITE FOR THE DURATION OF THE CONTRACT AND IS RESPONSIBLE FOR ANY BREACHES TO THE LAWS.
- THE CONTRACTOR MUST HAVE AND MAINTAIN IN FORCE AN ENVIRONMENTAL MANAGEMENT PLAN FOR THE DURATION OF THE CONTRACT WHICH SHALL INCORPORATE BUT NOT BE LIMITED TO ANY SEDIMENT AND EROSION CONTROL REQUIREMENTS INCLUDED IN THE CONTRACT DOCUMENTATION.
- ENVIRONMENTAL LAW REQUIRES THE CONTRACTOR TO EXERCISE DUE DILIGENCE IN PREVENTING THE OPERATIONS OF HIS PERSONEL AND OTHERS WHO ENTER THE SITE WITH OR WITHOUT HIS PERMISSION FROM BREACHING ENVIRONMENTAL LAWS
- ANY BREACH TO THE LAWS MUST BE REPORTED TO THE APPROPRIATE AUTHORITIES AS SOON AS POSSIBLE.

STANDARD DRAWINGS

UNLESS NOTED OTHERWISE REFERENCES TO STANDARD DRAWINGS "STD DWG" ARE CMDG AND AUSTROADS STD DWGS.

ROADWORKS

- RW.1. ALL ROADWORK SETOUT AND LEVELS MUST BE CONFIRMED ON SITE PRIOR TO COMMENCING ANY CONSTRUCTION.
- CONTRACTOR IS RESPONSIBLE FOR THE LOCATION AND PROTECTION OF ALL UNDERGROUND SERVICES PRIOR TO COMMENCEMENT OF WORKS.
- EXISTING SIGNAGE AND GUIDE POSTS MAY NOT HAVE BEEN SURVEYED. ALL AFFECTED SIGNAGE TO BE RELOCATED TO SUIT NEW ROADWORKS AS APPROVED BY ADMINISTRATOR.
- THE CONTRACTOR IS TO SELECT APPROPRIATE CONSTRUCTION TECHNIQUES AND COMPACTION EQUIPMENT IN THE VICINITY OF UNDERGROUND PIPES & SERVICES TO ENSURE NO DAMAGE OR DEFORMATION OF THE UNDERGROUND SERVICE.

EARTHWORKS

- THESE DRAWINGS SHOULD BE READ IN CONJUNCTION WITH SPECIFICATIONS AND AS3798 'GUIDELINES ON EARTHWORKS FOR COMMERCIAL AND RESIDENTIAL DEVELOPMENTS.
- EW.2. EARTHWORKS SHOULD AVOID THE FROSION OR SILTATION OF ADIDINING LANDS STORMWATER SYSTEMS OR WATERCOURSES. REFER CONCEPT EROSION AND SEDIMENT CONTROL NOTES (ESO1). ALL EROSION AND SEDIMENT CONTROLS TO BE INSTALLED AND FULLY OPERATIONAL PRIOR TO COMMENCEMENT OF EARTHWORKS.
- EW.3. ALL EARTHWORKS ACTIVITIES INCLUDING STRIPPING, EXCAVATION, FILLING, COMPACTION AND

- TESTING, IS TO BE UNDERTAKEN IN ACCORDANCE WITH MRTSQ4, THE DRAWINGS, SPECIFICATIONS, CURRENT RELEVANT AUSTRALIAN STANDARDS, OTHER STATUTORY REQUIREMENTS AND TO THE SATISFACTION OF THE LOCAL AUTHORITY AND THE ENGINEER.
- EARTHWORKS QUANTITIES HAVE BEEN CALCULATED BETWEEN THE STRIPPED NATURAL SURFACE AND THE FINISHED SUBGRADE LEVELS. EXCESS SPOIL TO BE TRANSPORTED TO A LOCATION CONFIRMED BY COUNCIL.
- EW.4.1. ROAD EMBANKMENTS SHALL ACHIEVE THE FOLLOWING MINIMUM STANDARDS.
- EW.4.1.1. GREATER THAN OR EQUAL TO 0.3m BELOW PAVEMENT SUBGRADE: 95% STD. M.D.D.R.
- EW.4.1.2. LESS THAN 0.3m BELOW PAVEMENT SUBGRADE: 100% STD. M.D.D.R.
- EW.4.1.3. NON COHESIVE MATERIALS:- FILL SHALL ACHIEVE A MINIMUM DENSITY INDEX RATIO OF 75%
- EW.5. GEOTECHNICAL CERTIFICATION SHALL BE 'LEVEL 1' AS PER AS. 3798.

TOPSOIL:

- EW.6. PRIOR TO ANY EARTHWORKS ACTIVITIES, TREE STUMPS, BUILDING DEBRIS, ORGANIC RICH TOPSOIL AND SEVERELY ROOT AFFECTED AREAS MUST BE REMOVED.
- ORGANIC RICH TOPSOIL MUST NOT BE USED IN FILL. IT SHALL BE STOCKPILED FOR RE-USE IN LANDSCAPING OR DISPOSED OF. TOPSOIL STOCKPILES SHALL NOT EXCEED 2.0m IN HEIGHT.

- EW.8. CONTRACTOR TO ENSURE STOCKPILES ARE NOT LOCATED IN A POSITION WHERE THEY COULD BE WASHED INTO A GUTTER DRAIN OR WATER BODY, SUCH AS:
- FW.8.1 ON A ROAD PAVEMENT.
- EW.8.2. WITHIN AN OVERLAND FLOW PATH-
- EW.8.3. ADJACENT TO WATER COURSES.
- EW.9. CONTRACTOR TO ENSURE STOCKPILES ARE COVERED WITH A TARP OR OTHER IMPERVIOUS COVER. LONG TERM STOCKPILES CAN BE COVERED WITH MULCH OR TEMPORARY VEGETATION
- EW.10. CONTRACTOR TO ENSURE APPROPRIATE DUST CONTROL MEASURES EXIST FOR ALL STOCKPILES AND APPROPRIATE SEDIMENT CONTROLS ARE LOCATED DOWN-SLOPE OF ALL

ACID SULPHATE SOILS

- EW.11. ACID SULPHATE SOILS ARE PREDOMINANTLY FOUND IN COASTAL AREAS WHERE THE ELEVATION IS LESS THAN 5.0m ABOVE SEA LEVEL
- EW.12. EXPOSURE OF POTENTIAL ACID SULPHATE SOILS (ABOVE THE WATER TABLE) EXCEEDING 24 HOURS REQUIRES TREATMENT
- EW.13. THESE DRAWINGS SHALL BE READ IN CONJUNCTION WITH ALL SITE GEOTECHNICAL REPORTING. TO BE UNDERTAKEN AND SUPPLIED.

GEOTEXTHES

- EW.14. GEOTEXTILE SHALL BE THE APPROPRIATE STRENGTH CLASS AND FILTRATION CLASS COMPLYING WITH THE REQUIREMENTS OF MRTS27.
- EW.15. GEOTEXTILES USED IN PAVING APPLICATIONS SHALL BE IN ACCORDANCE WITH MRTS57.
- EW.16. GEOTEXTILES SHALL BE FREE OF ANY FLAWS.
- THE AREA ON WHICH THE GEOTEXTILE IS TO BE PLACED CLEAR OF ALL SHARP OBJECTS AND LARGE ROCKS. NO CONSTRUCTION EQUIPMENT SHALL STAND OR TRAVEL DIRECTLY ON THE

SITE REHABILITATION

- EW.18. ENSURE THE SOIL SURFACE IS SCARIFIED PRIOR TO THE PLACEMENT OF TOPSOIL TO BREAK UP ANY EXCESSIVE COMPACTION, AND ENABLE THE APPROPRIATE KEYING OF THE SOIL
- EW.19. SCARIFY LIGHTLY COMPACTED SOILS TO A MINIMUM DEPTH OF 100mm AND HEAVILY COMPACTED SUBSOIL TO A MINIMUM DEPTH OF 300mm
- EW.20. TURF MUST NOT BE PLACED ON EXCESSIVELY COMPACTED SOILS.
- EW.21. SOIL TESTING SHOULD BE USED TO DETERMINE ANY REQUIRED CHEMICAL ADJUSTMENT TO THE SOIL (E.G. GYPSUM, LIME, FERTILISER, PH ADJUSTMENTS).
- EW.22. THE CONTRACTOR SHALL MONITOR ALL SITE REHABILITATION MEASURES, PARTICULARLY AFTER RAINFALL

LOCAL ASSET OWNERS ASSET OWNER TYPF CONTACT ELECTRICAL ERGON OLD 13 10 46 COMMUNICATIONS TELSTRA OLD REGIONAL 1800 653 935 RAIL CORRIDOR AURIZON NETWORK PTY LTD (07) 3019 7969

LEGEND:



NO WORK IS SO IMPORTANT THAT IT CANNOT BE **DONE SAFELY**

| EXISTING DESIGN | | W |
|-----------------|-------------|----------------------------------|
| - | | RP BOUNDARY |
| | | LIMIT OF WORKS |
| | | ROAD CENTRELINE/CONTROL INE |
| | TY3 | KERB & CMDG TYPE |
| 11 | <u> </u> | EARTHWORKS BATTER |
| | | TRAIN CORRIDOR |
| | | CONTOUR MAJOR |
| | // | FENCE |
| | | EXISTING VEGETATION BORDER |
| | | HYDROMULCH |
| SWD | 3517/15 | STORMWATER PIPE |
| | | CHANNEL/SWALE/TABLE DRAIN INVERT |
| | | FLOOD MAP WATER WAY |
| | | CATCHMENT BOUNDARY |
| 0 | 0 | MANHOLE |
| | ₩ | HEADWALL |
| | ens ens | GULLY PIT - SAG / DN-GRADE |
| D | 0 | FIELD INLET |
| ——R ——R —— | ——R ——R —— | SEWER EFFLUENT MAIN |
| ss | 5 | SEWER GRAVITY MAIN |
| SRY | | SEWER RISING MAIN |
| | —— <u> </u> | ELECTRICAL UG |
| £0(B) | EOh | ELECTRICAL & STAYWIRES OH |
| | | COMMUNICATIONS / NBN |
| | | |

| Α | BBREVIATIONS TABLE |
|--------|-------------------------------------------------|
| ABBR. | DESCRIPTION |
| PR | PROPOSED |
| EX | EXISTING |
| ELEC | ELECTRICITY |
| STRM | STORMWATER |
| WATR | WATER |
| SEWR | SEWER |
| TELS | TELSTRA |
| EFF | EFFLUENT |
| MDW | NON DRINKING WATER |
| COMMS | COMMUNICATION |
| STD. | STANDARD |
| DWG. | DRAWING |
| HV | HIGH VOLTAGE |
| IPWEA | INSTITUTE OF PUBLIC WORKS ENGINEERING AUSTRALIA |
| RP BDY | REAL PROPERTY BOUNDARY |
| CP | COMMON PROPERTY |
| ESL | EXISTING SURFACE LEVEL |
| FSL | FINISHED SURFACE LEVEL |
| RL | REDUCED LEVEL |
| FL | EARTHWORKS FINISHED LEVEL |
| PL | FINISHED PAVEMENT LEVEL |
| GL | GARAGE FLOOR LEVEL |
| LL | LIP LEVEL OF KERB |
| BOW | BOTTOM OF WALL |
| TOW | TOP OF WALL |
| DTMR | DEPARTMENT OF TRANSPORT AND MAIN ROADS |
| FRC | FRASER COAST REGIONAL COUNCIL |

WARNING

NOTE: EXISTING SERVICES SHOWN IN AREA OF WORKS ARE LEVEL D PER ASS488 AND ARE TO BE VERIFIED BY CONTRACTOR PRIOR TO CONSTRUCTION

| A | FOR APPROVAL | 05.08.24 |
|-----|--------------|----------|
| No. | Revision | Date |

Martecs ABN 27 158 351 663 PH: 1300 220 195 EMAIL: admin@hartecs.com.au OFFICE: ROCKHAMPTON


GFOUD MTS - Banana Shire Council afMW - Banana Shire Council SAMANTHA WILSON CHASE KEMP

Certified CHARLES COOK RPEQ #: 8480



PAVEMENT REHABILITATION, RESEAL & DRAINAGE WORKS SHEPHERDSONS RD. BILOELA **GENERAL NOTES AND LEGEND**

| Dwg. No. | Sheet | | | - |
|------------------|-------|----|----|---|
| PRJ-0342-01-GN02 | 02 | OF | 19 | |

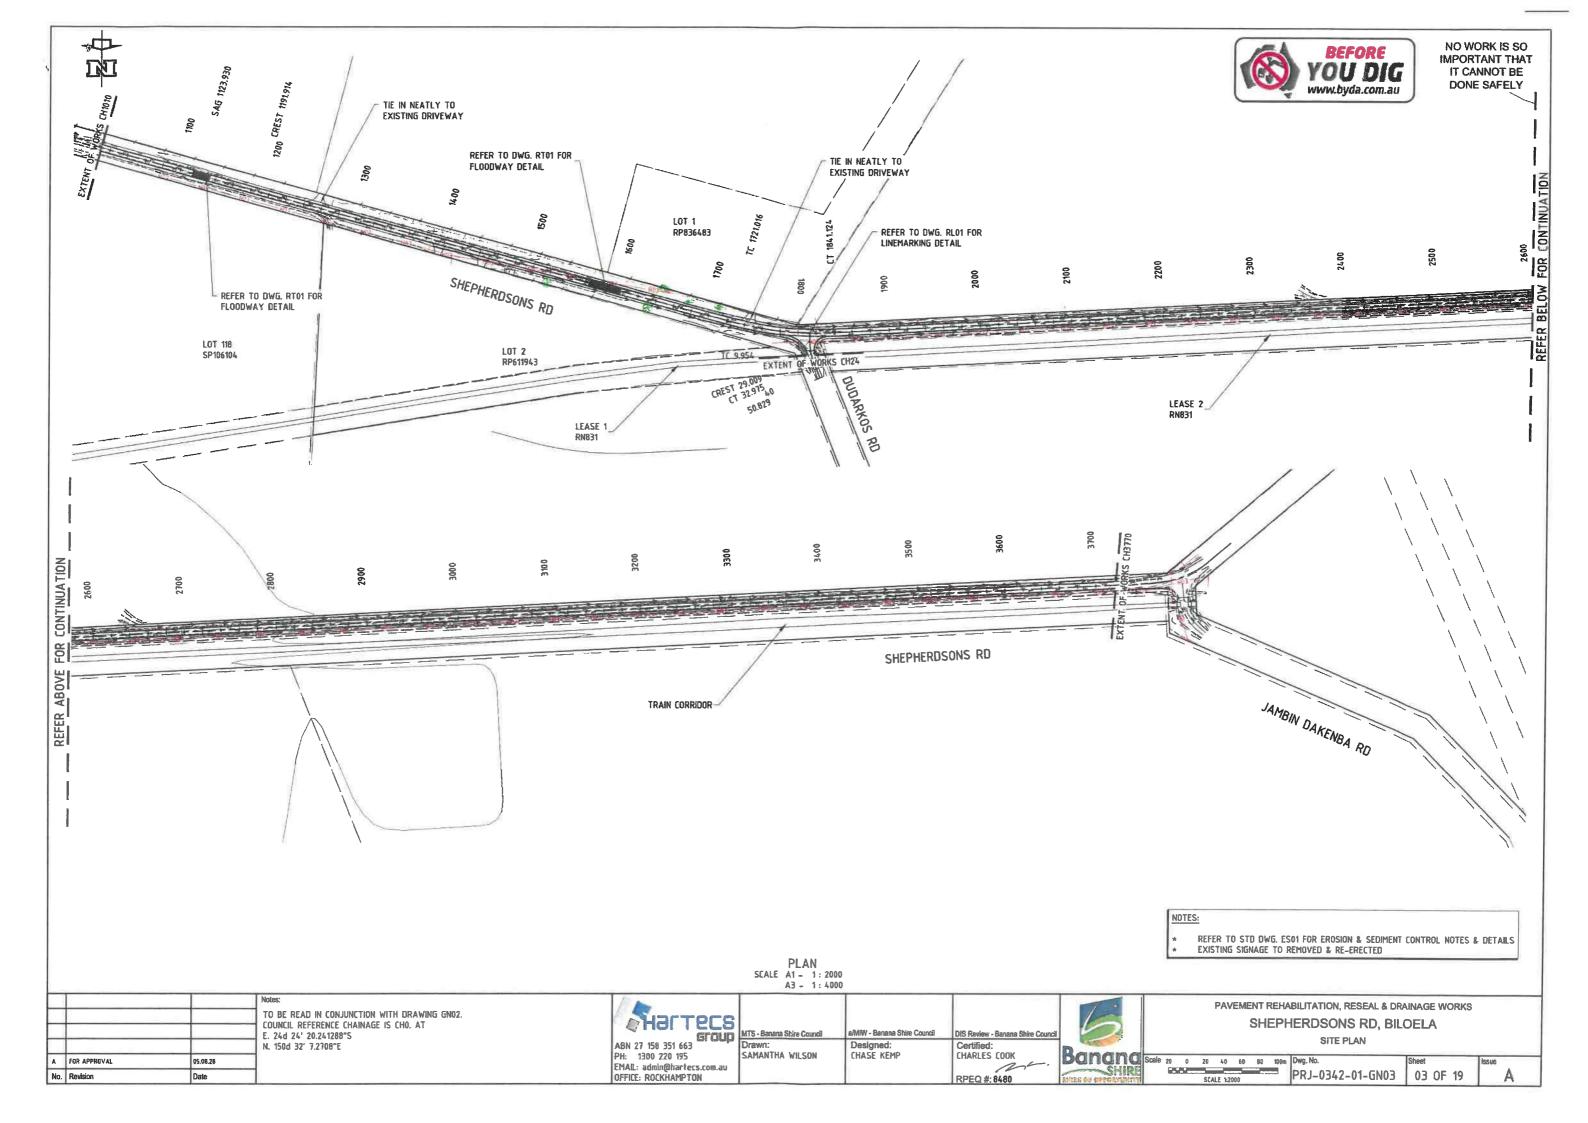



NO WORK IS SO IMPORTANT THAT IT CANNOT BE DONE SAFELY

SOIL & WATER MANAGEMENT PLAN

OBJECTIVES OF THIS PLAN

- TO MINIMISE DISTURBANCE OF THE SITE BY RESTRICTING ACCESS TO THOSE AREAS OF THE SITE NOT REQUIRED AS PART OF THE ROADWORK.
- TO LOCATE STOCKPILES IN AREAS WHERE THEY WILL NOT IMPEDE THE FLOW OF WATER SO AS TO MINIMISE LOSS OF MATERIALS FROM THE STOCKPILE AND SUBSEQUENT MOBILISATION OF SEDIMENTS.
- TO DIVERT/CAPTURE RUNOFF FROM AREAS OF DISTURBANCE & STOCKPILE AREAS IN SEDIMENT TRAPS PRIOR TO DISCHARGING OFF SITE.
- TO AS FAR AS PRACTICAL DIVERT WATER FROM AREAS NOT PART OF THE OPERATIONS AWAY FROM OPERATIONAL AREAS - SEPARATE 'CLEAN' & 'DIRTY' WATER.
- 5. TO CONTROL AND MANAGE DUST AND NOISE GENERATED AS A RESULT OF SITE OPERATIONS.
- 6. TO ENSURE THAT GENERAL RUBBISH GENERATED BY THE SITE & IT'S WORKERS & SUBCONTRACTORS ETC IS PROPERLY STORED ON SITE & DISPOSED OF IN THE CORRECT MANNER BY TRANSPORTING TO AN AUTHORISED LAND FILL SITE
- TO ENSURE THAT GENERAL MATERIALS SUCH AS SAND, CEMENT, FUEL, OILS, PAINT ETC ARE STORED IN A
 PROPER MANNER & LOCATED SO AS NOT TO POLLUTE THE SURROUNDING AREA IN THE EVENT OF AN
 ACCIDENTAL SPILL.
- 8. TO PUT IN PLACE APPROPRIATE MEASURES TO PREVENT AT ALL TIMES THE UNCONTROLLED TRANSPORTATION/HAULAGE OF MATERIALS OFF SITE & SUBSEQUENT POLLUTING OF THE ENVIRONS
- 9. TO MONITOR THE IMPLEMENTATION OF THIS PLAN & ADJUST MEASURES AS REQUIRED TO IMPROVE THE EFFECTIVENESS OF THE DEVICES USED TO CONTROL SOIL & WATER ON THIS SITE. THE INFORMATION PRESENTED ON THESE PLANS REPRESENTS A MASTER PLAN APPLICABLE AT THE TIME OF PREPARING THESE PLANS. THE EROSION & SEDIMENT CONTROL DEVICES (ESCD) REQUIREMENTS ARE EXPECTED TO VARY DURING THE COURSE OF THE LIFE OF THE OPERATION TO SUIT CHANGES IN OPERATIONS. THE REQUIREMENTS SHALL BE CONTINUALLY REVIEWED & THE ESCD PLAN AND MEASURES UPDATED ACCORDINGLY.

GENERAL MANAGEMENT & IMPLEMENTATION OF PLAN

- THE CONTRACTOR SHALL HAVE APPOINTED A SUITABLY QUALIFIED SITE WORKS PRACTICES SUPERVISOR TO MANAGE SOIL EROSION & POLLUTION BY SEDIMENTS & OTHER CONTAMINANTS.
- 11. THE SITE WORKS PRACTICES SUPERVISOR SHALL ALSO BE RESPONSIBLE FOR CONTROLLING SUBCONTRACTORS ETC ON THE SITE.
- 12. THE SITE WORKS PRACTICES SUPERVISOR SHALL SET UP A REGULAR PROGRAM OF INSPECTION OF THE SITE TO ENSURE THAT THE MEASURES INTRODUCED TO CONTROL SOIL & WATER ON THE SITE ARE WORKING CORRECTLY & REMAINING IN GOOD ORDER. THE RE-ESTABLISHMENT OF GROUND COVERS SHALL BE REGULARLY MONITORED DURING THE CONSTRUCTION PERIOD & AREAS MADE GOOD IMMEDIATELY THERE ARE SIGNS OF DETERIORATION.
- 13. THE SUITABILITY OF THE SEDIMENT & EROSION CONTROL MEASURES IN PLACE SHALL BE CONTINUALLY REVIEWED AND ADJUSTMENTS MADE AS REQUIRED TO MAINTAIN ADEQUATE PROTECTION AND CONTROL MEASURES.
- 14. THE SEDIMENT & EROSION CONTROL MEASURES SHALL REMAIN IN FORCE & BE MAINTAINED UNTIL SUCH TIME AS REHABILITATION IS COMPLETED & PERMANENT POST PRODUCTION MEASURES ARE IN PLACE & SUFFICIENTLY ESTABLISHED TO ENSURE SITE STABILITY.
- 15. TEMPORARY SEDIMENT SUMPS SHALL BE INSPECTED PRIOR TO & AFTER ANY SIGNIFICANT RAINFALL EVENT.
- A PLAN OF THE CURRENT SITE SEDIMENT & CONTROL MEASURES SHALL BE KEPT AT ALL TIMES IN A READILY ACCESSIBLE PLACE IN THE SITE OFFICE.
- 17. THE CONSTRUCTION PROGRAM FOR THE WORKS SHALL BE BASED ON ENSURING THAT THE TIME BETWEEN WHEN A PORTION OF THE WORKS IS STARTED TO THE TIME THAT IT HAS RECEIVED ITS FINAL SURFACING/PROTECTIVE COVERING/LANDSCAPING IS MENIMISED. THE INSTALLATION/ CONSTRUCTION OF FINAL SURFACINGS/ PROTECTIVE COVERINGS/LANDSCAPING SHALL BE STAGED AND CARRIED OUT PROGRESSIVELY TO MINIMISE THE TIME OF DISTURBANCE.

MATERIALS HANDLING PLAN

- SOIL TYPE STOCKPILES OF MATERIALS SHALL HAVE DIVERSION DRAINS PROVIDED ON THE UP-SLOPE SIDE & SILT FENCES ON THE DOWN-SLOPE SIDES.
- DIESEL, FUELS & OILS SHALL BE STORED IN A DESIGNATED AREA WITH APPROVED SPILLAGE TRAPS/CONTAINMENTS & PROTECTED FROM SPILLING ONTO ADJOINING AREAS.
- 20. STOCKPILED MATERIALS ARE TO BE SURROUNDED WITH APPROPRIATE SELT BARRIERS TO PREVENT LOSS OF SEDIMENTS TO THE SURROUNDING AREA.

DUST CONTROL PLAN

- 21. SUITABLE DEVICES SUCH AS A WATER TRUCK SHALL BE AVAILABLE AT ALL TIMES FOR DUST SUPPRESSION.
- 22. THE CONTRACTOR SHALL MONITOR WIND CONDITIONS AT ALL TIMES & SHALL PROVIDED ADEQUATE DUST SUPPRESSION TO SUIT CONDITIONS. THIS SHALL INCLUDE THE CESSATION OF OPERATIONS IF DUST GENERATED FROM CONSTRUCTION OPERATIONS CANNOT BE ADEQUATELY CONTROLLED.
- 23. ADEQUATE DUST SUPPRESSION SHALL BE APPLIED TO ALL AREAS OF OPERATIONS & OTHER DISTURBED AREAS AT ALL TIMES.

WATER CONTROL PLAN

- 24. STORMWATER RUNOFF SHALL BE DIRECTED AWAY FROM THE WORKS & DISTURBED AREAS AS FAR AS IS POSSIBLE.
- 25. WATER SHOULD BE DISCHARGED FROM THE WORK AREAS AS SOON AS POSSIBLE. WATER SHOULD NOT BE ALLOWED TO ACCUMULATE INTO LARGE VOLUMES AS THESE BEGIN TO MOVE FAST & CARRY EXCESS ENERGY WHICH WILL CAUSE GREATLY INCREASED EROSION AT THE FINAL POINT OF DISCHARGE OFF SITE.
- 26. SILT BARRIERS ARE TO BE USED TO CATCH SILT IN WATER DISCHARGES. EVERY EFFORT IS TO BE MADE TO ENSURE THAT THE WATER PASSING THROUGH THE SITE FINALLY DISCHARGES IN AN UNPOLLUTED STATE, FREE OF AS MUCH SEDIMENT & SILT AS POSSIBLE.
- 27. WATER CONTAMINATED WITH CHEMICALS, CEMENT OR OTHER POLLUTANTS SHALL NOT BE ALLOWED TO DISCHARGE OFF SITE.

CONSTRUCTION PLAN

- 28. ESCD's SHALL BE ERECTED PRIOR TO ANY EARTHWORKS COMMENCING.
- 29. SUITABLE SITES FOR STOCKPILING TOPSOIL & GENERAL FILL MATERIAL (IF NOT TO BE PLACED IN AN EMBANKMENT IMMEDIATELY) ARE TO BE SELECTED & DELINEATED.
- 30. CUT TO FILL OPERATIONS ARE TO BE CONDUCTED IN SUCH A WAY AS TO MINIMISE DISTURBANCE TO THOSE AREAS OF THE SITE THAT DO NOT NEED TO BE DISTURBED AS PART OF THE GENERAL SCOPE OF WORKS.
- 31. SILT BARRIERS SHALL BE SPECIFICALLY CONSTRUCTED AT THOSE POINTS WHERE WATER RUNOFF WOULD LEAVE THE DISTURBED AREA OF THE SITE & PASS ONTO ADJACENT SITES/PROPERTIES.
- 32. THE WORKS SHALL BE PROGRAMMED IN SUCH A WAY AS TO ALLOW AREAS TO BE FINISHED OFF AS THEY BECOME COMPLETED. LE. SECTIONS OF WORK SHOULD BE FINALLY TRIMMED, RE-TOPSOILED & REVEGETATED AS SPECIFIED AS AN ONGOING ACTIVITY RIGHT THROUGH THE CONSTRUCTION PHASE OF THE PROJECT. THIS WILL ALLOW THE EARLY ESTABLISHMENT OF NEW GROUND COVER, THUS MINIMISING THE TIME THE WORKS ARE LEFT VULNERABLE TO EROSION ETC.
- 33. ONCE A SECTION OF WORKS HAS BEEN COMPLETED & THE REQUIRED STABILISATION CONSTRUCTED, THE CONTRACTOR SHALL NOT DISTURB ANY AREAS OTHER THAN THOSE ABSOLUTELY NECESSARY TO ALLOW THE INSTALLATION OF SERVICES. ANY AREAS DISTURBED DURING THE INSTALLATION OF SERVICES SHALL BE IMMEDIATELY RE-INSTATED UPON COMPLETION OF THE SERVICE INSTALLATION.
- 34. ONCE A SECTION OF THE WORKS IS OPENED UP THE WORKS SHALL BE COMPLETED BEFORE A NEW SECTION IS OPENED UP, I.E. CONSECUTIVE WORKS APPROVAL.
- 35. THE OUTLET OF THE DRAIN LINES SHALL HAVE THE HEADWALL & APRON STRUCTURES & DOWNSTREAM SCOUR PROTECTION WORKS CONSTRUCTED WITHOUT DELAY SO THAT OUTFALLING WATER WILL BE PREVENTED FROM SCOURING & ERODING THE AREA AROUND THE PIPE OUTLET AND DOWNSTREAM.
- SILT BARRIERS SHALL BE FIXED DOWNSTREAM OF EACH DRAINAGE OUTLET TO CAPTURE ALL PASSING FLOWS.
- 37. ROAD GRAVELS USED TO CONSTRUCT THE ROAD PAVEMENT SHALL BE PLACED, SPREAD & COMPACTED IMMEDIATELY THEY ARE BROUGHT ONTO SITE SO AS TO PREVENT POSSIBLE MASSIVE LOSS OF PARTICLES & SEDIMENT SHOULD A RAIN STORM OCCUR WHILST THEY ARE IN AN UNCONSOLIDATED STATE.
- 38. ROAD SURFACINGS SHALL BE PROTECTED AS SOON AS THE PAVEMENT CONSTRUCTION & INSTALLATION OF DRAINAGE STRUCTURES HAS BEEN COMPLETED.
- 39. AS STOCKPILE AREAS BECOME REDUNDANT THEY SHALL BE SCARIFIED, RETOPSOILED & REVEGETATED AS SPECIFIED. SIMILARLY OTHER DISTURBED AREAS OF THE SITE USED FOR ACCESS, STORAGE OF MATERIALS & THE CONTRACTORS COMPOUND ETC ARE TO BE SCARIFIED, RETOPSOILED AS NECESSARY & REVEGETATED AS THEY BECOME NO LONGER REQUIRED FOR THE PERFORMANCE OF THE WORKS.
- 40. EXPOSED BANKS & BATTERS SHALL BE RE-TOPSOILED PLANTED & LANDSCAPED IN ACCORDANCE WITH THE EROSION & SEDIMENT CONTROL PLAN AS SOON AS POSSIBLE AFTER FINAL TRIMMING.
- 41. BEFORE PLACING TOPSOIL THE BANK SHALL BE SCARIFIED TO 75mm DEEP TO HELP BOND THE TOPSOIL LAYER.
- 42. REVEGETATED & LANDSCAPED AREAS SHALL BE REGULARLY WATERED TO ASSIST WITH GERMINATION & ESTABLISHMENT OF THE COVER.
- 43. BANKS & BATTERS TO BE REGULARLY INSPECTED TO IDENTIFY AREAS OF EROSION & MAKE THE NECESSARY RECTIFICATIONS TO STOP RECURRENCE.

INSPECTION & MONITORING PLAN

INSPECTIONS SHOULD BE UNDERTAKEN

- 44. DURING ANY STORM EVENT THAT THREATENS TO EXCEED THE AVAILABLE CAPACITY IN THE SEDIMENT OR POLLUTION STORAGE STRUCTURES.
- 45. AFTER ANY STORM THAT HAS CAUSED RUNOFF.
- 46. WEEKLY AS A MATTER OF SITE ROUTINE FOR ALL SITE WORK PRACTICES.
- 47. BEFORE SITE CLOSURE OR ANY OTHER TIME WHEN THE SITE MAY BE UNATTENDED FOR LONGER THAN 12 HOURS.

RECORD / DIARY KEEPING

THE SITE WORKS PRACTICES SUPERVISOR SHALL MAINTAIN A RECORD OR DIARY DOCUMENTING

48. DATES OF INSTALLATION & REMOVAL OF SITE WORK PRACTICES REPAIR OF ANY DAMAGE TO SITE WORKS PRACTICES RAINFALL DEPTHS, DURATIONS & TIMES STORAGE CAPACITY AVAILABLE IN CONTROL STRUCTURES CONDITION OF SITE WORK PRACTICE STRUCTURES & STABILISED SURFACES.

49. MAINTAIN A SITE RAINFALL GAUGE AND RECORDING

- 50. CARRY OUT WATER SAMPLING AT MONITORING POINTS FOR A SAMPLE OF LOW AND HIGH FLOW EVENTS DURING THE WET SEASON AND RECORD DATE, TURBITY, PH AND AMOUNT OF RAINFALL.
- 51. RECORD KEEPING MUST INCLUDE A PHOTOGRAPHIC RECORD.

INSPECTION PROGRAM

- 52. INSPECT BATTERS & EMBANKMENT SLOPES FOR SCOUR OR EROSION & MAKE GOOD
- 53. INSPECT CATCH DRAINS & TABLE DRAINS & CLEAR OUT SEDIMENT AS REDUIRED
- 54. INSPECT INLETS & PIPES & CLEAN OUT AS REQUIRED.
- 55. INSPECT OUTLETS & IMMEDIATELY MAKE GOOD ANY SIGN OF EROSION.
- 56. INSPECT STOCKPILES TO ENSURE NO MATERIAL IS ESCAPING BEYOND THE SILT FENCES.
- 57. INSPECT THE AREAS USED TO STORE MATERIALS FOR PROPER STORAGE PRACTICES.
- 58. INSPECT THE CONTRACTORS COMPOUND AREA FOR CORRECT STORAGE OF MATERIALS.
- 59. INSPECT THE REFUSE BINS TO ENSURE THEY HAVE BEEN REGULARLY CLEARED.

REFERENCES/STANDARD DRAWINGS

REFERENCE INTERNATIONAL EROSION CONTROL ASSOCIATION (AUSTRALASIA (IECA) BEST PRACTICES MANUALS.

TMR STD DWG'S

EROSION & SEDIMENT CONTROL MANAGEMENT

EROSION & SEDIMENT CONTROL IMPLEMENTATION

- ESI.1. ALL EXIST TREES TO BE MULCHED ON SITE & SPOIL REMOVED. MULCH TO BE STOCKPILED FOR RE-USE ON SITE.
- ESI.2. DISTURBANCE TO EXISTING GRASS COVER SHALL BE MINIMISED. CONSTRUCTION TRAFFIC SHALL NOT USE GRASSED AREAS FOR PARKING EQUIPMENT OR STOCKPILING MATERIALS.
- ESI.3. SEQUENCING OF THE INSTALLATION OF LANDSCAPING, SEDIMENT & DEVICES ARE SHOWN ON THE PLAN.
- ESI.4. STORMWATER OUTLETS MUST BE PREVENTED FROM CAUSING SCOUR & EROSION.
- ESI5. THE CONTRACTOR IS RESPONSIBLE FOR THE CONTROL OF DUST & SILT ON THE SITE. DUST SUPPRESSION MEASURES MUST BE IMPLEMENTED AT ALL TIMES DURING THE CONTRACT PERIOD & DURING THE CLEARING & GRUBBING PHASE.
- ESI.6. ALL DISTURBED AREAS & SERVICE TRENCHES ON THE SITE MUST BE RE-TOPSOILED & HYDROMULCHED INCLUDING ALL HAUL TRACKS CREATED BY THE CONTRACTOR, UNLESS SHOWN OTHERWISE
- ESI.7. SILT FENCES MUST BE INSTALLED ON THE LOW SIDE OF ALL STOCKPILES.

SEQUENCING

- PRIOR TO COMMENCEMENT OF EARTHWORKS
- DURING & AFTER COMPLETION OF EARTHWORKS & FOR DURATION OF CONSTRUCTION PERIOD
- 3 AFTER COMPLETION OF CONSTRUCTION & FOR DURATION OF MAINTENANCE PERIOD
- PERMANENT

FOR CONSTRUCTION SEDIMENT & EROSION CONTROL PLAN & MEASURES REFER TO CMDG D-050, D-0501 & D-060.

| SITE | ER | OSI | ON | RI | SK | AS | SE | SS | ME | NT | | |
|--------------------------------|-------|------|--------|-------|-------|--------|-----|-------|-----|-----|------|-----|
| ASSESSMENT CRITERIA | JAN | FEB | MAR | APR | MAY | N | JUL | AUG | SEP | OCT | NOV | DEC |
| AVERAGE RAINFALL | 154 | 145 | 94 | 49 | 57 | 38 | 34 | 32 | 27 | 58 | 72 | 130 |
| SITE EROSION RISK RATING | Н | н | М | М | М | L | Ł | VL | VL | М | М | н |
| RATING SITE EROSION RISK RA | TING: | HIGH | (H); M | IODER | ATE (| M); LC | | ; VER | | | - (7 | r |

TO BE READ IN CONJUNCTION WITH DRAWING GN02. COUNCIL REFERENCE CHAINAGE IS CHO. AT E. 24d 24' 20.241268"S N. 150d 32' 7.2708"E

ABN 27 158 351 663
PH: 1300 220 195
EMAIL: admin@hartecs.com.au

OFFICE: ROCKHAMPTON

MTS - Banana Shire Council Drawn: SAMANTHA WILSON

a/MfW - Banana Shire Council

Designed:
CHASE KEMP

DIS Review - Banana Shire Count Certified: CHARLES COOK RPEQ #: 8480





PAVEMENT REHABILITATION, RESEAL & DRAINAGE WORKS
SHEPHERDSONS RD, BILOELA
CONCEPT EROSION & SEDIMENT CONTROL NOTES AND DETAILS


CONCEPT EROSION & SEDIMENT CONTROL NOTES AND DETAILS

Scale 50 0 50 100 150 200 250m Dwg. No. Sheet Issue

PRJ-0342-01-ES01 4 0F 19

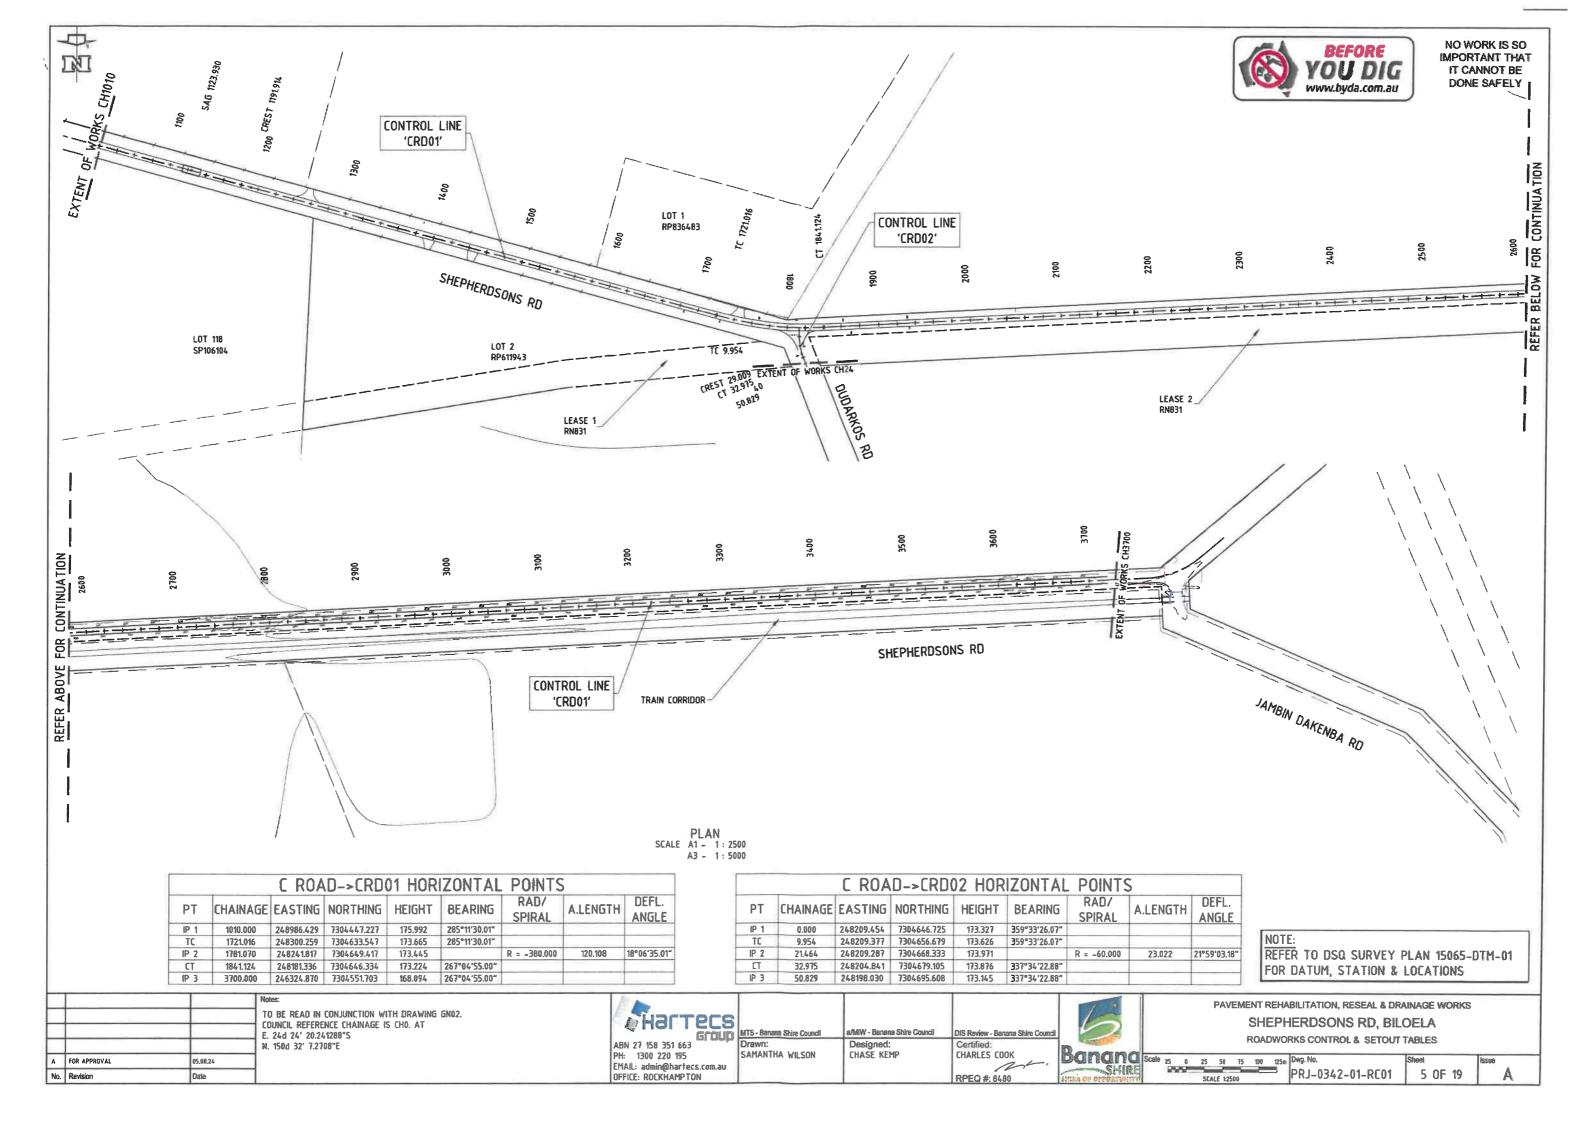


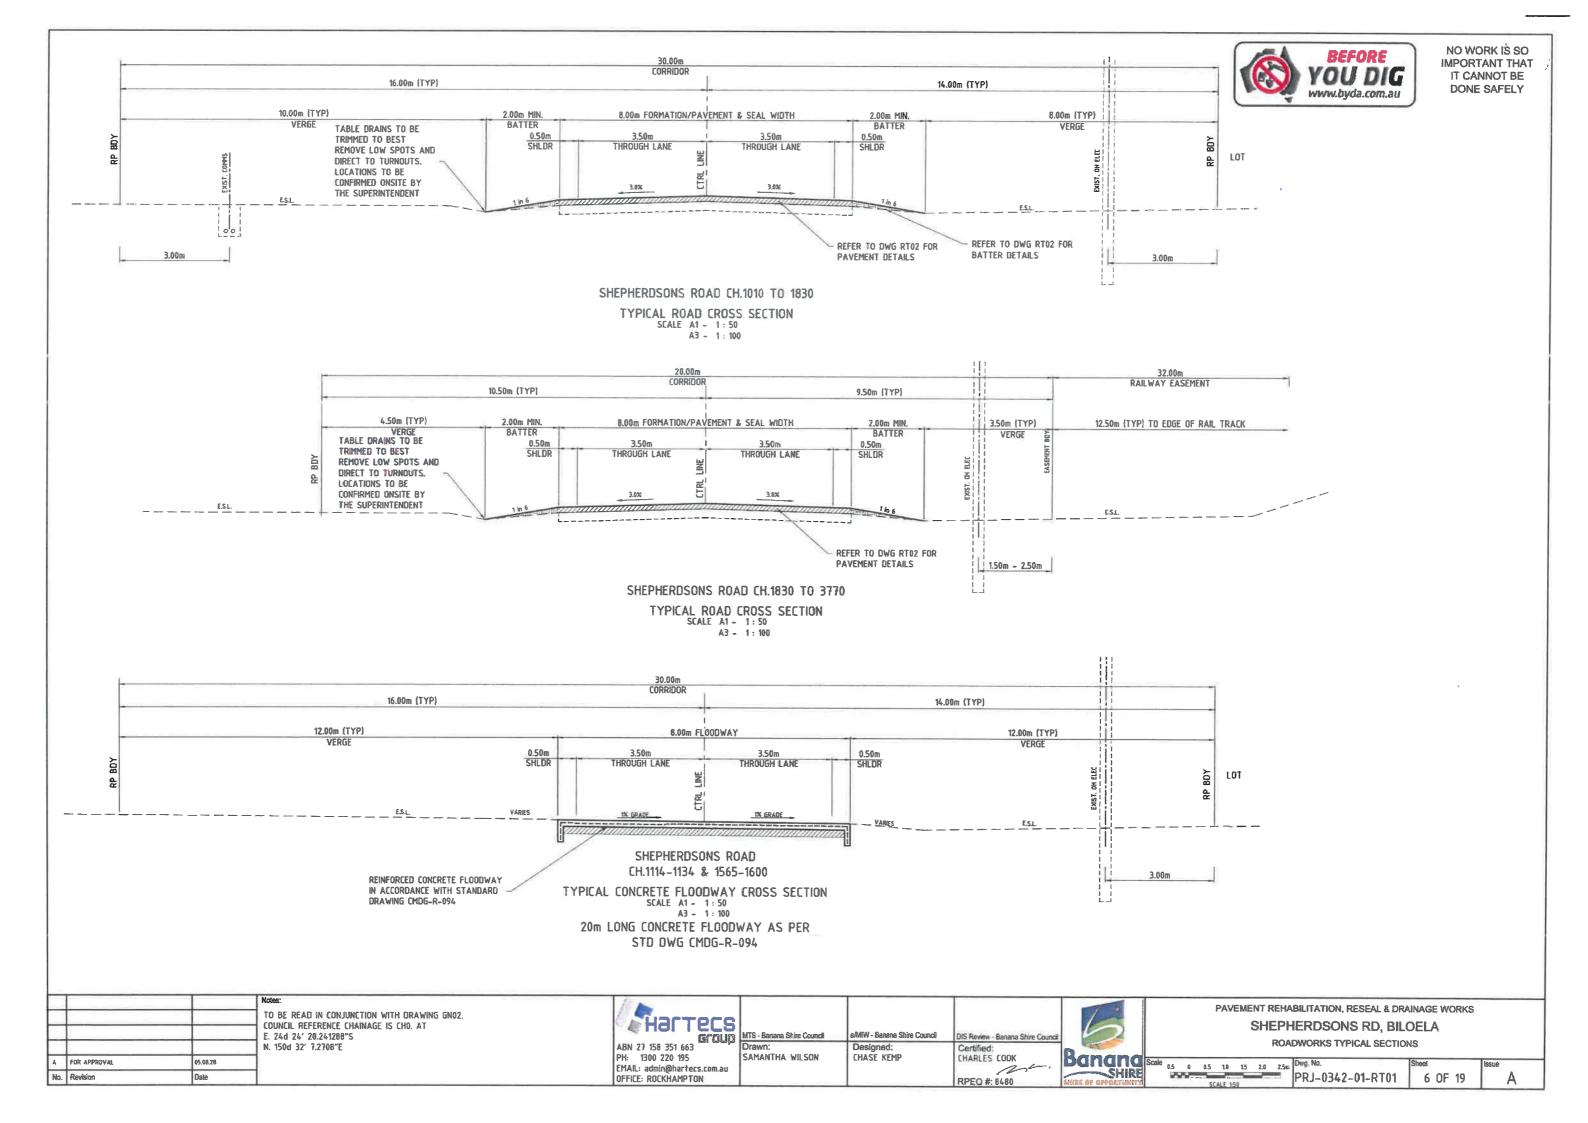

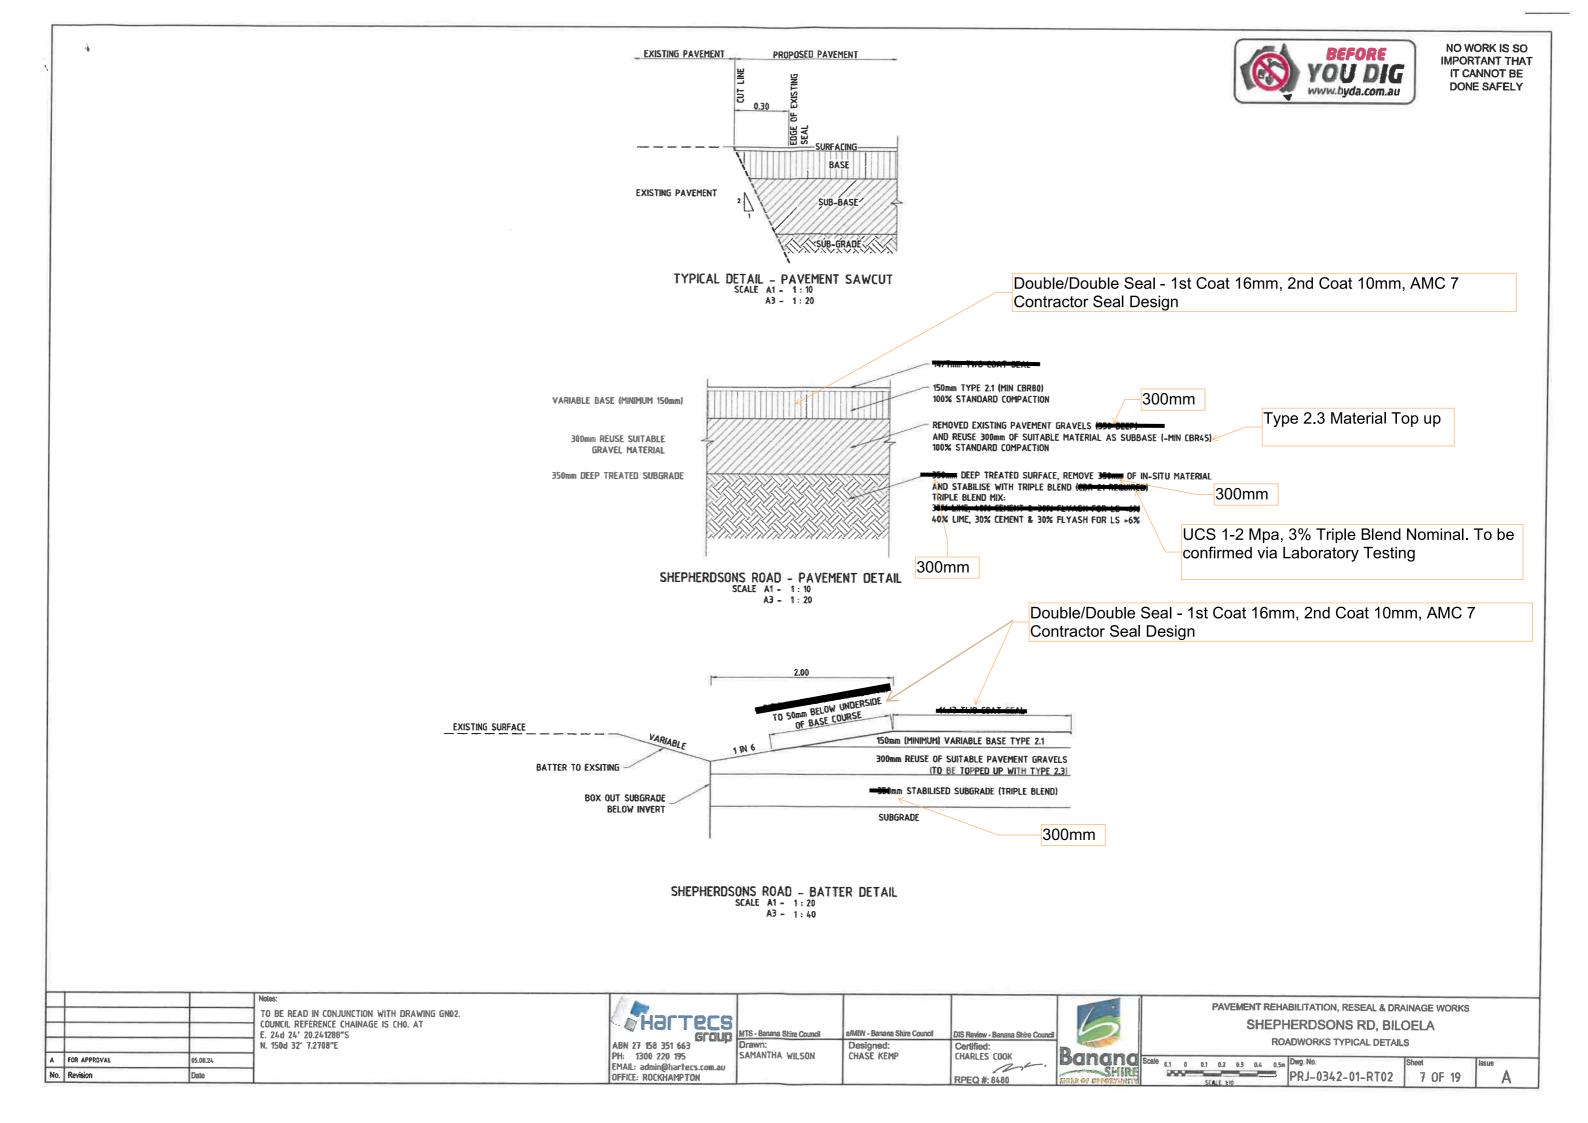



NO WORK IS SO IMPORTANT THAT
IT CANNOT BE DONE SAFELY

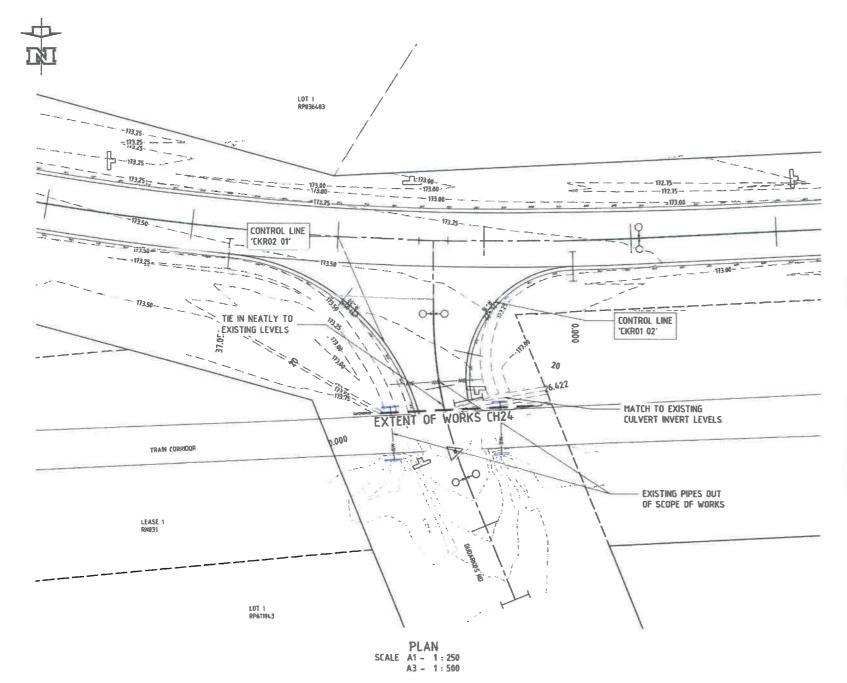

| | (| ROAD-> | CKR01 02 | 2 HORIZ | CONTAL | SEGMEN | TS | |
|----|----------|------------|-------------|---------|---------------|---------|---------|---------|
| PT | CHAINAGE | EASTING | NORTHING | HEIGHT | BEARING | DEP.SEG | DEP.RAD | DEP.LEN |
| S | 0.000 | 248190.305 | 7304650.186 | 173.362 | 347°31′23.67″ | ARC | -15.000 | 26.422 |
| | 5.000 | 248195.189 | 7304651.144 | 173.381 | 69°21'03.57" | | -15.000 | |
| | 10,000 | 246199,490 | 7304653,640 | 173.399 | 50"15"08.64" | | -15.000 | |
| | 15.000 | 248202.736 | 7304657.421 | 173.551 | 31°09′13.70″ | | -15.000 | |
| | 20.000 | 248204.568 | 7304662.048 | 173.706 | 12°03'18.77" | | -15.000 | |
| | 25.000 | 248204.786 | 7304667.020 | 173.856 | 352°57′23.83″ | | -15.000 | |
| Ε | 26.422 | 248204.545 | 7304668.421 | 173.899 | 347°31'23.67" | | | 7 |

| | [| ROAD-> | CKR01 0 | 2 HORIZ | CONTAL | SEGMEN | TS | |
|----|----------|------------|-------------|---------|---------------|---------|---------|---------|
| PT | CHAINAGE | EASTING | NORTHING | HEIGHT | BEARING | DEP.SEG | DEP.RAD | DEP.LEN |
| S | 0.000 | 248190.305 | 7304650.186 | 173.362 | 347°31'23.67" | ARC | -15.000 | 26.422 |
| | 5.000 | 248195.189 | 7304651.144 | 173.381 | 69°21'03.57" | | -15.000 | |
| | 10.000 | 248199.490 | 7304653.648 | 173,399 | 50°15'08.64" | | -15.000 | |
| | 15.000 | 248202.736 | 7304657.421 | 173.551 | 31°09'13.70" | | -15.000 | |
| | 20.000 | 248204.568 | 7304662.048 | 173.706 | 12°03'18.77" | | -15,000 | |
| | 25.000 | 248204.786 | 7304667.020 | 173.856 | 352°57'23.83" | | -15.000 | |
| E | 26.422 | 248204.545 | 7304668.421 | 173,899 | 347°31'23.67" | | | |

| | | | Notes: TO BE READ IN CONJUNCTION WITH DRAWING GN02. COUNCIL REFERENCE CHAINAGE IS CHO. AT E. 24d 24' 20.241288"S N. 150d 32' 7.2708"E |
|-----|--------------|----------|----------------------------------------------------------------------------------------------------------------------------------------|
| A | FOR APPROVAL | 05.08.24 | === |
| No. | Revision | Date | |

Нагтесь ABN 27 158 351 663
PH: 1300 220 195
EMAIL: admin@hartecs.com.au
OFFICE: ROCKHAMPTON

aAHW - Banana Shire Council Designed: CHASE KEMP Certified: CHARLES COOK

RPEQ #: 8480


DIS Review - Banana Shire Council Banana Scale SHIRE SHIRE OF EXPORTUNITY


PAVEMENT REHABILITATION, RESEAL & DRAINAGE WORKS SHEPHERDSONS RD, BILOELA **ROADWORKS INTERSECTION DETAIL & SETOUT TABLES**


| 2.5 | 0 | 2.5 | 5.9 | 7.5 | 10 | 12.5m | Dwg. No. |
|-----|---|-----|--------|-----|----|-------|----------|
| | | | | - | _ | _ | PRJ-034 |
| | | SC | ALE 12 | 50 | | | PKJ-034 |

342-01-RI01 8 OF 19

A

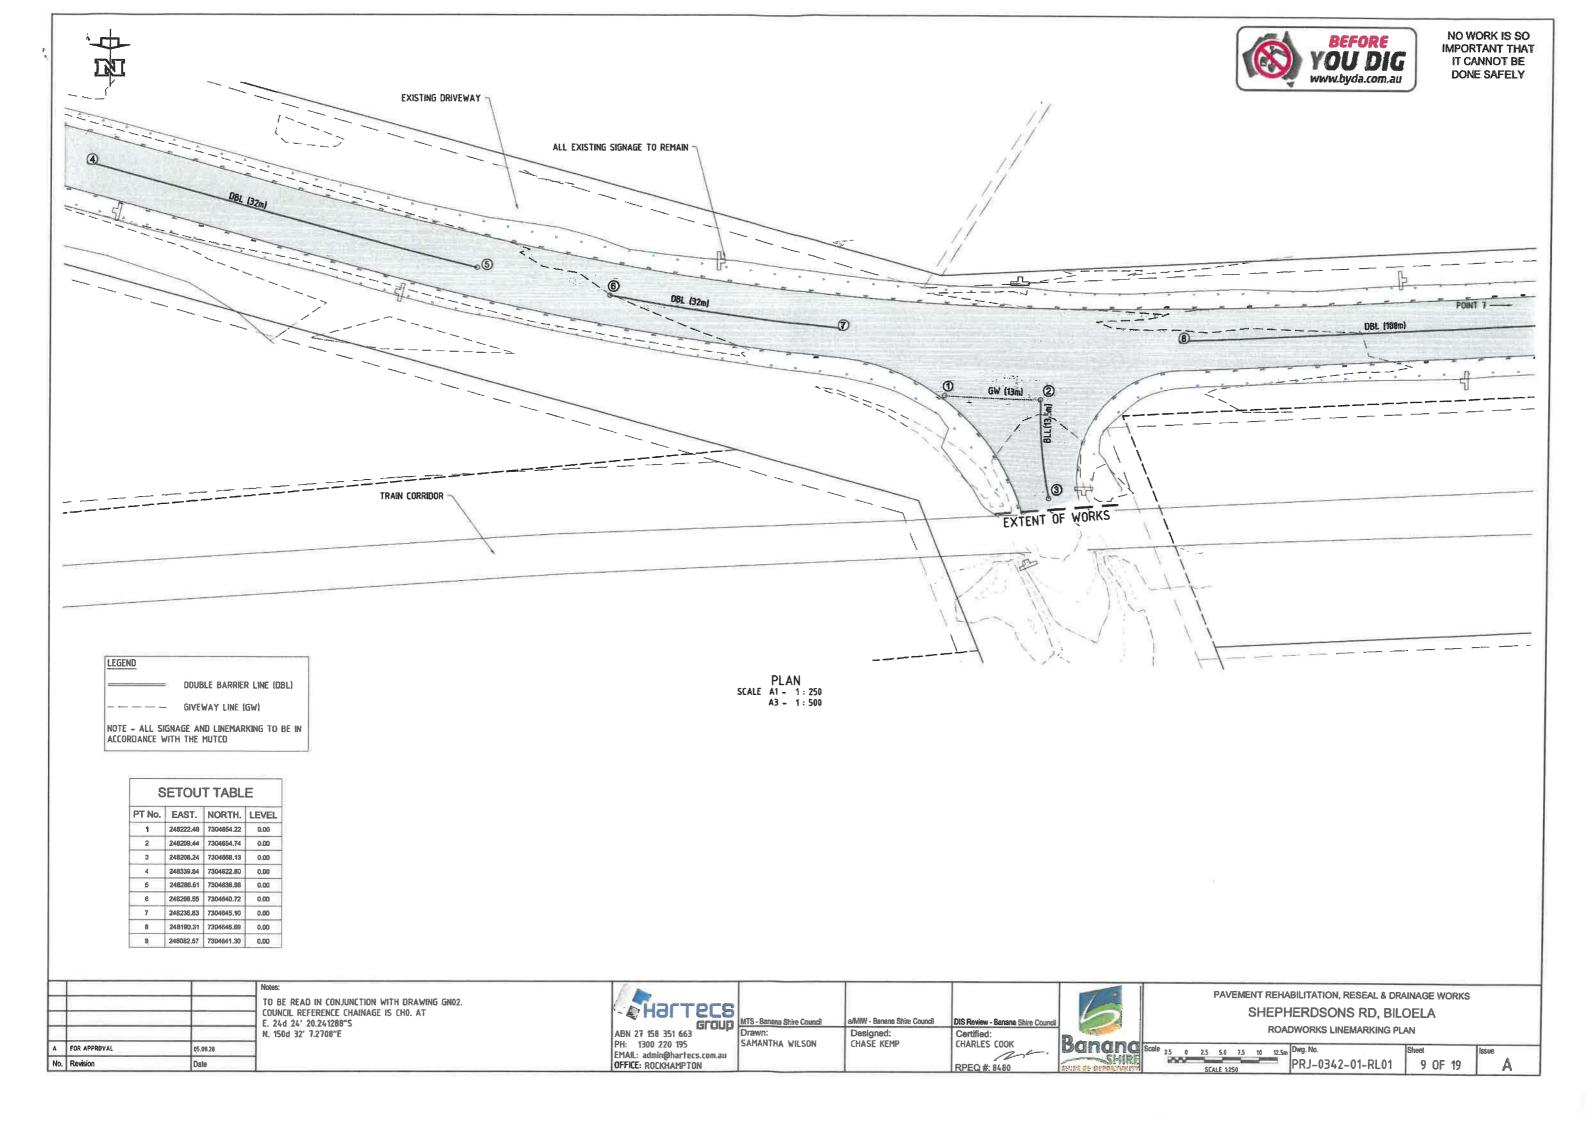

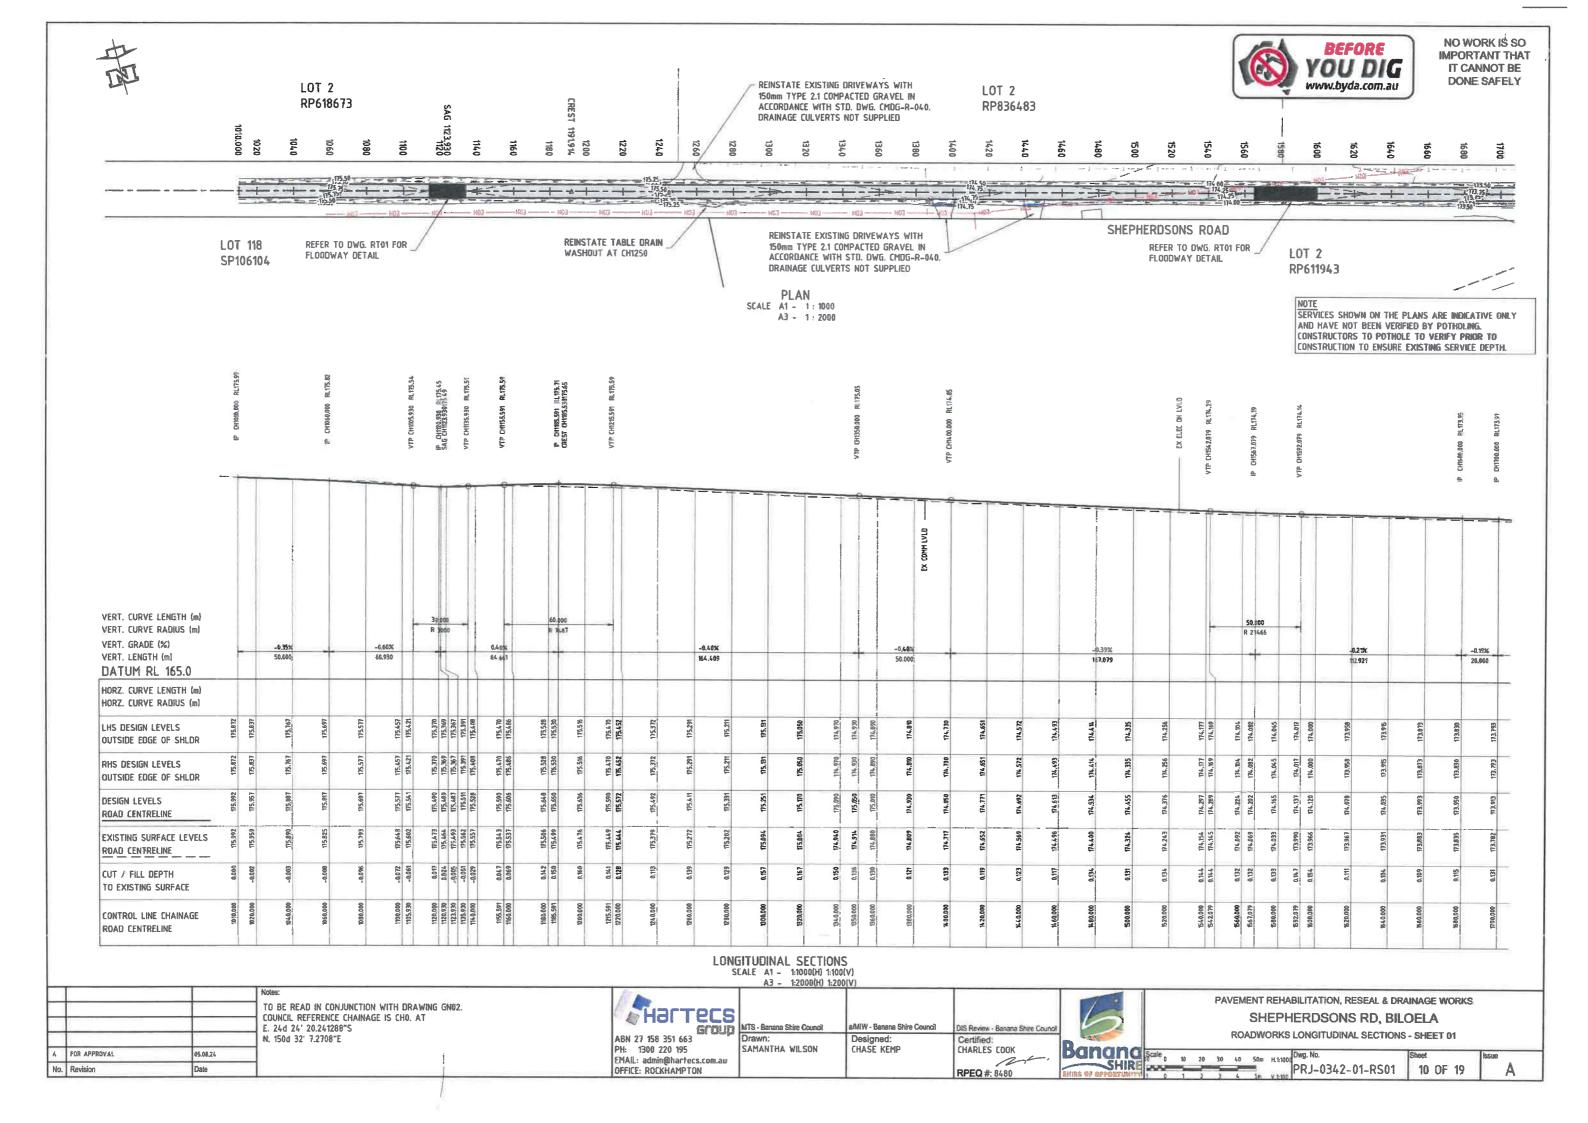

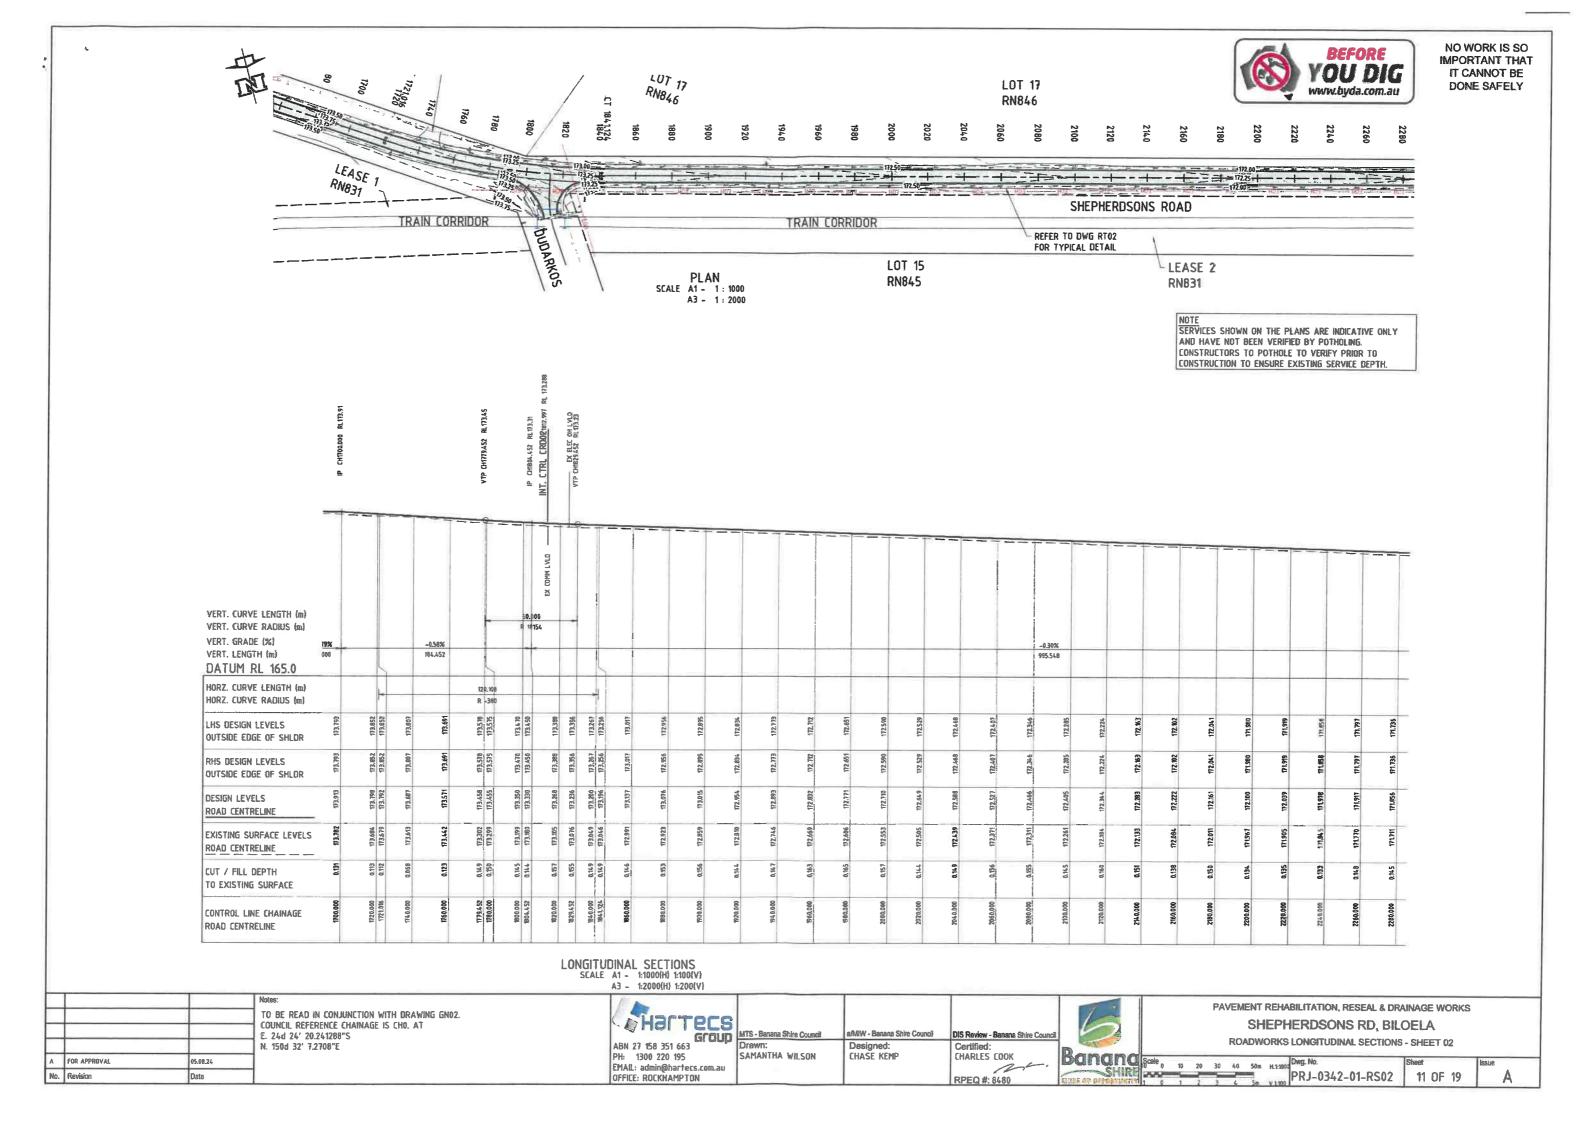



LOT 17 RN846



BEFORE YOU DIG www.byda.com.au

NO WORK IS SO IMPORTANT THAT IT CANNOT BE DONE SAFELY

SHEPHERDSONS ROAD TRAIN CORRIDOR REFER TO DWG RT02 FOR TYPICAL DETAIL LEASE 2 LOT 15 LOT 2 RN845 RP611619 RN831

PLAN SCALE A1 - 1:1000 A3 - 1:2000

SERVICES SHOWN ON THE PLANS ARE INDICATIVE ONLY AND HAVE NOT BEEN VERIFIED BY POTHOLING. CONSTRUCTORS TO POTHOLE TO VERIFY PRIOR TO CONSTRUCTION TO ENSURE EXISTING SERVICE DEPTH.

VERT. CURVE LENGTH (m) VERT. CURVE RADRIS (m) VERT, GRADE (%) -0.25% VERT. LENGTH (m) **DATUM RL 165.0** HORZ. CURVE LENGTH (m) HORZ. CURVE RADIUS (m) LHS DESIGN LEVELS OUTSIDE EDGE OF SHLDR RHS DESIGN LEVELS OUTSIDE EDGE OF SHLDR DESIGN LEVELS ROAD CENTRELINE EXISTING SURFACE LEVELS ROAD CENTRELINE CUT / FILL DEPTH TO EXISTING SURFACE CONTROL LINE CHAINAGE ROAD CENTRELINE

> LONGITUDINAL SECTIONS SCALE A1 - 1:1000(H) 1:100(V) A3 - 1:2000(H) 1:200(V)

TO BE READ IN CONJUNCTION WITH DRAWING GN02. COUNCIL REFERENCE CHAINAGE IS CHO. AT E. 24d 24' 20.241288"S N. 150d 32' 7.2708"E A FOR APPROVAL 05.08.28 No. Revision

Hartecs ABN 27 158 351 663 PH: 1300 220 195 EMAIL: admin@harfecs.com.au

OFFICE: ROCKHAMPTON

GFOUD MTS - Banana Stire Council SAMANTHA WILSON

a/M/W - Banana Shire Council IS Review - Banana Shire Council Certified: CHARLES COOK 120 RPEQ #: 8480

CHASE KEMP



PAVEMENT REHABILITATION, RESEAL & DRAINAGE WORKS SHEPHERDSONS RD, BILOELA **ROADWORKS LONGITUDINAL SECTIONS - SHEET 03**

| ale, | 46 | 20 | 30 | 10 | 50m | 111100 | Dwg. No. | Sheet | issue | |
|------|----|----|----|----|------|----------|-------------------|----------|-------|--|
| | N/ | 20 | 20 | 40 | SUIR | 11.1:100 | DD 1 02/2 04 DC02 | 42 OF 40 | A | |
| 0 | 1 | 2 | 3 | 4 | 5m | V 1:100 | PRJ-0342-01-RS03 | 12 UF 19 | A | |





RP611619

NO WORK IS SO IMPORTANT THAT IT CANNOT BE **DONE SAFELY**

LOT 17 RN846

SHEPHERDSONS ROAD TRAIN CORRIDOR REFER TO DWG RT02 FOR TYPICAL DETAIL LOT 2 LEASE 2

RN831

PLAN SCALE A1 - 1: 1000 A3 - 1: 2000

SERVICES SHOWN ON THE PLANS ARE INDICATIVE ONLY AND HAVE NOT BEEN VERIFIED BY POTHOLING. CONSTRUCTORS TO POTHOLE TO VERIFY PRIOR TO CONSTRUCTION TO ENSURE EXISTING SERVICE DEPTH.

VERT. CURVE LENGTH (m) VERT. CURVE RADIUS (m) VERT. GRADE (%) -0.25% -0.15% VERT. LENGTH (m) **DATUM RL 165.0** HORZ. CURVE LENGTH (m) HORZ. CURVE RADIUS (m) LHS DESIGN LEVELS OUTSIDE EDGE OF SHLDR RHS DESIGN LEVELS OUTSIDE EDGE OF SHLDR DESIGN LEVELS ROAD CENTRELINE EXISTING SURFACE LEVELS ROAD CENTRELINE CUT / FILL DEPTH TO EXISTING SURFACE CONTROL LINE CHAINAGE ROAD CENTRELINE

LONGITUDINAL SECTIONS SCALE A1 - 1:1000(H) 1:100(Y) A3 - 1:2000(H) 1:200(Y)

| 410 | Davidsian | D-t- | |
|-----|--------------|----------|--------------------------------------------------------------|
| A | FOR APPROVAL | 05.08.24 | |
| | | | N. 150d 32' 7.2708"E |
| | | | COUNCIL REFERENCE CHAINAGE IS CHO. AT E. 24d 24' 20.241288"S |
| | | | TO BE READ IN CONJUNCTION WITH DRAWING GNO2. |
| | | | Notes: |

| | Hartecs | - |
|------|-----------------------------|---|
| - 14 | ABN 27 158 351 663 | 1 |
| Ŧ | PH: 1300 220 195 | ŀ |
| | EMAIL: admin@hartecs.com.au | l |
| 1 | DFFICE: ROCKHAMPTON | |

| TS - Banana Shire Council | a/MiW - Banana Shire Council | DIS Review - Banana Shire Co |
|---------------------------|------------------------------|------------------------------|
| Drawn: IAMANTHA WILSON | Designed: CHASE KEMP | Certified: CHARLES COOK |
| | | RPEQ #: 8480 |

| D. | 6 | |
|----|--------|-------|
| | Banana | Şcale |


PAVEMENT REHABILITATION, RESEAL & DRAINAGE WORKS CHEDITED COMO DE BUIGELA


| | | | | | SH | EPHERDSONS RD, | RITOFFA |
|-----------------|----|----|------|-----|--------------|-------------------------|----------------|
| | | | | RO | ADW(| ORKS LONGITUDINAL SECTI | ONS - SHEET 04 |
| de _o | 10 | 20 | 30 | 40 | 50m | H.1:100 Dwg. No. | Sheet |
| E.F | | | 2000 | 200 | and the last | DD 1 02/2 04 DC | N |


PRJ-0342-01-RS04

13 OF 19


NO WORK IS SO IMPORTANT THAT IT CANNOT BE DONE SAFELY

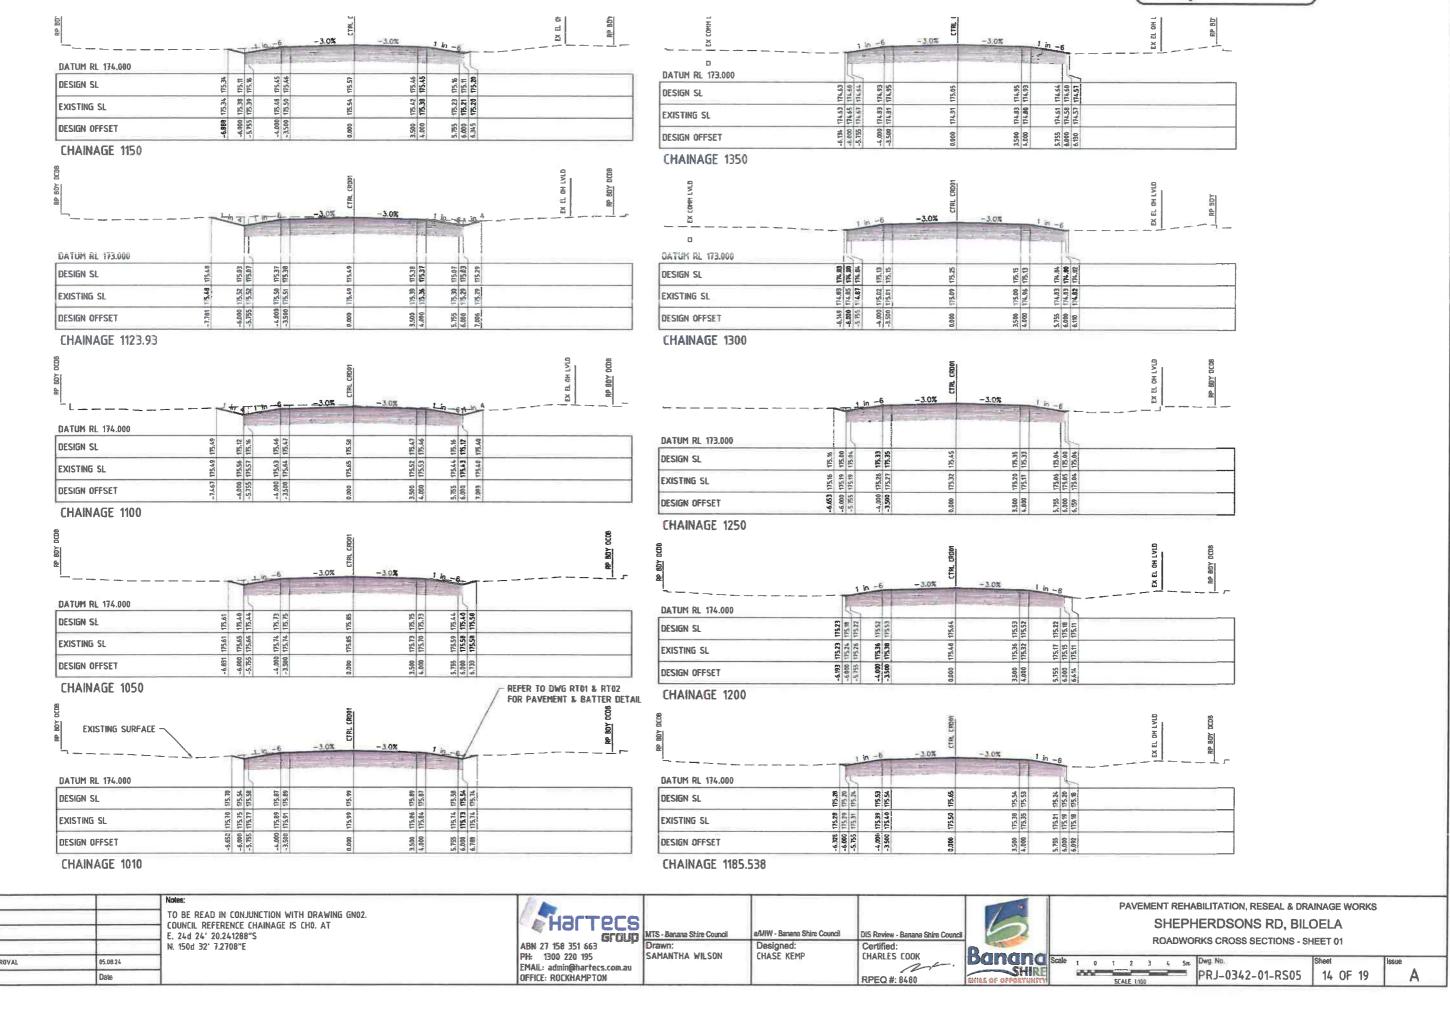


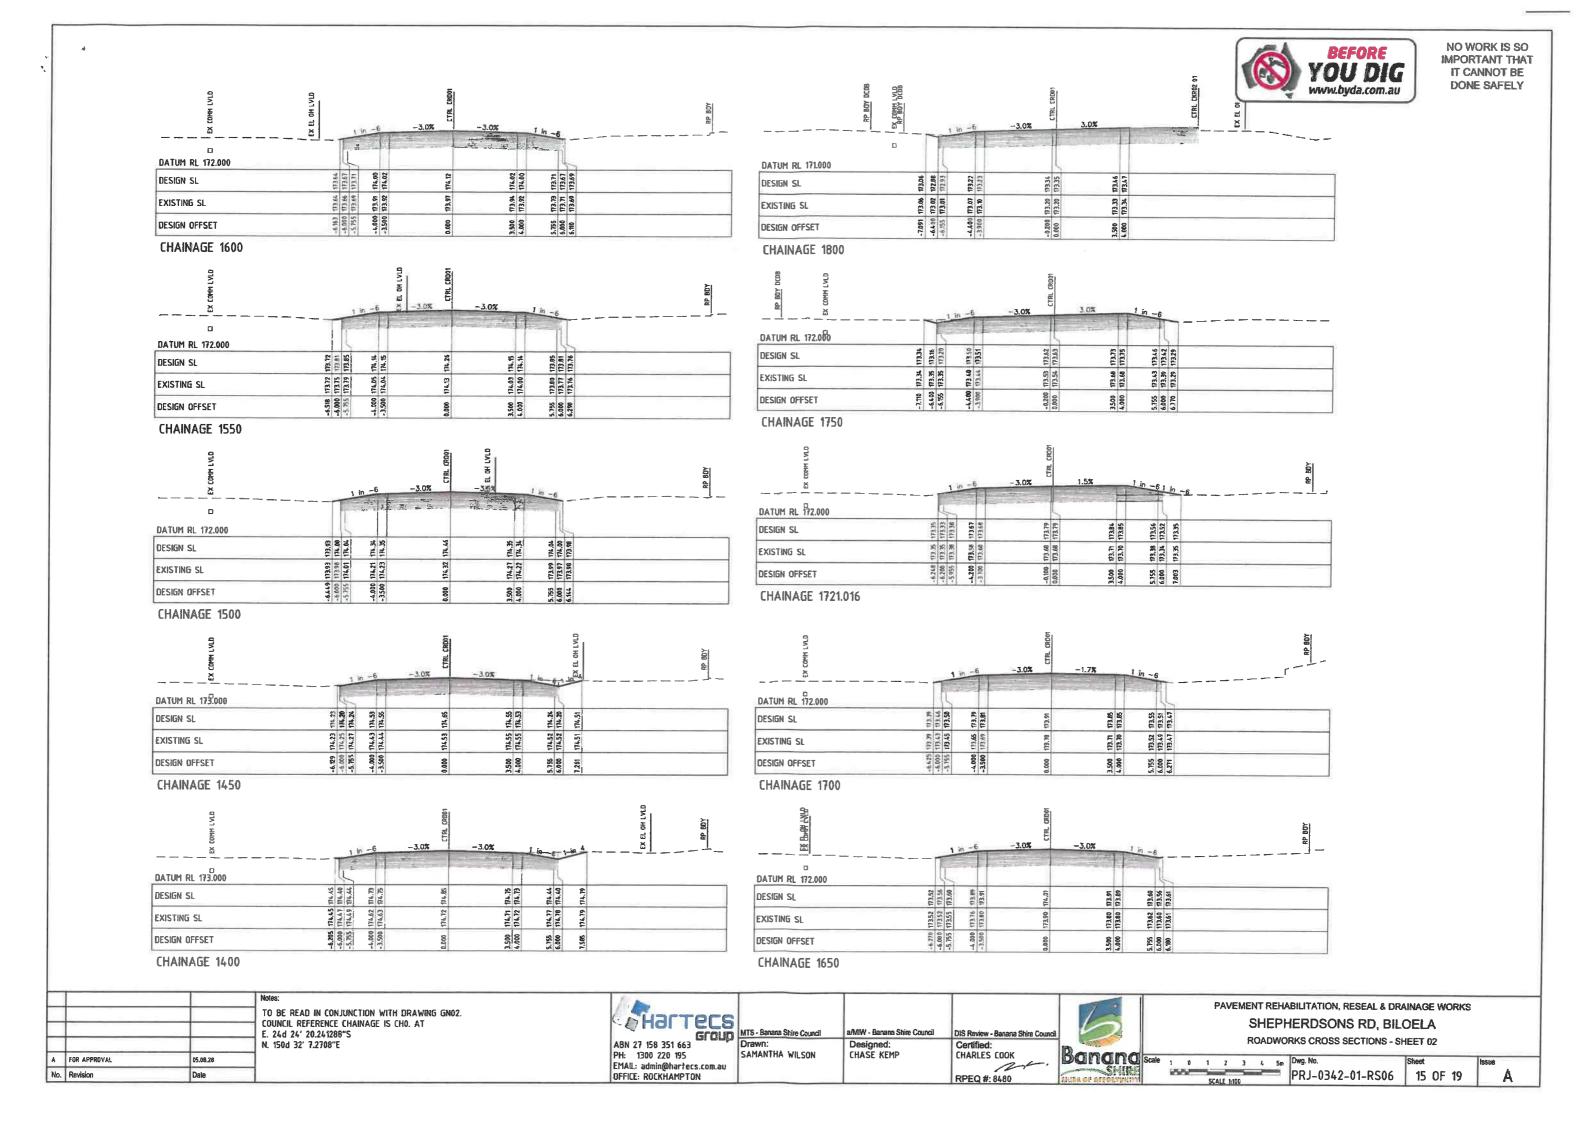

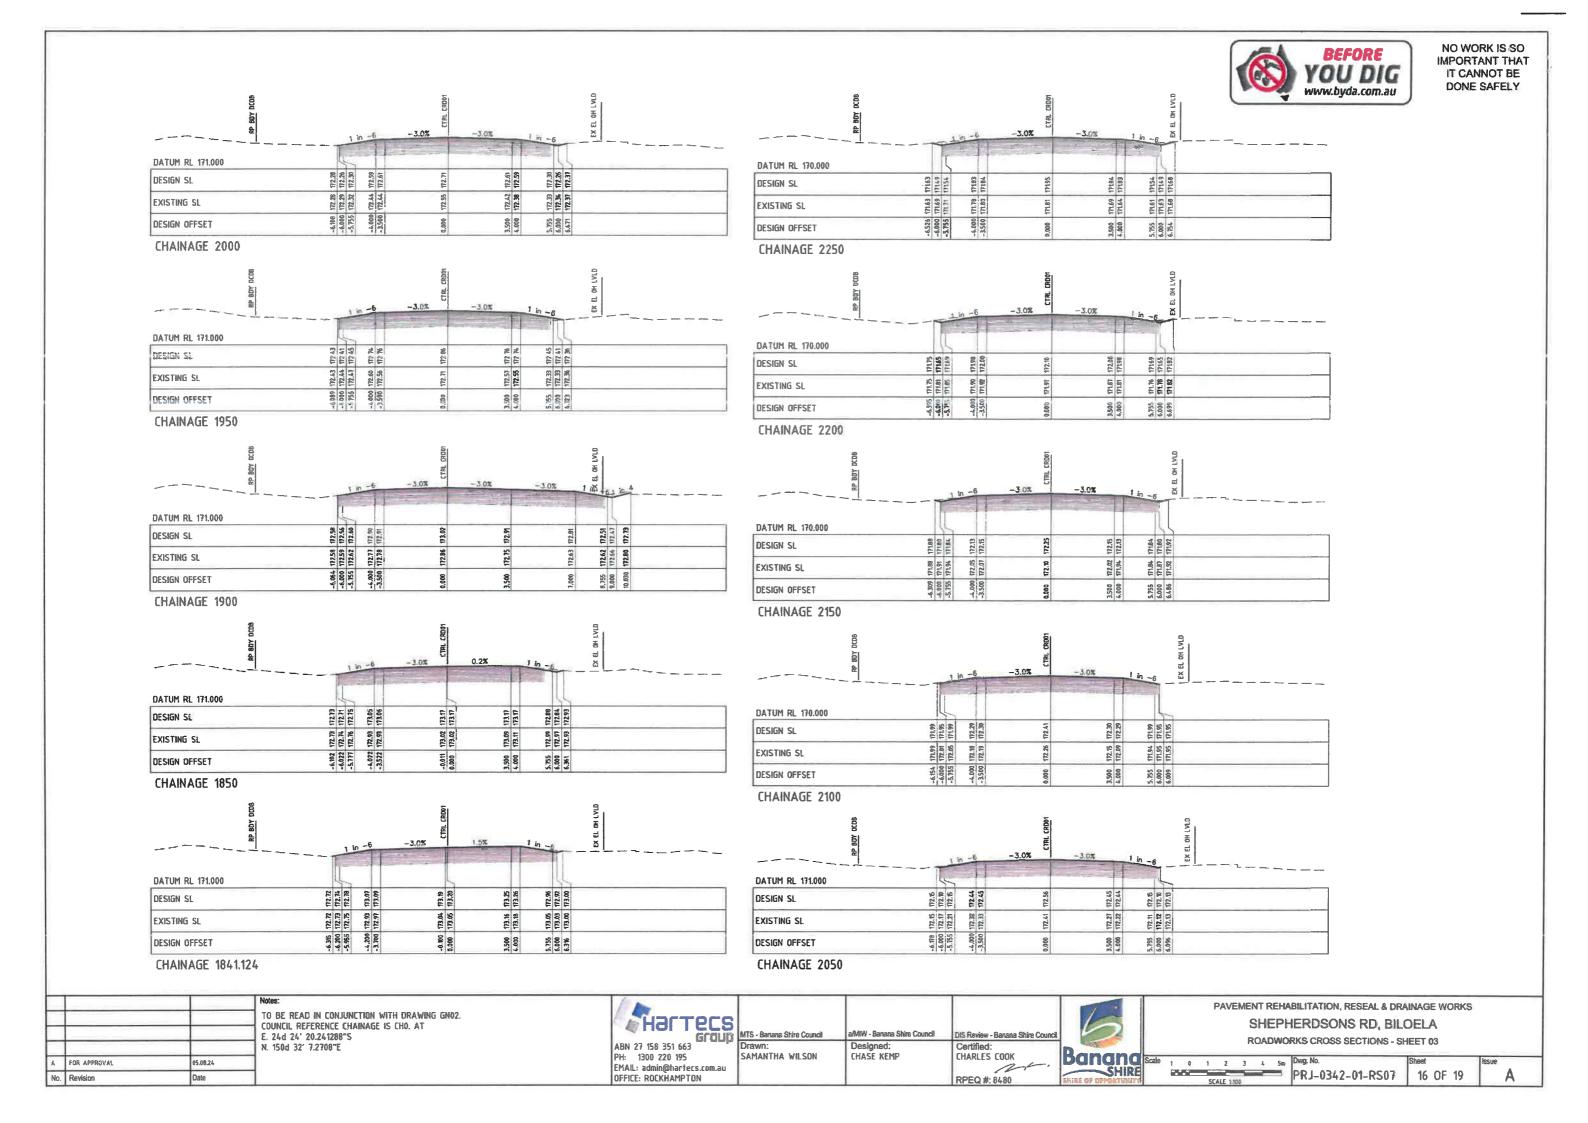


NO WORK IS SO IMPORTANT THAT IT CANNOT BE DONE SAFELY







CHAINAGE 2450



CHAINAGE 2400



CHAINAGE 2350




CHAINAGE 2300

| RP BDY DCDB | | 1 | in -t | -3.0% | -3.0% | l in | -6 | EX EL OH LYLD | |
|------------------|--------|--------|------------------|--------|--------|-------|------------|---------------|--|
| DATUM RL 168.800 | | 1 | | | | | | L | |
| DESIGN SL | 170.08 | 170.01 | 170.30 170.32 | 170,42 | 70.32 | 95.07 | 10.01 | 19.0 | |
| EXISTING SL | 170.08 | | 170.24 | 170.31 | 170.18 | | 169.97 | | |
| DESIGN OFFSET | 5445- | | -4.000 | 0000 | 3.500 | 4 | 5.755 | _ | |
| CHAINAGE 2750 | 1 1 | | .1171 | 0 | m · | *! | 5 4 | 5 40 | |

| RP BOY OCCS | ı in | -6 | -3.0% | -3.0% ₁ | EX EL OH LVLD | |
|------------------|----------------------------|--------|--------|--------------------|----------------|--|
| DATUM RL 169.000 | The same | | | 4 | | |
| DESIGN SL | 170.21 | 170.46 | 170.58 | 170.47 | 170.12 | |
| EXISTING SL | 170.26 170.26 170.30 | 770.39 | 170,46 | 170.26 | 70.07 70.07 | |
| design offset | -6.334 -6.000 -5.755 | -3.500 | 0,000 | 3.500 | 6.214 | |

CHAINAGE 2700



CHAINAGE 2650


| 8000 | | CRD01 | | 1 LVB | |
|------------------|------------------|----------------------|------------------|---------------------------|--|
| RP 800Y | | -6 -3.0% | -3.0% | E E O | |
| DATUM RL 169.000 | 15 | | | | |
| DESIGN SL | T70.55 | 770.76 170.88 | 770.78 770.76 | 70.47 770.43 170.41 | |
| EXISTING SL | 170.55 170.64 | 7.07 7.07 7.07 | 170.64 | 170.37 | |
| DESIGN OFFSET | -6,480 -6,000 | -3500 | 3,500 | 6.000 | |

CHAINAGE 2600


| RP BOY DCOB | | in -6 | -3.0% | -3.0% | | 2 E C OH LV.D |
|------------------|----------------------------|--------|--------|-----------------|--------|---------------|
| DATUM RL 169.000 | \$1 25 ES | TP0.91 | | | | x |
| DETIGIT DE | 170 170 | 17 | 114.03 | 170.93 P.071 | 170.62 | 011 |
| existing SL | 170 68 170 71 | 170.87 | 170.90 | 170.76 | 170.53 | 98.071 |
| DESIGN OFFSET | -6.000 -5.000 -5.055 | -3500 | 0.000 | 3,500 | 5.755 | 860.9 |

CHAINAGE 2550

| | | TO BE READ IN CONJUNCTION WITH DRAWING GN02. COUNCE, REFERENCE CHAINAGE IS CHO. AT E. 24d 24' 20.241288"S N. 150d 32' 7.2708"E | ABN 27 158 351 663 | MTS - Banana Stire Council Drawn: | Designed: | DIS Review - Banana Shire Council Certified: | 6 | PAVEMENT REHABILITATION, RESEAL & DRAINAGE WORKS SHEPHERDSONS RD, BILOELA ROADWORKS CROSS SECTIONS - SHEET 04 |
|--------------|----------|--------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------|--------------------------------------|------------|-------------------------------------------------|-----------------|---------------------------------------------------------------------------------------------------------------|
| FOR APPROVAL | 05.08.24 | | PH: 1300 220 195 EMAIL: admin@hartecs.com.au | SAMANTHA WILSON | CHASE KEMP | CHARLES COOK | banana | Scale 1 0 1 2 3 4 Spp Dwg. No. Sheet Issue |
| o. Revision | Date | | OFFICE: ROCKHAMPTON | | | RPEQ #: 8480 | MILLS OF STREET | PRJ-0342-01-RS08 17 OF 19 A |

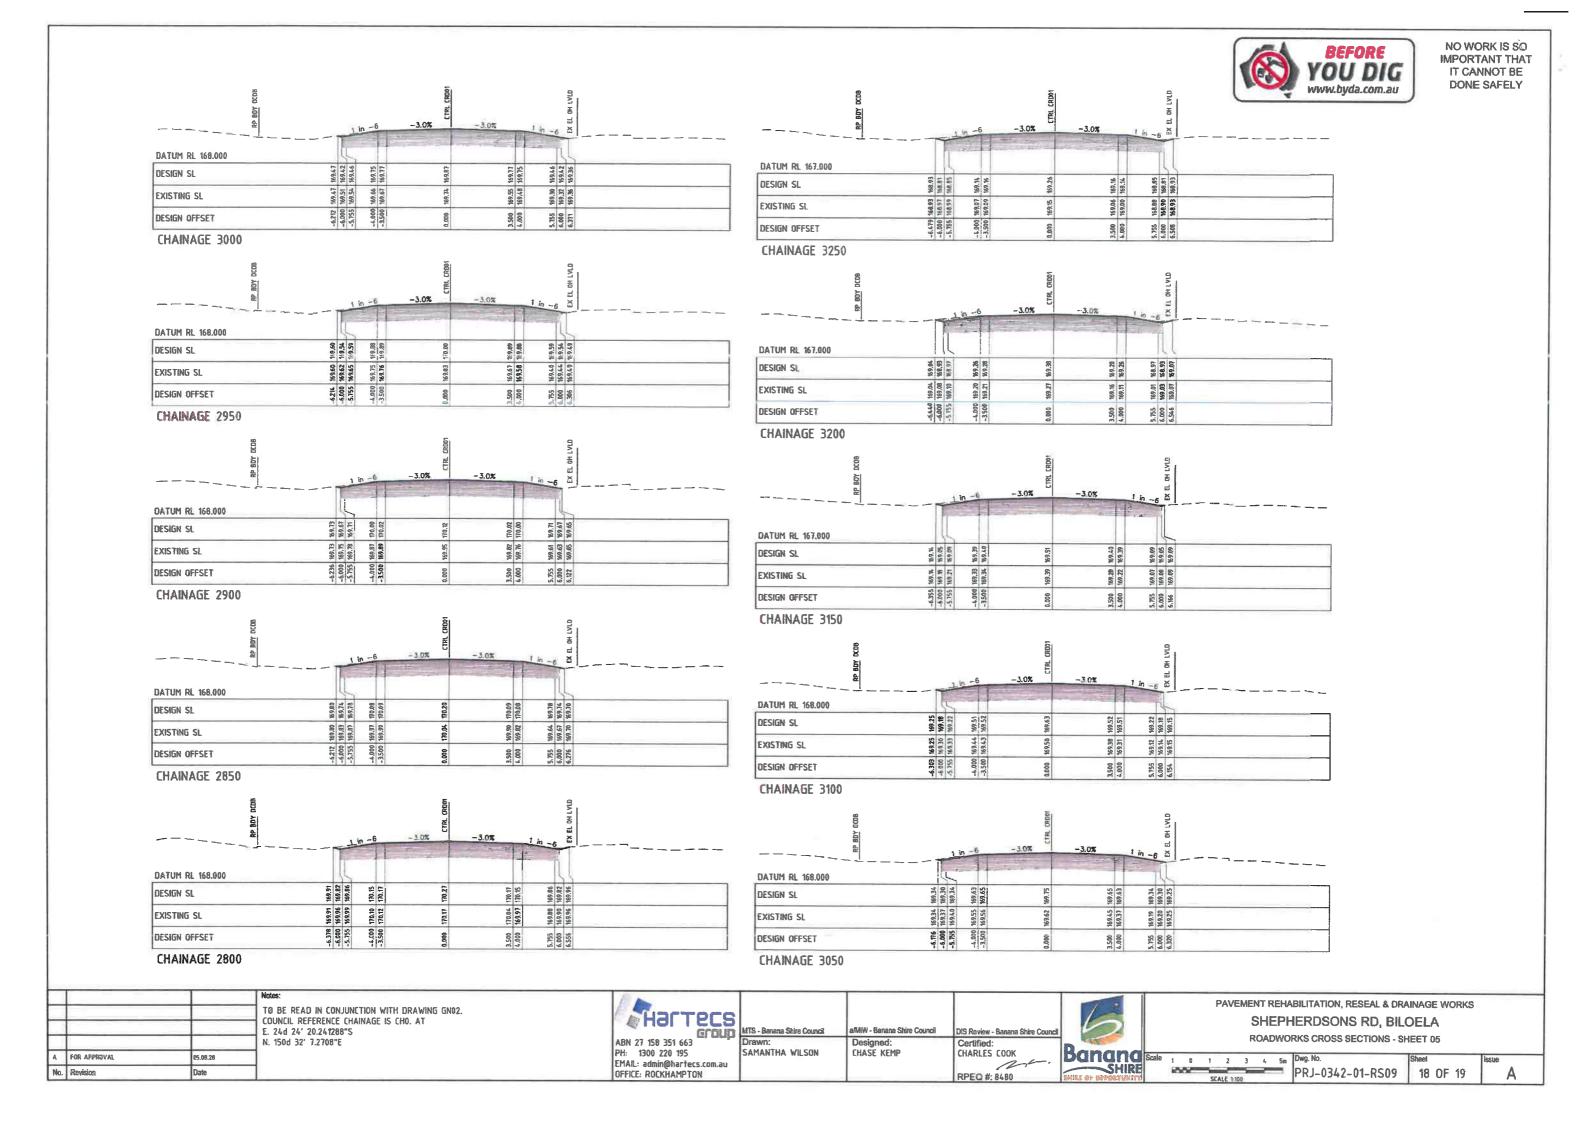






| 80 Å 0C08 | | | | CTRL CRD01 | 3.08 | | | EI, OH LVLD | |
|------------------|--------|--------|--------|------------|--------|--------|---------|-------------|---|
| DATUM RL 168.000 | | 11 | 1 -6 | -3.04 | -3.0% | 1 | I In -6 | EX | J |
| DESIGN SL | 09 591 | 169.59 | 169.88 | 170.00 | 169,89 | 169,88 | 169.59 | 169.49 | |
| EXISTING SL | 169.60 | 169.65 | 169.75 | 169,63 | 169.67 | 169,58 | 169.40 | 169.49 | |
| DESIGN OFFSET | 4129- | -5.755 | -4.000 | 0.000 | 3,500 | 4.000 | 5.755 | 906.9 | |

| RP 60Y DOB | 1 in -6 | -3.0% | -3.0 x | EX EL OH LVLD | |
|------------------|-----------------------------|--------|---------------|-----------------------------|--|
| DATUM RL 168.000 | | | | | |
| DESIGN SL | 169,631 169,63 17,000 | 770.02 | 170.02 | 16.9.71 7.9.63 7.9.63 | |
| EXISTING SL | 169.73 169.73 169.87 | 169.85 | 169.82 | 169.61 | |
| DESIGN OFFSET | | -3.500 | 3,500 | 5.755 6.000 6.022 | |



| 800 <u>vo</u> 8 | | | | | | K. CRDOI | | | | | OH LVLD | |
|------------------|--------|--------|--------|--------|--------|----------|--------|--------|--------|--------|---------|--|
| 20 B | | | | 10- | | -3.0% | -3.0% | | 1 in - | 3 | ᇳ | |
| DATUM RL 168.000 | | | L | 1 | | | | | | - | | |
| DESIGN SL | 16.991 | 169.82 | 169.86 | 170.15 | 170.17 | 170.27 | 170,17 | 170.15 | 169.86 | 169.02 | 169.96 | |
| EXISTING SL | 16991 | 169.96 | 169.99 | 170.10 | 170.12 | 170,17 | 170.04 | 169.97 | 88,988 | 169.90 | 169.96 | |
| DESIGN OFFSET | 6.378 | 000 | 5.755 | 90 | -3.500 | 0.000 | | 4.000 | | | 6.556 | |

| | | | Notes: TO BE READ IN CONJUNCTION WITH DRAWING GNO2. COUNCIL REFERENCE CHAINAGE IS CHO. AT E. 24d 24' 20.241288"S N. 150d 32' 7.2708"E |
|---|--------------|----------|----------------------------------------------------------------------------------------------------------------------------------------|
| A | FOR APPROVAL | 05.08.24 | |
| | | | |

CHAINAGE 2950

| HALTECS FOULD ABN 27 158 351 663 | M |
|----------------------------------------------------|---|
| ABN 27 158 351 663 PH: 1300 220 195 | S |
| EMAIL: admin@hartecs.com.au OFFICE: ROCKHAMPTON | |

| S - Banana Shire Council | a/M!W - Banana Shire Council | DIS Review - Banana Shire Cour |
|--------------------------|------------------------------|--------------------------------|
| awn: | Designed: | Certified: |
| Mantha Wilson | CHASE KEMP | CHARLES COOK |

DATUM RL 167.000

DESIGN SL

EXISTING SL

DESIGN OFFSET

CHAINAGE 3250

DATUM RL 167.000

DESIGN SL

EXISTING SL

DESIGN OFFSET

CHAINAGE 3200

DATUM RL 167.000

DESIGN SL

EXISTING SL

DESIGN OFFSET

CHAINAGE 3150

DATUM RL 168.000

DESIGN SL

EXISTING SL

DESIGN OFFSET

CHAINAGE 3100

DATUM RL 168.000

DESIGN SL

EXISTING SL

DESIGN OFFSET

CHAINAGE 3050

168.93 168.81

16893 16897 16899

6.036 5.735

169,04 146,93 168,97

169.08 169.08

6.000

269.14 269.05

169.14 169.18

6.000

169.75 169.72 169.51

169.25 169.30 169.44 169.44

169.34 169.30 169.34 169.63

169.34 169.40 169.55 169.56

-6.176 -6.000 -5.755 -4.000

3.500

6.000

169.20

4.000

169.39

169.33

3500

169.14

169.07

3.500

168.85 168.81 168.93

168.88 168.90 168.93

5.755 6.000 6.508

168.93 169.07

169.01 169.03

3.755

169.09 169.05

169.08 169.08 169.09

6.000

5.755 6.000 6.154

169.34 169.30 169.25

169.19 169.20 169.25

6.000

169.16

169.06

3.500

169.2B

169.16

200

169.40

169.28

3.500

169.52

3.500



3.500

| | | | | | F | | | RKS CROSS SECT | |
|-------|---|---|---|---|---|---|----|----------------|-------|
| Scale | 1 | 0 | 1 | 2 | 3 | 4 | 5m | Dwg. No. | Sheet |

| • | | | | | | R | OAE | owo | RKS CROSS SECTIONS - S | SHEET 06 | |
|------|-------|-----|---|---|---|---|-----|-----|------------------------|----------|-------|
| na | Scale | 1 | 0 | 1 | 2 | 3 | 4 | 5m | Dwg. No. | Sheet | Issue |
| HIRE | | 100 | - | _ | | - | _ | | PRJ-0342-01-RS10 | 19 OF 19 | Ι Δ |

| | * <u>\$</u> | |
|--|----------------|--|
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |

DES-EM-30-064 Page 1 of 2 Document Version: 4 July 2016



SCHEDULE 15 - ABORIGINAL CULTURAL HERITAGE IDENTIFICATION REPORT

This document is to be prepared when a site inspection or site visit occurs.

ABORIGINAL CULTURAL HERITAGE IDENTIFICATION REPORT Insert Name PEOPLE

This form is to be completed by the Aboriginal Party or Aboriginal Party's Representative after a Site Inspection and then handed to the Council Representative on the same day that the inspection is completed.

| | Council Job Ref: | W8646 |
|----|---------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| | Work Project: | Sherherdsons Road - Rehabilitation |
| | Location of Site Inspection/ Monitoring: | CH950 to CH3,770 |
| | Date(s): | 14 November 2024 |
| | Aboriginal Party Representative: | Deborah Tull + Cyesha Tull - [Gungulus (GNP) |
| | Council Representative In Attendance: | Elena Hayward |
| 1. | details in the related Proposed W | (insert name) on behalf of the |
| | | |
| | If the 'Yes' box is ticked – si | gn here Signature: <u>Dlegrah Jull</u> People) Date: 14/11/2024 |
| | (on behalf of the <u>Gang</u> | 11 V People) Date: 14/11/2024 |
| | If the 'No' box is ticked - co | |
| 2. | | spection I have identified in the proposed works area, Aboriginal cultura ify type of cultural heritage find e.g. artefact, painting, etching, burial site, sacred sitence): |
| | | |
| | | |
| | | |
| 3. | The Aboriginal Cultural Herita | ge is located on or near: (specify general location or if possible GPS coordinates). |
| | | |
| | | |
| | | |
| | | |

DES-EM-30-064 Page 2 of 2 Document Version: 4 July 2016

| 4. | . The People make the following recommendation(s): (tick relevant recommendation (s)): (tick relevant recommendation): (Through the Consultative Committee, the Parties may continue to refine this Notice template). | ntion/s). | | | | | | | | | |
|------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------|--|--|--|--|--|--|--|--|--|
| | ☐ Monitors are employed during work in the location of identified Aboriginal Cultural Heritage. | | | | | | | | | | |
| | ☐ The work project is to avoid specified areas. | | | | | | | | | | |
| | ☐ A fence is to be erected to prevent access on or around an area of cultural significance. | | | | | | | | | | |
| | ☐ An expert is to be engaged to evaluate and document the general location of a cultural heritage find. | | | | | | | | | | |
| | ☐ The People relocate a cultural heritage find made. | | | | | | | | | | |
| | Other action is recommended (specify): | | | | | | | | | | |
| | | | | | | | | | | | |
| | | | | | | | | | | | |
| | | | | | | | | | | | |
| | Cyesha Tull General 14.11. Deborgh Tull Debouch Jule 14/11 | 24. | | | | | | | | | |
| | Cyesha Tull Quelo Inl Gangula 14.11. Dehorah Tull Name of Representative Signed on behalf of the Gang Ulu People Date | 124 | | | | | | | | | |
| | | | | | | | | | | | |
| - <u>/</u> | Elena Hayword Name of Representative Signed on behalf of Banana Shire Council Date | 24 | | | | | | | | | |
| Sk | ketch indicating general location of cultural heritage at or around the work site | | | | | | | | | | |
| | • | | | | | | | | | | |
| | No cultural heritage located. | | | | | | | | | | |
| | | | | | | | | | | | |
| | | | | | | | | | | | |
| | | | | | | | | | | | |
| | | | | | | | | | | | |
| | | | | | | | | | | | |
| | | | | | | | | | | | |
| | | | | | | | | | | | |
| | | | | | | | | | | | |

Shepherdsons Road Cultural

- HIDIO to CH 3700 Fence to Fence + 50m both ends.
 - -24.35189,150.498967 & -24.351750,150.498940 Abovered Shepherdsons - Giveway sign to Enside Larrier. CH3,770
 - -24.35/801, 150.49925 + -24.351879, 150, 501462 CH 3,510
- -24.351476, 150.505093 + -24.351542, 150.505092 CH 3,140
- -24.351512, 150.505373 & -24.351518, 150.505398 WCH 2,920
- $-24.351\frac{337}{362}$, 150.509215 4 24.351489, 150.509208 CH 2, 730
- 24.351453, 150-50924 +-24,351430, 150.512381 CH2,400
- -24.35|125, 150.5|639| + -24.351267, 150.5|6406 CH 1990
- -24.351114, 150.517160 + -24.351223, 150.518001 CH 1830
- -24.351439, 160.619940 + -24.351599, 150.519874 CH 1,630
- -24.353163,150.526325 +-24.353162,150.526257 CH 950
- . All area inside of above listed points have been checked and cleared.
